





STATE ROAD 56
WESLEY CHAPEL, FLORIDA

CAPITAL TRUST AGENCY
SENIOR HOUSING REVENUE BONDS
SERIES 2016A \$21,710,000
DATED: OCTOBER 6, 2016
CUSIP: 140532BP6

CAPITAL TRUST AGENCY
SENIOR HOUSING REVENUE BONDS
SERIES 2016B \$1,040,000
DATED: OCTOBER 6, 2016
CUSIP 140532BQ4

MONTHLY REPORT
AND
CERTIFICATION

Period Ended August 31, 2017

ISSUED: OCTOBER 11, 2017



CONTENTS

- I. Introduction
- II. Officer's Certificate
- III. Development Activities

Construction Update Development Budget Comparison Construction Monitoring Report

- IV. Operations & Marketing
- V. Financial Reports

Income Statement Balance Sheet Statement of Cash Flow

VI. Balances of Trustee-held Funds



I. INTRODUCTION

Pursuant to Section 530 of the Loan Agreement ("Loan Agreement") dated as of October 1, 2016, between the Capital Trust Agency as Issuer and PSL Wiregrass, LP as Borrower, Prevarian Companies is pleased to present this report summarizing the progress of Wesley Chapel's newest assisted living and memory care development, Beach House at Wiregrass Ranch (the "Community" or the "Project").

Information pertaining to construction reflects progress through August 31, 2017. The financial reports reflect accounting activity from January 1, 2017 through August 31, 2017 and account balances as of August 31, 2017. Operational and Marketing information presented includes activity through September 30, 2017.







II. OFFICER'S CERTIFICATE



OFFICER'S CERTIFICATE

Capital Trust Agency Senior Housing Revenue Bonds (Beach House at Wiregrass Ranch), Series 2016A Dated October 6, 2016 – CUSIP 140532BP6 Series 2016B Dated October 6, 2016 – CUSIP 140532BQ4

MONTHLY STATEMENT OF BORROWER

PERIOD ENDED August 31, 2017

October 11, 2017

As an Authorized Representative of the Borrower, I hereby submit this monthly statement of Borrower. Pursuant to Section 530 of the Loan Agreement ("Loan Agreement") dated as of October 1, 2016, between the Capital Trust Agency as Issuer and PSL Wiregrass, LP as Borrower, the following information is furnished:

- A. A summary statement as to the status of construction including the report of any Construction Monitor;
- B. Unaudited financial reports on the development costs of the Project incurred during the month and on an aggregate basis; and
- C. Statements of the balances for each fund and account required to be established under the Loan Agreement or under the Indenture as of the end of the month (obtained from the Trustee), all in reasonable detail

I hereby certify that: (a) this information is hereby delivered in compliance with the requirements of Section 530 of the Loan Agreement and (b) as of the date hereof no event or condition has happened or existed or is happening or exists that constitutes, or that with notice or lapse of time or both, would constitute, an "Event of Default" under the Loan Agreement or the Trust Indenture (the "Indenture") dated as of October 1, 2016, between the Capital Trust Agency and U.S. Bank National Association as Trustee, (as such terms are defined in the Indenture).

PSL WIREGRASS, LP

a Texas Limited Partnership

By: GP PSL Wiregrass, LLC its general partner

H. Dodd Crutcher, President




III. DEVELOPMENT ACTIVITIES

Construction Update



Interior finish work ramped up significantly in August. Tile installation advanced to the third and final phase of the facility, walls were primed in approximately 60% of the building, and casing/trim work was completed in approximately 40% of the building. Cabinets were delivered for and installed for about half of the facility, and residential doors were painted and hung as they were delivered to the site.







▲ Unit Door Installation



Beach House at Wiregrass Ranch Assisted Living + Memory Care MONTHLY STATEMENT OF BORROWER AUGUST 2017

All above-ceiling systems work was completed. The remainder of gypsum board soffits were being finished, and acoustical ceiling grid installation commenced. Elevator installation work approached completion, and cabs will soon be ready for inspection.






- ▲ Acoustical Ceiling Grid Installation
- ◀ Elevator Installation

Outside, painting and metal roofing were nearing completion, and all rooftop mechanical work was finished and inspected. Decorative bracket installation continued - once completed, work can begin in the central courtyard. The transfer to permanent power was completed on August 30th, and HVAC systems will be started for climate control in September.





By August 31, 2017, the project was approximately 75% complete with a total billed-to-date of \$10,110,943:

Original Contract Sum	\$14,641,950	
Change Orders ¹	\$279,082	
Adjusted Contract Sum	\$14,921,032	_'
Completed and Stored to Date	\$11,234,380	75%
Less Retainage	(\$1,123,437)	_
Total Earned Less Retainage	\$10,110,943	

1. As of August 31, 2017, two (2) change orders were executed for a total of \$297K:

Change Order #1	\$270,224
Change Order #2	\$8,858
	\$279.082

At loan closing, \$128,386 of Owner Construction Contingency expense was disbursed to pay the Cash Bond for the construction of the S.R. 56 Deceleration Lane. The amount was not included in the project capitalization total, because it was 100% refundable from the Florida Department of Transportation. Upon completion of the road in August, the \$128,386 refund was received and deposited to the Working Capital Fund.

10/9/2017	S.R. 56 Deceleration Lane Cash Bond	128,385.88
8/31/2017	Reimbursement Deposited to Working Capital Fund	(128,385.88)
Remaining to	be Reimbursed	0.00

\$270,224 of Owner Construction Contingency was reallocated to ALF Construction (Hard Costs) for Construction Costs of Offsite Roadway Improvements. This amount is to be refunded from the land seller upon completion of the work and replenished to the Owner Construction Contingency budget. The first reimbursement installment of \$158,081 was received in April, and an additional \$50,589 was received in June. These checks were deposited in the Borrower's account in June. The collective \$208,670 in reimbursements was transferred to the Lender in July and reflected as an increase to the Owner Construction Contingency Budget balance in the same period.

12/31/2016	Change Order #1 Offsite Roadway Improvements	270,224.00
4/10/2017	Seller Reimbursement	(158,081.00)
6/6/2017	Seller Reimbursement	(50,588.98)
Remaining Ow	red to Owner Construction Contingency Budget	61,554.02




Approximately \$198K of the total \$448K Owner Construction Contingency Budget is currently deployed; however, \$62K of this will be reimbursed to the Construction Contingency Budget as discussed above. To date, the effective contingency utilization is approximately \$137K; this is only 31% of the Owner Construction Contingency Budget vs. 75% construction progress.

Owner Construction Contingency Budget	447,550	
Florida Department of Transportation Cash Bond	128,386	
Change Order #1 - Offsite Improvements ¹	270,224	(Reimbursable)
Change Order #2	8,858	
Offsite Improvements Reimbursements ¹	(208,670)	
Total Contingency Budget Currently Deployed	198,798	
Pending Reimbursements	(61,554)	
True Contingency Utilized to Date	137,244	31%

 $1. \qquad \text{Reimbur sements totaling $208,670 have been received and were transferred to the Lender in July.}$

As of August 31, 2017, the project was on schedule per the Construction Contract Exhibit (see Page 13 of Appono Consulting Construction Monitoring Report). Although occurring after its initial inspection and subsequent to the August Pay Application, Appono addresses the potential impact of Hurricane Irma on the project schedule on Page 15 of its report. Appono speculates that the effects of the severe weather may delay the completion date for up to seven (7) days, but maintains that it is possible for the GC to finish on-time with strategic planning and scheduling. Recent and upcoming project milestones include:

- The common area bathroom tile is approved and on site.
- Kitchen equipment is being stored at the subcontractor's warehouse.
- The acoustical ceiling grid in C2 started 8-30-17.
- The A2 door casing and trim is complete.
- The A2 and C2 window sills will be completed by 9-1-17.
- The access control equipment is arriving on 9-7-17 and subcontractor will be on site on 9-11-17.
- The bathroom accessories in C2 will be installed by 9-8-17.
- The B2 cabinets will be completed by 9-8-17.
- The closet shelving will be onsite by 9-11
- Shutters will arrive the week of 9-11-17.
- A2 flooring is scheduled to start on 9-18-17.
- The C2 vinyl flooring will begin the week of 9-25-17.

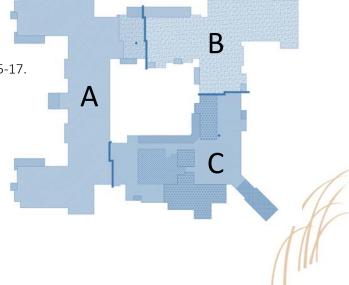

WIREGRASS - ASSISTED LIVING AND MEMORY CARE

DEVELOPMENT BUDGET COMPARISON	CURRENT BUDGET	PROJECT FUND REQUISITION #12 9/7/2017	TOTAL PAID TO DATE	REMAINING BUDGET
Total Land Acquisition Costs	\$1,490,000.00	\$0.00	\$1,490,000.00	\$0.00
Total Hard Costs	\$14,921,031.97	\$906,070.00	\$10,110,942.97	\$4,810,089.00
Total Development Soft Costs	\$3,841,945.53	\$96,735.35	\$1,184,647.83	\$1,523,916.61
TOTAL CONSTRUCTION ACCOUNT	\$20,252,977.50	\$1,002,805.35	\$13,918,971.89	\$6,334,005.61
CAPITALIZED INTEREST	\$2,811,672.50	\$0.00	\$860,293.05	\$1,951,379.45
CAPITALIZED ISSUER'S FEE THROUGH STABILIZATION	\$81,900.00	\$0.00	\$17,062.47	\$64,837.53
PROJECT FUND	\$23,146,550.00	\$1,002,805.35	\$14,796,327.41	\$8,350,222.59
WORKING CAPITAL FUND 1	\$1,410,000.00	(\$108,385.88)	\$102,943.13	\$1,307,056.87
COSTS OF ISSUANCE	\$738,450.00	\$0.00	\$734,403.26	\$4,046.74
UNDERWRITER'S DISCOUNT	\$455,000.00	\$0.00	\$455,000.00	\$0.00
COSTS OF ISSUANCE FUND	\$1,193,450.00	\$0.00	\$1,189,403.26	\$4,046.74
TOTAL PROJECT BUDGET	\$25,750,000.00	\$894,419.47	\$16,088,673.80	\$9,661,326.20

^{1.} See *Construction Update*: The \$128,385.88 Cash Bond for S.R. 56 Deceleration Lane on deposit with Florida Department of Transportation was refunded by the State in September and deposited to the Working Capital Fund. A Working Capital Draw of \$20,000.00 was submitted in Project Fund Requisition #12, therefore the net activity in the Working Capital Fund was (\$108,385.88) for the period.



Aerial Video

To follow Beach House at Wiregrass Ranch construction progress, please subscribe to the project YouTube channel: Beach House – Construction Update, where aerial videos of the project site are periodically published.



You can also access the channel with the "What's New" menu on the community website home page: <u>beachhousewiregrass.com</u> or in the Senior Communities gallery at <u>prevarian.com</u>.



CONSTRUCTION MONITORING REPORT – CM_11 (AUGUST Pay Application) 09.15.17




TABLE OF CONTENTS

1	Disclaimers and Requirements	1
2	Summary	2
3	Check List	4
4	Notice of Commencement	4
5	Permits and Approvals	5
6	Construction Schedule/ Budget	11
7	Lien Releases	17
8	Change Orders	24
9	Pay Applications and Certifications	29
10	Submittals and RFIs	36
11	l Licenses	39
12	2 Insurance	39
Α	Site Visit Photographs and Comments	40
В	Meeting Minutes	46

1 DISCLAIMERS AND REQUIREMENTS

The following report is provided in accordance with the Construction Disbursement and Monitoring Agreement for the above referenced project. All reviews are based on the material as provided to the construction monitor at the time of the report. The consultants or their consultants providing this report assume no responsibility for the schedule, design or construction of this facility. Comments and clarification requests noted in this report do not necessarily imply an error or omission exists. Comments or clarifications noted should be evaluated by the project design team and general contractor with response back to the construction monitor for inclusion into subsequent reports. Note: documents provided in this report are excerpts only to maintain a reasonable file size while provided some representation and reference. Full copies of these documents are available in the CM dropbox or by request.

2 SUMMARY

The General Contractor, per pay application #11 dated 08/31/17, has **completed 69%** of the project and has a completion date of **November 13**, 2017. The current schedule shows a delay, in comparison of the original schedule, in some trades (HVAC and Doors of approximately 4 to 6 weeks). However overall, the GC has indicated they are on schedule referring to a buffer in the schedule which was also identified by the CM in the pre-closing report. The CM will continue to monitor progress and has informed the owner and contractor a delay is possible based on the current projections and progress reviewed on the site should other trades be slowed or affected by the above divisions. The CM is continuing to participate in the mid-month OAC phone conference meetings to further monitor the potential delay.

In Pay Application #2 form December, 2016, Change Order #1 for \$270,224.00 for infrastructure improvements was introduced and a slightly lower portion paid out against this work to date. This change order was anticipated at closing but, was being reimbursed by the land seller. Thus, the change order was deducted from the contingency and was subsequently reimbursed by the owner and processed thorough USBank to the contingency as required by the CM. As of this pay application, \$208,669.98 has been reimbursed to the owner and is to be added back to the project contingency via check from the project to US Bank as Trustee.

Thus, the project is currently on budget but, is an approximately 2-3 weeks behind schedule as estimated by the CM.


Current Pay Application Summary

Original Contract Sum	\$14,641,950.00
Net Change (COR) from closing	\$279,081.97
Contract Sum to Date	\$14,921,031.97
Total Completed and Stored to Date	\$11,234,379.97
Less Retainage and Stored	\$1,123,437.00
Total Earned Less Retainage and Stored	\$10,110,942.97
Less Previous Payments	\$9,204,872.97
Requested Current Payment Due	\$906,070.00
Balance to Finish Including Retainage	\$4,810,089.00

WORK COMPLETION

Time/ Production Tabulation

Pay Application Date	Completed to date	Projected to date
10.06.16	0%	0%
10.31.16	1%	2.0%
11.30.16	5%	6.7%
12.31.16	13%	13.3%
01.31.17	20%	21.3%
02.28.17	30%	30.6%
03.31.17	39%	40.5%
04.30.17	47%	50.7%
05.31.17	52%	61.6%
06.30.17	60%	71.9%
07.31.17	69%	80.4%
08.30.17	75%	87.2%
09.31.17		94.7%
10.30.17		99.5%
TCO 11.13.17		100.0%

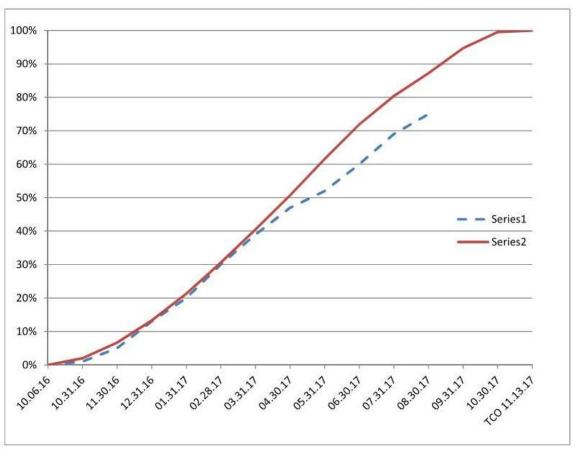

3 CHECKLIST

Requested Document	Responsible Team Member	Received
1. AIA G702 Pay Application	The Douglas Company	08/30/17
2. AIA G703 Continuation Schedule	The Douglas Company	08/30/17
3. Notice of Commencement	The Douglas Company	11/16/16
4. Copy of Current Permit Card	The Douglas Company	09/28/16
5. Required Permit Appendix A/B	The Douglas Company	08/30/17
6. Construction Schedule & Budget	The Douglas Company	08/30/17
7. GC-Arch Meeting Minutes	The Douglas Company	08/30/17
8. Lien Release	The Douglas Company	08/30/17
9. Lien Notices Received	The Douglas Company	None
10. Change Orders (If Applicable)	The Douglas Company	None
11. Architect's Certification	Architectural Concepts Inc.	08/30/17
12. Contractors Certification	The Douglas Company	08/30/17
13. Construction Monitors Cert.	Appono Consulting	09/01/17*

^{*}Item 13 is contingent on completion of Items 1-12.

4 NOTICE TO PROCEED / NOTICE OF COMMENCEMENT

Notice to Proceed - 10/03/16

Notice of Commencement - 10/13/16

^{**} Item has been requested but not received by time of report.

prevarian	2016161492
October 10. 2016	Permit Nos. 19133 and 74354 Permit Disc. 20 5/20 0/0000-01100 0110 0110 0110 0110 0110
0.000.1 20, 2020	State of Florida County of Pasco
Mr. Dennis Robinson The Douglas Company 200 East Robinson Street, Sulte 400 O'Irados, Foroida 32801	THE UNDERSHONED hereby gives notice that improvement will be made to certain real property, and in accordance with Chapter 713, Florida Stanten, the following information is provided to this Notice of Commencement.
Re: Notice To Proceed - Beach House Assisted Living at Wiregrass Ranch	 Description of property: Lot 1, Wirearna Parcel M24, according to plat recorded in Plat Book 23, Page 84, 85 and 86, of the Public Records of Pance County, Florida
Wesley Chapel, Florida	 General description of improvement: <u>Approximately 95.000 square fort, 2 story arrinted living center</u>
Dear Dennis:	3. Owner information:
This letter shall serve as the official Notice To Proceed with the construction of Beach House	a. Name and address: PSJ, Wirugmas, LP, a Texas limited partnership, 8214 Wastchester Drive, Suite
Assisted Living and Memory Care at Wiregrass Ranch per our contract dated September 9, 2016.	600, Dalles, TX
Due to Hurricane Matthew, and per previous conversations, the official "Date of	b. Interest in property: Fee Simple Owner
Commencement" under the contract shall be Wednesday, October 12, 2016.	c. Name and address of fee simple titleholder (if other than Owner):
We look forward to working with you on this project.	4. Contractor: The Donales Company, 200 ff. Robinson, Seitz 400, Drimdo, FL.
Sincerely.	Phone number: (407) 270 2001
11. Pull Cath	 Sirrety: Liberty Mutual Sweey, Bink One Towers, 8044 Montgomery Read, Suite 1508. Cincinnet. OH 43236
H. Dodd Crutcher	Phone number: (513) 792-1867
	Amount of Bond: \$14,691,950,00
	 Lander: J.S. Bank Noticensi Association, at Troster, 725 E. Robinson Street, Suite 250, Orlando, FL. 22001, Attn. Corporate Treat Department.
cc: J. Scott Walker	 Persons within the State of Florida designated by Owner upon whom notices or other documents may be served as provided by Section 713.13(1)(a)7. Florida Statume: Notes.
Michael Hass Kevin Green	 In addition to itself, Owner designates the following individuals to receive a copy of the Lienor's Netlice as provided in Section 713.13(1)(b), Florida Statutes: None.
	Expiration data of notice of commencement: <u>January</u> 15, 2018.
	PALAS CHELP DO RECO CURVA CONTROLLER 10/13/2016 19:133 AM 1 of 2 OR BK 9441 20 23 15
8214 Westchester Chrise, Sta. 600, Dallac, Texas 79225 214 736 7000 - prevanien com	

5 PERMITS AND APPROVALS

Based on information provided by the architect, general contractor, civil engineer and various governmental agencies the following permits & approvals may be required for the project. Permits and approval modifications made after closing shall be maintained by the Contractor and updated monthly as required by the CMDA.

Permit or Approval	Corresponding Plan Date / Permit Number	Received
 Zoning / Entitlement Approval 	20-26-20-0000-00100-0010	06/29/16
2. Plat / Re-Plat (County)	Parcel M24/ MSD15-002	04/06/16
3. Water Mgmt. Dist. Approval	714599/43027030.109	02/10/16
4. Site Plan Permit	PDD16-541 / LRG15-027	04/11/16
5. FDOT Permits	2015- (A-798-14 & D-798-9)	04/20/16,11/10/15
6. Utility Capacity	04-148-72	12/17/16
7. Building Permit	#74354 & #74353	11/16/16
8. FDEP Permit	FLR10PT88	07/26/16
9. NPDES Permit	Generic	01/13/16

Appendix A - Site Permits

Permits

State of Florida

Department of Environmental Protection


NPDES Generic Permit

For

Stormwater Discharge from Large and Small Construction Activities

Effective Date: 02/2015

This permit is issued under the provisions of Section 403.0885, Florida Stahutes, and applicable rules of the Florida Administrative Code pursuant to the Department's Redurally-approved National Floridate Elimination System (MPCES) stormwater regulatory program. Stormwater discharge associated with large construction activity, as defined at 40 C.F.R. Floridate 22.05(k) (1400, and herein, is regulated pursuant to Section 402(b)(2) of the federal Clean Walter Act (CWA). Stormwater discharge hosein, is regulated pursuant to Section 402(b)(2) of the Federal Clean Walter Act (CWA). Stormwater discharge hosein, is regulated pursuant to Section 402(b)(6) of the CWA. This permit constitution activities to surface waters of the Section 402(b)(6) of the CWA. This permit constitution activities to surface waters of the State, including through a Municipal Separate Storm Sever System (MSA). (Little this permit is terminated, modified or revoked, permittees that have properly distalland coverage under this permit are authorized to discharge to such that permit is demanded and the surface with the terms and conditions of this permit.

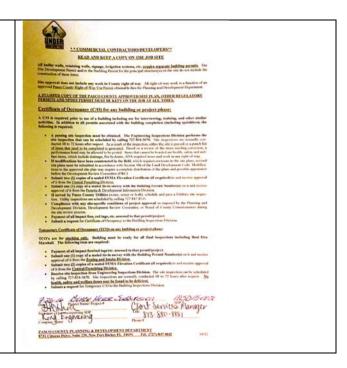



Florida Department of **Environmental Protection**

Bob Martinez Center 2600 Blair Stone Road Tallahassee, Florida 32399-2400 Rick Scott

Carlos Lopez-Cantera Lt. Governor

Jonathan P. Steverson Secretary

January 13, 2016

Dodd Crutcher Prevarian Senior Living 8214 Westchester Drive, Suite 600 Dallas, TX 75225

RE: Facility ID: FLR10PT88

Beach House Assisted Living Facility at Wiregrass Parcel M24 County: Pasco

The Florida Department of Environmental Protection has received and processed your Notice of Intent to Use Generic Permit for Stormwater Discharge from Large and Small Construction Activities (NOI) and the accompanying processing fee. This letter acknowledges that:

- · your NOI is complete
- your processing fee is paid-in-full; and
- you are covered under the Generic Permit for Stormwater Discharge from L Small Construction Activities (CGP), DEP Document No. 62-621 300(4)(a). om Large and

Your project identification number is FLR10PT88. Please include this number on all future idence to the Department regarding this pen

This letter is not your permit; however, this letter does serve as verification of permit coverage. A copy of the permit language is available online at www.dep.state.fl.us/water/stormwater/npdes/docs/cgp.pdf or by contacting the NPDES Stormwater Notices Center.

Facility ID: FLR10PT88 Page 2 January 13, 2016

Your permit coverage becomes effective 1/11/2016 and will expire 1/10/2021. To terminate your coverage prior to this expiration date, you must file a National Pollutant Discharge Elimination System (NPDES) Stormwater Notice of Termination, DEF Form 62-621,300(6) (NOT). An NOT must be filed within 14 days of either (a) your final stabilization of the site or (b) your relinquishment of control of the construction activities to a new operator. To renew your coverage beyond the expiration date, you must submit a new NOI and processing fee to the Department no later than two days before coverage expires.

Until your permit coverage is terminated, modified, or revoked, you are authorized to discharge stormwater from the construction site referenced in your NOI to surface waters in accordance with the terms and conditions of the CGP. Some key conditions of the CGP

- implementation of your stormwater pollution prevention plan (SWPPP);

- implementation of appropriate construction best management practices (BMPs);
 conducting and documenting routine inspections; and
 retaining the records required by the permit (including your SWPPP) at the construction site or the alternate location specified in your NOI.

If you have any questions concerning this acknowledgment letter, please contact the NPDES Stormwater Notices Center at (866) 336-6312 (toll-free).

Sincerely,



Krishna P Baral Computer Operator II NPDES Stormwater Program

ENGINEER COPY DRIVEWAY/CONNECTION PERMIT FOR ALL CATEGORIES PART 1: PERMIT INFORMATION OF Application Number: 2015-A-198-14 policytischer (1 Heavy sech für construction and the confidence of t Permittee: Prevarian Senior Living Note: See attached sheet h Section/Mile Post: 14091/5,860 Rt. State Road: 56 Sector/Mile Post: State Rose This contractor shall post this Perimt and Never available on this project side at all times and at exPART 2: PERMITTEE BY ORBANTOR—IN to the FDOT'S Design Standards Standard Sector/Locktor. Permittee Name: <u>Prevarian Senior Livro, Afth.: Dodd Coulter</u> This Driveway Permit does not permit utilities. Chy, Sase, Zip. Date. TX.75225. It is the responsibility of the Permittee to determine and comply with all County and determine and comply with all County and ExpressConnutardor Project Manager: King Engineerize Associates. Objection or the grain and entiry sections of the County and Engineer responsible for construction inspection: Mett Angenssa, P.E. the parmit appliage more stringent than NAME Department of Ransportation requirement Asling Address: #921 Memorial Highway, Suite 300 The Applicant is responsible for notifying The Applicant is responsible for onlying City, State, Zip. Tamba, Ft. 305M Chester of all clusting actival or braced utilized or for any order of the control of the contr PART 3: PERMIT APPROVAL The slove application has been reviewed and is hareby approved subject to all Provisions as situated. The divineway/connection shall be per Design The divineway/connection shall be per Design Standarder's 15. The existing pavenoist in free of connection between the grade and experience and pavenoist make on stating or connection to be stating or connection to the stating Department Representative's Name: ARRIN Gettin, P.E. With a Certific P.E. With a Cert Special provisions attached: S YES NO NO 2/20/16 If this is a normal (non-temporary) permit it authorizes construction to be extended by the Department as specific in 14-96.007(6). Ras following names for Flament and Shariful Provisions. porary) permit it authorizes construction for one year from the date of issuance. This can only



PASCO COUNTY, FLORIDA

"Bringing Opportunities Home"

WEST PASCO GOVERNMENT CENTER
PLANSING AND DEVELOPMENT DEPARTMENT
8731 CITZEND SRIVE. SUITE 230
NEW PORT RICHEY, PL. 34654
TELEPHONE: (727) 647-8142
FAX: (727) 647-8142
FAX: (727) 647-8140

March 1, 2016

Matt Angeross, P.E. King Engineering Associates, Inc. 4921 Memorial Highway, Suite 300 Tamps, Ft. 33634 mangerosa@kingengineering.com

RE: Beach House ALF – Wiregrass (M24), LRG15-027 Preliminary Site Plan Submittal

Please be advised that on March 1, 2016 the Planning and Development Department reviewed and approved the above-referenced project as noted on the enclosed agenda memorandum PDD16-541. This approval is issued under the provisions of Section 300, <u>Development Bruiew Procedures</u>, of the Pasco County Land Development Code.

The ownerfdeveloper is hereby notified that no activity shall commence on-site until both the completed notarized acknowledgment portion of the above-referenced agenda memorandum and receipt for payment of Pasco County utility impact fees (if applicable) are received by the Planning and Development Department. Any site specific conditions listed as requiring completion prior to Site Development Permit issuance must also be completed.

The owner's ideveloper's acceptance of the enclosed conditions constitutes a notice of authorization to perform all related work as allowed by Section 300, <u>Development Review Proceedures</u> of the Land Development Code, but shall not include the structure, septic tanks, signs, construction within Country/State right-of-way, and all other construction activities requiring separate governmental permits. Should the owner/developer object to any condition of approval as stated on the attached, a witten notice of appeal shall be submitted within 30 days of this decision in accordance with Section 40171, <u>Accordition</u> of the Passoc County's Land Development of the decision of the Passoc County's Land Developmental of the Country Co

"Pasco Cranty—Florida's premer county for halanced economic growth, environmental natainability, and first class services."



Southwest Florida 2279 Broad Breat, Broadwille, Florida 34004-8899 Water Management District (302) 78-7271 or 1-800-227-147 (Fl. only)

Prevarian Companies, LP Attr. Dodd Crutcher 8214 Westchester Drive, Suite 600 Deltas, TX 75225

Notice of Intended Agency Action - Approval
ERP Minor Modification
Project Name
Beach House Assisted Living Facility at Wiregrass Parcel M24
App IOPent No:
714999 / 43027030.109
PMSCO
Letter Received:
Spiritudin Data:
ScotTopHage:
10.2015
ScotTopHage:
521/T265/R20E; S29/T265/R20E; S20/T265/R20E

The File of Record associated with this application can be viewed at <u>http://www.fl.s.mdemed.state/.lus/erprieruheaech/ERPE/leacch.assz</u> and is also available for inspection Monday through Friday, accept for District holdeys, from 8:00 a.m. phough 5:00 p.m. at the District's Tampa Service Office, 7601 U.S. Highway 301 North, Tampa, Fronta 3:637.

If you have any questions or concerns regarding the application or any other information, please contact the Environmental Resource Permit Bureau in the Tampa Service Office.

Michelle K. Hopkins, P.E. Buneau Chief Sureau Chlef Environmental Resource Permit Bureau Regulation Division

Matt Angerosa, P.E., King Engineering Associates, Inc.

PLACE THIS SIGN WHERE IT CAN BE SEEN FROM THE STREET

SITE DEVELOPMENT PERMIT

PROJECT NAME: BERLY HOUSE SUBJECT NO: MSUIS-OFE ISSUED TO, DELIGIALING, SECULE LIVING PHONE: 44+ 18-18-19 DATE ISSUED: 1-24-1014 LOO NO 18-044 SY 254 ENERGY!

PASCO COUNTY

(727) 847-8132

CALL PROJECT MANAGEMENT 5 DAYS PRIOR TO COMMENCEMENT (727) 834-3670



PASCO COUNTY BUILDING PERMIT

COM - New Masonry or Masonry and Frame Walls

TO SCHEDULE AN INSPECTION OR DISCUSS A PROBLEM PLEASE CALL ONE OF THE FOLLOWING DADE CITY: (352) 521-4279 LAND O'LAKES: (813) 929-2766 NEW PORT RICHEY; (727) 847-8127

CONDITIONS OF THE PERMIT CONDITIONS OF THE PERMIT

A permit issued shall be construed to be a license to proceed with the work and not as authority to violate, cancel, after or set askide any of the provisions of the technical codes, nor shall issuance of a permit prevent the building official from thereafter requiring a correction of errors in plans, construction or violations of this code. Every permit sisued shall become invalid unless the work suthorized by such permit a commenced within six (6) months after the time the work is commenced. An extension may be requested in writing from the Building Official for inlenty (90) days and will demonstrate justifiable cause for the extension. If work ceases for ninety (90) days, the job is considered shandoned.*

*All work shall be performed in accordance with Pasco County Codes and Ordinances. Final site inspection and the provided of the prov

Engineering Department Inspection.

* Sanitation facilities shall be provided for the duration of construction at new building siles per FBC 3311.2.

* Final inspections are required for all permits issued. Failure to compty with this requirement could lead to a \$500.00 fine 80 days in the county jail, or both.

WARNING TO OWNER: YOUR FAILURE TO RECORD A NOTICE OF COMMENCEMENT MAY RESULT IN YOUR PAYING TWICE FOR IMPROVEMENTS TO YOUR PROPERTY. A NOTICE OF COMMENCEMENT MUST BE RECORDED AND POSTED ON THE JOB SITE BEFORE THE FIRST INSPECTION. IF YOU INTEND TO OBTAIN FINANCING, CONSULT WITH YOUR LENDER OR AN ATTORNEY BEFORE RECORDING YOUR NOTICE OF COMMENCEMENT.

DATE 03/01/2016 ISSUE LOCATION FLOOD ELEV. 72.3 OWNER JOB LOCATION 30070 STATE ROAD 56 PARCEL NO. ZONING DISTRICT WIREGRASS RANCH 20 26 20 0000 00100 0010 CONTRACTOR THE DOUGLAS COMPANY

Development Permits issued by Pasco County do not waive requother agency. Do NOT rely solely on this document. rement for obtaining any other permits issued by any

NOTICE OF RESTRICTIONS

To the requirements of this permit, there may be additional restrictions applicable to this property that may be public records of this County, and there may be additional permits required from other governmental entities the management districts, state agencies or federal agencies.

This PERMIT may be subject to 'Deed Restrictions' which are more restrictive than County regulations. The PERMIT holder assumes responsibility for compliance with applicable deed restrictions.



PASCO COUNTY **BUILDING PERMIT**

COM - New Masonry or Masonry and Frame Walls

TO SCHEDULE AN INSPECTION OR DISCUSS A PROBLEM PLEASE CALL ONE OF THE FOLLOWING DADE CITY: (352) 521-4279 LAND O'LAKES: (813) 929-2766 NEW PORT RICHEY: (727) 847-8127 CONDITIONS OF THE PERMIT

A permit issued shall be construed to be a license to proceed with the work and not as authority to violate, cancel, alter or set aside any of the provisions of the technical codes, nor shall issuance of a permit prevent the building official from thereafter requiring a correction of errors in plans, construction or violations of this code. Every provisions after the time the become invalid unless the work authorized by such permit a commander within (6) months after the time the work is commenced. An extension may be requested in writing from the Building Official for ninely (90) days, and will demonstrate justifiable cause for the extension. If work ceases for micro-shall be made by the Engineering inspections Division for all commercial industrial, and multi-family construction, as per site plan, before final power release in given. Call (727) 634-3670 to schedule an Engineering Department inspection.

Sanitation facilities shall be provided for the duration of construction at new building sites per FBC 3311.2.

Final inspections are required for all permits issued. Faiture to comply with this requirement could lead to a \$500.00 fine 60 days in the county juil, or both.

WARNING TO OWNER: YOUR FAILURE TO RECORD A NOTICE OF COMMENCEMENT MAY WARNING TO OWNER: YOUR FAILURE TO RECORD A NOTICE OF COMMENCEMENT MAY RESULT IN YOUR PAYING TWICE FOR IMPROVEMENTS TO YOUR PROPERTY. A NOTICE OF COMMENCEMENT MUST BE RECORDED AND POSTED ON THE JOB SITE BEFORE THE FIRST INSPECTION. IF YOU INTEND TO OBTAIN FINANCING, CONSULT WITH YOUR LENDER OR AN ATTORNEY BEFORE RECORDING YOUR NOTICE OF COMMENCEMENT.

ISSUE LOCATION NPR FLOOD ELEV. DATE 03/01/2016 ZONING DISTRICT MPUD PARCEL NO. 20 26 20 0000 00100 JOB LOCATION 30070 STATE ROAD 58 OWNER WIREGRASS RANCH 0010 CONTRACTOR
THE DOUGLAS COMPANY BACK SET BACKS-FR SIDE Development Permits issued by Pasco County do not waive requirement for obtaining any other permits issued by any other agency. Do NOT rely solely on this document.

In addition to the requirements of this permit, there may be additional restrictions applicable to this property that in the polici records of this County, and there may be additional restrictions applicable to this property that such as water management districts, state agencies or federal agencies.

The PERMIT may be subject to 'Deed Reserves...

This PERMIT may be subject to 'Deed Restrictions' which are more restrictive than County regulations. The PERMIT hoter assumes responsibility for compliance with applicable deed restrictions.


ELEVATION CERTIFICATION:


I.S. DEPARTMENT OF HOWELAND SECURITY edical Emergency Management Agency anoid Finite insulance Program				r.	OMB No. 1980-0008 Expiration Date: November 30, 201	
		Important	TION CERT	nn pages 1-9.		
by all pages of th					enticompany, and (3) building owner	
		TION A - PROPERTY	INFORMATION		OR INSURANCE COMPANY USE	
A1. Building On Prevarian Senior		Yenguiss UP			Policy Number:	
Box No.		cuding Apt., Unit, Suit	le, and or tildg. No.) or P	O. Route and	Company NAIC Number:	
30070 State Hos	0.96				tiP Code	
City Wester Cha			Stane Florida		DP COOR - 13543	
	structor (List a		as Pascel Number, Logal		1000	
A4 Punton lise	in a Reader	tial Non-Residential.	Addison, Accessiny, etc.	V		
A5. Lastudation			Long 82.3243°e		☐ NAD 1967 (NAD 1963	
			e Certificate is being use			
			in Construct to Design poo			
A7. Building Dis						
		pace or endosum(s)	n nav 1994			
		nguck or enclosure(k)				
				within 1.0 foot above	rdjacent grade 0	
		penings in Aff.b		within 1.0 foot above i	edjacont grade 0	
c) Total net	overs of Bood or		0 sqin	within 1.0 foot above /	edjaconi grade 0	
c: Total net d) Engineer AS. For a buildin	area of Bood o and flood operar g with an orfact	gerings in Aff.h ge? ☐ Yes 图 R red garage:	ni peg in	Within: 1.0 foot above /	ediaconi grade 0	
c; Total net ill: Engineer All: For a buildin	area of Bood o and flood operar g with an orfact	gerings in All b ger? 🔲 Yes 🖾 fi	ni peg in	within 1.0 foot above /		
 G: Total net d) Engineer AD: For a building a) Square h 	area of Bood o ed flood operar g with an infact setage of attact	penings in A6.b Ige? ☐ Yes ☐ R and garage: and garage ☐	ni peg in			
c) Total net il) Engineer A9. For a buildin a) Square h b) Number	area of Bood o ed flood operar g with an infact sotoge of other if permanent fo	perings in All b gg?	0 og m og #			
c) Total net d) Engineer AB For a truldin a) Square fi (i) Number c) Total net	area of Bood of aid flood operar g with an infact sotoge of attact if permanent fo area of Bood or	perings in All b gg?	0 sq in aq 1 nuchod garage within 1.5 aq in			
c) Total net d) Engineer AB For a truldin a) Square fi (i) Number c) Total net	area of Bood operar g with an infact setage of attact if permanent 6 area of Bood operar and Bood operar	penings in Affibración de la propertie de la p	0 sq in aq 1 machos garage within 1.5 0 aq in No	tocratore adjacent gr	whe 0	
ci Total Het di Enginea All For a buildin a) Square fi b) Number c) Total nel d) Enginear	area of Bood or and flood operar g with an infact obtage of obsol if permanent 6 area of Bood or and Rood operar SE arth Harris & C	penings in A6 h gg? ves n ned garage red garage	0 sq in 10 sq in 10 sq in 10 sq in 10 sq in	tocratore adjacent gr	antr0	
cii Total Het iti Engineer All. For a tuildin a) Square fi iiii Number ci Total net di Engineer Bit NEP Comm New Port Richey Vi Magi Pared	area of Bood or and flood operar g with an infact obtage of obsol if permanent 6 area of Bood or and Rood operar SE arth Harris & C	penings in All bioge?	0 sq m aq m machod garage within 1.5 0 sq in No INSURANCE RATE MA Paleo D7, FIRM Faris	tocratore adjacent gr	0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0	
cii Total Het iti Engineer Adi. For a tuictin a) Square fi iii) Number cii Total net dii Engineer Bii NEIP Comm New Port Richtey Vi Mago [®] aned Rumber	area of Food or and flood operar g with an infact ordage of attact of permanent fi area of flood or and flood operar SR arety Name & C City of & 1200 BS. Suffer	serings in A&b ggr	0 sq in sq 1	toor above educant of AP (FIRM) INPORMAT TO	83. Some Feedar 89. Ber Fred Devalation (1) 2 now AV, cod Base	
ci Total Het di Engineer All. For a tuicte a) Square fi ii) Number c) Total net d) Engineer B1 NEIP Comm New Port Richey d Magin** Rundler Rundler	area of Food o ed flood operar g with an infact ootoge of attact of permanent fi- area of flood operar and flood operar SE area, Floor is A. C. Cop of S. 1200	penings in All bioge?	0 sq in 10 10 10 10 10 10 10 10 10 10 10 10 10	footaboye adjacent gr UP (FIRM) INFORMAT Inc.	0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0	
c) Tribal ned (ii) Engineera AD, For a quidel (iii) Equare fi (iii) Number (ii) Eugeneer (iii) Engineer (iii) E	ares of Eood of self-flood operaring with an entant selection of permanent if several of Social operaries operaries of Social operaries operaries of Social operaries	penings in A& b gg?	B sq in sq in	Increbing information AP (FIRM) INFORMATION BB Fixed Zone(s) X. A. AE double extend in fact.	83.564e 83.564e 83.564e 83.6646 83.6	
c) Tribal ned (ii) Engineera AD, For a quidel (iii) Equare fi (iii) Number (ii) Eugeneer (iii) Engineer (iii) E	ares of Eood of self-flood operaring with an entant selection of permanent if several of Social operaries operaries of Social operaries operaries of Social operaries	penings in A& b gg?	B sq in sq in	Increbing information AP (FIRM) INFORMATION BB Fixed Zone(s) X. A. AE double extend in fact.	E3	
c) Tribal ned (ii) Engineera AD, For a quidel (iii) Equare fi (iii) Number (ii) Eugeneer (iii) Engineer (iii) E	area of Eoual or med flood appears grading and appears grading and appears of permanent for a series of Special Appears of Spec	certifica in 46 b is greatly as a service of the certification of the ce	B sq in sq in	Increbing information AP (FIRM) INFORMATION BB Fixed Zone(s) X. A. AE double extend in fact.	83.564e 83.564e 83.564e 83.6646 83.6	

	RTANT: In these spaces, or					FOR INSU	RAND	E COMPANY USE
	ng Street Address (including 7 State Road 56	Apt., Unit, State, andico	Bidg No.) or P.O. Ro	ute and Box	No	Policy Nur	nter	
Dry Neore	vy Chapel	5io Pio	de 2/1 rida 331	Code 543		Company	HAIC S	ishber
	SECTION	ÓN C – BUILDING EL	EVATION INFORMA	TION (SURY	EY RE	QUIRED)		
	Building elevations are base 'A new Elevation Conficute		on Orewings* [2] the			cton* [Finish	ed Construction
C2	Elevations – Zones A1–A30 Complete terms C2 a–h beld Benchmark Utilized: 581-03	. AE, AH, A (with BFE), ow abcording to the buil	VE, V1-V30, V (with 8	SFE), AR. AR. In Ben A7. I	A AR	AE, AR;A1- a Riss only	A30, A entor	RIAH, ARIAO.
	Indicate elevation datum use			IW.				
		WAVE 1988 Chec						
	Datum used for building elev	rations must be the ear	to as that used for the	B1-E		Check	the Inie	beautinement used
	w). Top of bottom floor (Inclu	ding basement, crawing	sece, or enclosure floo	74	75	183	feet	☐ motors
	b). Top of the next higher fie	ice.		116	75	8	foot	- rotes
	a) Bottom of the lowest horse	zontal structural membe	er (V Zones anly)			- X	toot	☐ motors
	d). Attached garage (top of	stab)			_	58	feet	meters.
	 a) Lowest elevation of mach (Describe type of equipm 	hinory or equipment ser arm and location in Con	viong the building renents)		20	- 8	foot	☐ meters
	f) Lowest adjacent (finished	I) grade next to building	(6AG)		10	- 8	feet	neters.
	g). Highest adjacent (froshe	d) grade next to building	g (HAG)	. 74	70	- 8	teet	☐ meters
	 Lowest adjacent grade at structural support 	l lowest elevation of de-	ck or stars, including		70	×	feet	retes
	SECT	ION D - SURVEYOR	ENGINEER, OR AR	CHITECT C	ERTIFI	CATION		
	certification is to be signed a 5fy that the information on the ement may be pureshable by				ized by ravarie	law to cert the Tunder	Ty silev started t	alton information. Not any false
Wen	e twittede and longitude in Se	rction A provided by a fi	censed land surveyor?	El Yes D	No.	Che	ck hen	of attachments.
	Fer's Name pt Bis		License Number PLS 3860			П		
Title Proje	act Manager					1		
	pany Name Surveys, LLC					14	Pla Se	2
Addr P.O.	955 Box 180952	0.					. He	
City Atlan	nortie Springs /	900	State Ficrids	ZIP Code 32716				
Sign	sture fully	29	Date 02/07/2017	Telephone (407) 834	4 003			
Copy	all pages of this Elevation Ce	rtificitie and all attaches	ents for (1) community of	Worl, (2) Insu	rance a	genticompo	iny, an	(3) building owner
Com	ments (including type of equi ade at 0.50 below finals floor	pmerit and location, per	C2(v), if applicable)					

INSPECTION STATUS:

Permit # 74354

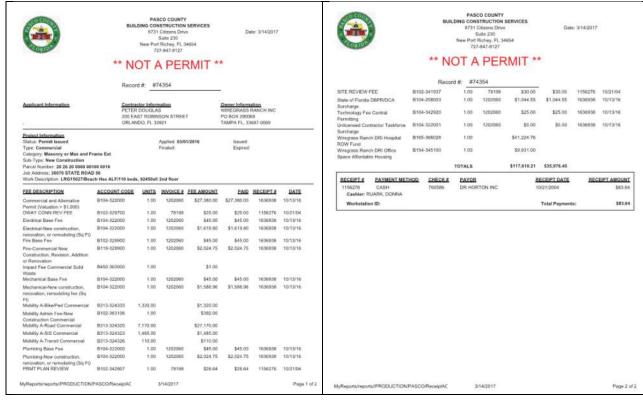

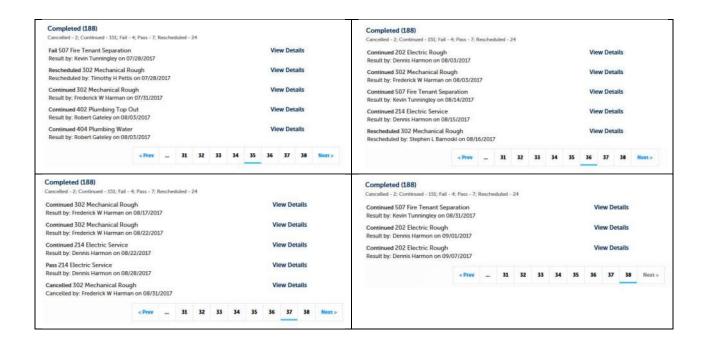

Failures under Permit #74354

There are no reported failures per the County inspection website for this pay application period.

PERMIT FEES:

The County has reduced its charges from \$13,735.00 to \$2,069.75 for revisions 2 through 6 submitted. At of the time of the OAC, the Owner had provided the GC payment for permit review fees, but there are a few outstanding electrical comments to be addressed. The County has not received funds at the time of this report.

To schedule inspections for your permit please select Inspections under Record Info. Instructions on how to: Pay 1 Fee Item if Multiple Inspection Fees Exist

Fees

Outstanding:				
Date	Invoice Number	Amount		
06/06/2017	1260489	\$45.00	Pay Fees	
05/18/2017	1279617	\$45.00	1.11.000.10.10.00	
05/17/2017	1255550	\$2,069.75		
Total outstanding	fees: \$2,159.75			
Paid:				
Date	Invoice Number	Amount		
09/01/2016	1202060	\$1,588.96	View Details	
10/21/2004	78199	\$25.00	View Details	
10/21/2004	78199	\$28.64	View Details	
10/21/2004	78199	\$30.00	View Details	
		< Prev Additional Results: 1234	Next >	


Total paid fees: \$36,156.45

6 Construction Schedule and Budget

Construction Schedule (Original)

Exhibit H - Project Schedule

	Task Name	Duration	Start	Finish
1	Beach House at Wiregrass Construction Schedule	278 days	Thu 10/6/16	Tue 11/7/17
2	Construction	278 days	Thu 10/6/16	Tue 11/7/17
3	Sitework	39 days	Thu 10/6/16	Wed 11/30/16
4	Mobilization	2 days	Thu 10/6/16	Fri 10/7/16
5	Survey/Silt Fence/Erosion Control Measures	3 days	Mon 10/10/16	Wed 10/12/16
6	Clear and Grub	2 days	Thu 10/13/16	Fri 10/14/16
7	Site Rough Grade	5 days	Mon 10/17/16	Fri 10/21/16
8	Building Pad Construction	10 days	Mon 10/24/16	Fri 11/4/16
9	Retaining Wall	15 days	Mon 11/7/16	Mon 11/28/16
0	Underground Utilities	27 days	Mon 10/24/16	Wed 11/30/16
16	Building Underground & Structure	121 days	Mon 11/7/16	Thu 4/27/17
17	Survey Building Corners	1 day	Mon 11/7/16	Mon 11/7/16
18	Elevator Pits	9 days	Tue 11/8/16	Fri 11/18/16
21	Concrete Foundations & MEP Sleeves	15 days	Tue 11/8/16	Tue 11/29/16
22	Masonry Stem Walls & MEP Sleeves	15 days	Tue 11/15/16	Tue 12/6/16
23	Underground MEP Rough In	16 days	Tue 11/22/16	Wed 12/14/16
32	Building C Soil Poison & Concrete SOG	5 days	Thu 12/1/16	Wed 12/7/16
33	Building B Soil Poison & Concrete SOG	5 days	Thu 12/8/16	Wed 12/14/16
34	Building A Soil Poison & Concrete SOG	8 days	Thu 12/15/16	Tue 12/27/16
35	1st Floor	37 days	Wed 12/7/16	Tue 1/31/17
36	Building C	15 days	Wed 12/7/16	Thu 12/29/16
37	Masonry Walls	10 days	Wed 12/7/16	Wed 12/21/16
12	Concrete Columns	15 days	Thu 12/8/16	Thu 12/29/16
13	Concrete & Masonry Beams	5 days	Thu 12/22/16	Thu 12/29/16
44	Building B	15 days	Wed 12/14/16	Fri 1/6/17
15	Masonry Walls	10 days	Wed 12/14/16	Thu 12/29/16
50	Concrete Columns	15 days	Thu 12/15/16	Fri 1/6/17
51	Concrete & Masonry Beams	5 days	Fri 12/30/16	Fri 1/6/17
52	Building A	24 days	Tue 12/27/16	Tue 1/31/17
53	Masonry Walls	16 days	Tue 12/27/16	Thu 1/19/17
58	Concrete Columns	24 days	Wed 12/28/16	Tue 1/31/17
59	Concrete & Masonry Beams	8 days	Fri 1/20/17	Tue 1/31/17
50	2nd Floor	47 days	Fri 12/30/16	Tue 3/7/17
51	Building C	25 days	Fri 12/30/16	Fri 2/3/17
62	Hollowcore Planks, Reinforce, Grout	7 days	Fri 12/30/16	Tue 1/10/17
63	Metal Pan Stairs	2 days	Mon 1/9/17	Tue 1/10/17
64	Safety Rails & Topping Slab	5 days	Wed 1/11/17	Tue 1/17/17
65	Framing and MEP Layout	3 days	Wed 1/18/17	Fri 1/20/17
66	Load Bearing Wood Walls & Sheathing	8 days	Wed 1/18/17	Fri 1/27/17
67	Masonry Walls	9 days	Tue 1/17/17	Mon 1/30/17
72	Elevator Shaft Concrete Cap	4 days	Tue 1/31/17	Fri 2/3/17
73	Building B	25 days	Mon 1/9/17	Fri 2/10/17
74	Hollowcore Planks, Reinforce, Grout	7 days	Mon 1/9/17	Tue 1/17/17
75	Metal Pan Stairs	2 days	Mon 1/16/17	Tue 1/17/17
76	Safety Rails & Topping Slab	5 days	Wed 1/18/17	Tue 1/24/17
77	Framing and MEP Layout	3 days	Wed 1/25/17	Fri 1/27/17
78	Load Bearing Wood Walls & Sheathing	8 days	Wed 1/25/17	Fri 2/3/17
79	Masonry Walls	9 days	Tue 1/24/17	Mon 2/6/17
84	Elevator Shaft Concrete Cap	4 days	Tue 2/7/17	Fri 2/10/17
85	Building A	25 days	Wed 2/1/17	Tue 3/7/17
86	Hollowcore Planks, Reinforce, Grout	10 days	Wed 2/1/17	Tue 2/14/17

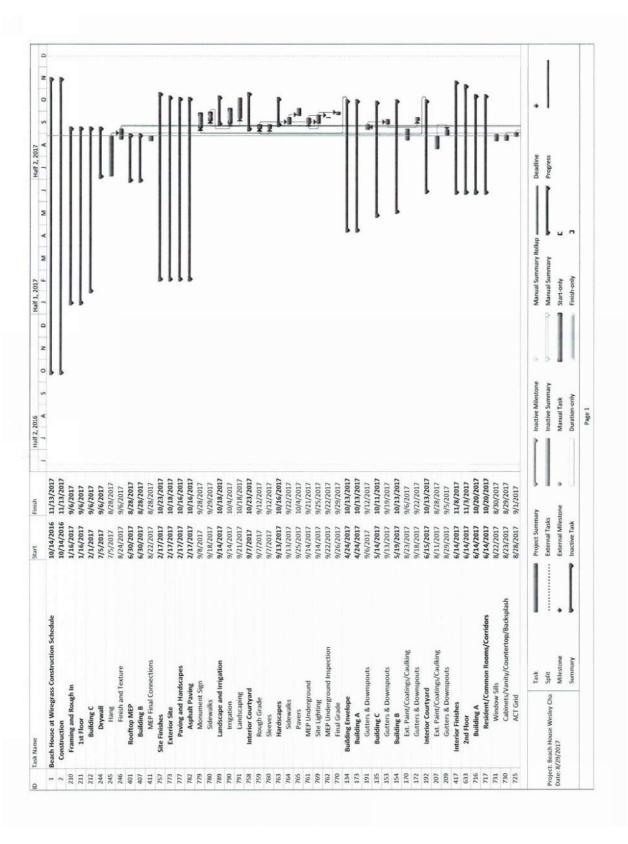

Potential Delays / Costs Being Monitored

HAND- GUARDRAIL ALONG RETAINING WALL NORTH SIDE

A guardrail shown in the civil plans along the west side of the site against the pond was deleted as part of a value engineering exercise. However, this guardrail has not been deleted from the civil plans prompting the CM to request acknowledgement from the civil engineer or architect that this wall is not required.

As 04/15/17 report, the architect has advised the CM this remains a non-issue.

STORM WATER TIE-IN TO RENTION POND - TURBIDITY ISSUES (NO DELAY AS TIE-IN IS COMPLETE)

The GC continues to work to resolve current turbidity issues in the off-site common master retention pond required to be used to by the project but, cannot due an unsatisfactory level of sediment by the governing authority.

The Owner and Project Architect have charged the Civil Engineer to aid and assist in the dewatering process of the pond to the south of the site. The pond is the end destination for the site's storm water. The Civil Engineer's email response and solution is outlined below and was sent to the water management district for approval earlier this month. Approval was received and dewatering of pond is slated to start April 17, 2017.

As of 05/15/17 report, the storm water tie in is complete and no delay expected.

INSTALLATION OF ROOFTOP HVAC UNITS DELAYED (Potential Delay)

There has been an industry wide shortage of HVAC units in this region due to increased construction projects. An HVAC delay has a direct impact on Interior finish as many of the products need to set or be stored on site in conditioned space, i.e. millwork and case work for installation. In addition, it can slow down interior framing of ceilings and soffits as HVAC installers need access. As of this report, all roof top units have not been turned on as the GC coordinates with the county fire department, HVAC and electrical subcontractors.

Residential PTAC units are scheduled to start installation by mid-August.

CASEWORK, and FINALIZED DOOR SCHEDULE, (Potential Delay)

In addition to the HVAC delays the following casework, flooring and doors can be delayed as a result of non-conditioned air in the building which can affect materials due to the high humidity in the region. Additionally, the GC advised it is delaying electrical tie in as he cannot secure the building due to unapproved and late approved door hardware schedules. The Owner has advised it will be these will be completed as soon as possible while the GC has secured a quick turnaround from their

supplier for the doors. At the time of this report, security issues are a concern as there are no exterior doors installed or on site. Temporary doors have been constructed and installed in all exterior opening to aid in security. Interior doors are onsite, being painted and installed.

SEVERE WEATHER DELAY - HURRICANE IRMA, (Imminent Delay)

The CM requested and received a copy of the GCs current Hurricane Preparedness Plan on 09/05/17. In addition, the GC provided a letter on 09/07/17 indicating a possible delay based on the pending storm. Please find the attached letter on page 16 of this report. Hurricane Irma made landfall on west coast of Florida and extended to the Wesley Chapel area on 09/10/17. A state of emergency was initiated for the State by the Governor however, no evacuations were ordered for this flood zone. Interim site visits where performed by the CM prior to and immediately after the hurricane to assess damages. The Architect and owner's representative have both visited the site. Minor water damage to drywall was observed in resident rooms where PTAC and VTAC units had not been placed and driving rains gained access through vents. Additional water intrusion was discovered in the memory care units on the north end of the building facing west due to incomplete grading. Minor facia damage was observed on one side of the building but, no other damage was evident. A meeting with the owner was conducted during the week following the event and the GC is in the process of removing any water damaged materials. The CM will continue to monitor and will update in the next report.

Due to storm preparation and mandatory site closures for high winds, the CM estimates a one-week (7 calendar day) delay to the project is likely. A delay of project change order or report from the GC has not yet been received.

As of 09/15/17 report, it is possible for the GC to make their contractual completion date with careful planning and scheduling of subcontractors to include weekends (currently being utilized on Saturdays) and utilizing a buffer the GC provided in the schedule. The CM will continue to monitor the issue and make the team aware of the potential delay and suggest appropriate actions. It is recommended that the Owner schedule the AHCA visit with the Operator after substantial completion but, in conjunction with the certificate of occupancy expectation date to avoid a 30-day lapse between the C.O. and licensing. This will be discussed in the next OAC meeting.

Schedule of Values Summary

Bid Package	Description	App	rox. Value
1	Sitework	\$	224,349.00
6	Asphalt Paving	\$	268,990.00
12	Landscaping	\$	210,426.00
23	Building Concrete	\$	808,124.00

24	Precast	\$ 321,190.00
25	Building Masonry	\$ 456,250.00
31	Rough Carpentry	\$ 626,000.00
33	Cabinets & Tops - units	\$ 316,792.00
34	Cabinets & Tops - commons	\$ 349,250.00
35	Interior Wood Trim	\$ 453,789.00
39	Flat TPO Roof	\$ 367,500.00
54	Stucco	\$ 203,000.00
55	Drywall, Metal Soffits	\$ 717,000.00
56	Ceramic & Vinyl Floors	\$ 356,632.00
59	Painting & Wallcoverings	\$ 238,049.00
72	Comm. Kitchen Equip.	\$ 255,888.00
75	HVAC	\$ 982,567.00
76	Plumbing	\$ 961,855.00
77	Fire Protection	\$ 239,300.00
78	Electrical & Low Voltage	\$ 1,460,203.00



September 6, 2017

Via email

Prevarian Senior Living 8214 Westchester Drive, Suite 600 Dallas, TX 75225

Mr. Scott Walker Attention:

Beach House at Wiregrass Project:

Hurricane Irma (Delay Notice) Subject:

Dear Mr. Walker:

As discussed today, The Douglas Company began making preparations for the impending Hurricane Irma on Wednesday, September 6, 2017. As such, the project's critical path is stopped. Currenty, Hurricane Irma is classified as a Category 5 Hurricane and is projected to make landfall in the State of Florida as a Category 4 Hurricane early Sunday, September 10, 2017. Depending on the final path of this hurricane and its severity, the project could experience an extended delay. This delay is specified as an Excusable Delay as defined in Article 8.3.1.2. The Douglas Company will be requesting a claim for additional time starting today until such time after the hurricane when TDC can safely return to the site and commence construction activities on the project's critical path.

§ 8.3 DELAYS AND EXTENSIONS OF TIME

(Paragraph deleted)

§ 8.3.1.1 For Excusable Delays, Contractor's sole remedy shall be an increase to the Contract Time in accordance with Section 15.1.5 of these General Conditions. For delays caused by the acts or omissions of Owner or the Architect, Contractor's sole remedy shall be a day for day extension of the Contract Time and per diem general conditions costs of \$1,800. Except for the remedies expressly provided in this Section 8.3. Contractor waives any right to make a claim for damages for delay in the Work of any type or duration whatsoever, whether contemplated. foreseeable or unforeseeable, including without limitation my claim to rescind the Contract or of quantum meruit or cardinal change. The foregoing is not intended to supersede or limit Section 3.7.4 hercof.

§ 8.3.1.2 "Excusable Delay" means any delay, obstruction, or interference in the Work resulting from any cause after the date of the Agreement and before Substantial Completion if such cause is beyond Contractor's and/or a Subcontractor's reasonable control and was not caused by Contractor's and/or a Subcontractor's error, fault, or negligence. Excusable Delay shall include delay, obstruction, or interference caused by: (a) acts of God; (b) fire, earthquake, explosion, landsfide, fightning or flood; (c) epidemic; (d) strikes (other than a strike caused by, or within the control of, Contractor and/or a Subcontractor); (e) lockcosts by persons or entities other than Contractor and/or a Subcontractor; (f) riots, civil disturbance, inserrection, enemy action, or war; (g) embargoes or blockades; (h) concealed or unknown conditions referred to in clauses (1) and (2) of Section 3.7.4; (i) [intentionally omitted]; (i) the delay of any governmental emity in issuing any permits necessary to perform the Work (including delay due to incompleteness or other inadequacies in the Contract Drawings and Specifications); provided that Contractor uses commercially reasonable efforts to secure all such permits and does not contribute to the failure of the governmental entity to timely issue any such permits; (k) injunctions, or orders of any governmental entity; (l) temporary or permanent interruption or failure of any company providing utilities to the Project or necessary in connection with the Work; (m) abnormal weather conditions; and (n) any other causes beyond Contractor's and/or a Subcontractor's reasonable control. For the avoidance of doubt, "Excusable Delay" does not include any delay, obstruction, or interference resulting from (i) uncovering, removal, replacement or repair of defective or incorrect Work previously performed by Contractor or any Subcontractor; (ii) Work required by reason of Contractor's (or any Subcontractor's) fault; (iii) any periods when any policy of Required Contractor Insurance or Bonds to be secured and maintained by Contractor or any Subcontractor is not in effect; (iv) Contractor's (or any Subcontractor's) failure to place timely orders for delivery of materials, equipment or services; (v) any other loss of time resulting from the fault or neglect or willful act or omission of Contractor, any Subcontractor, or their employees; or (vi) Contractor's and/or a Subcontractor's failure to employ an adequate construction force (number and quality).

§ 8.3.2 Claims relating to time shall be made in accordance with applicable provisions of Article 15.

Prevarian Senior Living September 7, 2017 Page Two

§ 15.1.5 CLAMS FOR ADDITIONAL TIME

§ 15.1.5.1 Contractor may request an increase in the Contract Time by giving a written notice to Owner which briefly describes the delay and estimates the duration of the delay (a "Delay Notice") within fourteen (14) days after Contractor receives notice or otherwise becomes aware that the Excasable Delay (defined in Section 8.3.1.2) has commenced or can be expected to commence. A Delay Notice shall specify in as much detail as reasonably practicable: (a) the date when the delay began; (b) the cause of delay; (c) the estimated duration of the delay and its effect on the construction schedule; and (d) actions taken or to be taken by Contractor to mitigate the delay, if any. A Delay Notice shall include all documents and other information then in Contractor's possession which Contractor decems refevant to the request for extension. If a delay continues after the giving of a Delay Notice, Contractor shall keep Owner reasonably apprised of the status of the matter and shall farnish to Owner any documents or information available to Contractor as Owner may reasonably request from time to time.

§ 15.1.5.2 If adverse weather conditions are the basis for a Claim for additional time, such Claim shall be documented by data substantiating that weather conditions were abnormal for the period of time, could not have been reasonably anticipated and had an adverse effect on the scheduled construction.

If you have any questions, please don't hesitate to contact me at 407.269.3275.

Very truly yours,

THE DOUGLAS COMPANY

Micah Hoskinson Project Manager

cc: Allan Brown

Dodd Crutcher

Michael Hass Bo Russ

Shawn Pierson

Steve Rodgers

Kevin Green

Dave Bockbrader

Peter Douglas

MIDWEST | 1716 Perrysburg Holland Road | Holland, OH 43528 | 419.865.8600 | 419.866.8835 fax SOUTHEAST | 200 East Robinson Street, Suite 400 | Orlando, FL 32801 | 407.370.2001 | 407.370.2005 fax

LIEN RELEASES

The following Notice to Owner (NTO) filings have been received by the CM: (Note the CM is not listed on the Notice of Commencement (NOC) and thus, will depend on notices received by the owner unless corrected.)

*With the pending delay in the project, the CM has authorized the pay application without the GC providing subcontractor's lien releases due to the time lag between previous payments and the Hurricane event. The GC has provided and an additional conditional Lien release at the request of the CM in lieu of this standard requirement. The CM is expecting the prompt payment to aid in the expedited/uninterrupted delivery of doors and other materials which have been an issue with the projects schedule. The GC is expected to have all lien releases to date for the next OAC/ pay application or payments will be held. The Owner has not advised the CM of any pending liens or intent to lien at the time of this report.

LIEN NOTICE TO OWNER SCHEDULE:

Lien Notice	Under Order By	NTO Date	Release (Partial)
The DOUGLAS COMPANY	PSL Wiregrass LP		08/31/17
ANGELO'S RECYCLED MAT.	The Douglas Company	01/10/17	07/08/17
ASAP SHELL CONTRACTING	The Douglas Company		05/25/17
Builders FirstSource	ASAP Shell Contracting	02/07/17	05/25/17
Hughes Tool Supply Inc	ASAP Shell Contracting	02/14/17	04/25/17
COLONIAL PRECAST CONC	The Douglas Company	01/19/17	02/25/17
CCS MECHANICAL	The Douglas Company		05/25/17
ACE Staffing Unlimited	CCS Mechanical		04/25/17
Tom Barrow CO.	CCS Mechanical	02/17/17	04/25/17
Carroll Air	CCS Mechanical		04/25/17
People Ready FL	CCS Mechanical		04/25/17
EARTH TRADES OF CENT. FL	The Douglas Company	11/14/16	04/25/17
A Plus Sock Installation	Earth Trades of Cent. FL	11/08/16	FINAL
Amerifactors- FL Silt Fence	Earth Trades of Cent. FL	11/07/16	FINAL
Allied Trucking of Orlando	Earth Trades of Cent. FL	11/16/16	04/25/17
Angelo's Recycled Mat.	Earth Trades of Cent. FL		04/15/17
Bach Asphalt	Earth Trades of Cent. FL		FINAL
Ferguson Enterprises	Earth Trades of Cent. FL	11/14/16	04/25/17
LS Curb Service	Earth Trades of Cent. FL	02/08/17	04/25/17
CEMEX	LS Curb Service	03/09/17	04/25/17
Mack Industries	Earth Trades of Cent. FL	12/06/16	FINAL
NEF Rentals	Earth Trades of Cent. FL	01/03/17	04/25/17

Newman Tractor Earth Trades of Cent. FL 10/27/16 04/25/17 Synergy Rentals Earth Trades of Cent. FL 04/25/17 Thompson Pump & MFR Earth Trades of Cent. FL 11/04/16 FINAL WBE Environment Earth Trades of Cent. FL FiNAL EAST COAST APPLICATORS The Douglas Company 05/07/17 06/25/17 FABRICATED PRODUCTS The Douglas Company 05/07/17 06/25/17 FRS CONSTRUCTION The Douglas Company 04/14/17 06/25/17 Gator Gypsum FRS Construction 04/26/17 05/25/17 JN ELECTRIC The Douglas Company 01/09/17 06/25/17 JN ELECTRIC The Douglas Company 01/09/17 06/25/17 O6/25/17 JN Electric Supply Inc JN Electric 01/18/17 06/25/17 O6/25/17 O6/25/				
Thompson Pump & MFR	Newman Tractor	Earth Trades of Cent. FL	10/27/16	04/25/17
WBE Environment Earth Trades of Cent. FL EAST COAST APPLICATORS The Douglas Company 05/07/17 06/25/17 FABRICATED PRODUCTS The Douglas Company 11/18/17 04/25/17 FRS CONSTRUCTION The Douglas Company 04/14/17 06/25/17 Gator Gypsum FRS Construction 04/26/17 06/25/17 JN ELECTRIC The Douglas Company 01/09/17 06/25/17 JN Electric Supply Inc JN Electric 03/15/17 06/25/17 City Electric Supply Inc JN Electric 02/24/17 06/25/17 Citical System Solutions Ilc JN Electric 02/24/17 06/25/17 Electric Supply Inc JN Electric 11/22/16 06/25/17 Mayer Electric Supply JN Electric 12/30/16 06/25/17 World Electric Supply Inc JN Electric 12/30/16 06/25/17 World Electric Supply Inc JN Electric 10/27/17 06/25/17 Werld Electric Supply Inc JN Electric 11/23/16 06/25/17 Werld Electric Supply Inc JN Electric 11/23/16 06/25/17 Werld Electric Supply Inc JN Electric 11/23/01/16 06/25/17 MEDIC AIR The Douglas Company 11/18/16 06/25/17 General Insulation Medic Air 11/18/17 06/25/17 Hughes Supply Medic Air 11/18/17 06/25/17 Sunbelt Rentals Medic Air 05/16/17 06/25/17 NEFF Rentals Medic Air 01/17/17 06/25/17 MIDSTATE CAULKING The Douglas Company 04/25/17 MiDSTATE CAULKING The Douglas Company 11/15/16 06/25/17 Ferguson Fire Fab Space Coast Fire&Safe 02/22/17 06/25/17 Fire Broofing And Construct. 11/15/16 03/25/17 The Douglas Company 11/15/16 03/25/17 The ROOFING AND CONSTR. The Douglas Company 11/15/16 03/25/17 The Roofing & Construct. 11/19/16 FINAL HD Supply Construction The Roofing & Construct. 12/20/16 02/25/17 The Roofing & Construct. 12/20/16 02/25/17 Preferred Materials Inc. The Roofing & Construct. 12/20/16 02/25/17 Preferred Materials Inc. The Roofing & Construct. 12/20/16 02/25/17	Synergy Rentals	Earth Trades of Cent. FL		04/25/17
EAST COAST APPLICATORS The Douglas Company 05/07/17 06/25/17 FABRICATED PRODUCTS The Douglas Company 11/18/17 04/25/17 FRS CONSTRUCTION The Douglas Company 04/14/17 06/25/17 Gator Gypsum FRS Construction 04/26/17 05/25/17 JN ELECTRIC The Douglas Company 01/09/17 06/25/17 Advance Cable Comm JN Electric 03/15/17 06/25/17 City Electric Supply Inc JN Electric 01/18/17 06/25/17 Critical System Solutions Ilc JN Electric 02/24/17 06/25/17 Critical System Solutions Ilc JN Electric 01/18/17 06/25/17 Mayer Electric Supply Inc JN Electric 11/22/16 06/25/17 World Electric Supply Inc JN Electric 12/30/16 06/25/17 World Electric Supply Inc JN Electric 01/27/17 06/25/17 MEDIC AIR The Douglas Company 11/18/16 06/25/17 Ferguson Enterprises Medic Air 05/16/17 06/25/17 Hughes Supply Medic Air <td>Thompson Pump & MFR</td> <td>Earth Trades of Cent. FL</td> <td>11/04/16</td> <td>FINAL</td>	Thompson Pump & MFR	Earth Trades of Cent. FL	11/04/16	FINAL
FABRICATED PRODUCTS The Douglas Company 11/18/17 04/25/17 FRS CONSTRUCTION The Douglas Company 04/14/17 06/25/17 Gator Gypsum FRS Construction 04/26/17 05/25/17 JN ELECTRIC The Douglas Company 01/09/17 06/25/17 Advance Cable Comm JN Electric 03/15/17 06/25/17 City Electric Supply Inc JN Electric 01/18/17 06/25/17 Critical System Solutions Ilc JN Electric 02/24/17 06/25/17 Critical System Solutions Ilc JN Electric 02/24/17 06/25/17 Mayer Electric Supply Inc JN Electric 11/22/16 06/25/17 Mayer Electric Supply Inc JN Electric 12/30/16 06/25/17 World Electric Supply Inc JN Electric 01/27/17 06/25/17 Medic Air 11/18/16 06/25/17 Ferguson Enterprises Medic Air 05/16/17 06/25/17 General Insulation Medic Air 05/16/17 06/25/17 Hughes Supply Medic Air 01/17/17 06/25/17 <td>WBE Environment</td> <td>Earth Trades of Cent. FL</td> <td></td> <td>FINAL</td>	WBE Environment	Earth Trades of Cent. FL		FINAL
FRS CONSTRUCTION The Douglas Company 04/14/17 06/25/17 Gator Gypsum FRS Construction 04/26/17 05/25/17 JN ELECTRIC The Douglas Company 01/09/17 06/25/17 Advance Cable Comm JN Electric 03/15/17 06/25/17 City Electric Supply Inc JN Electric 01/18/17 06/25/17 Crifical System Solutions IIc JN Electric 02/24/17 06/25/17 Electric Supply Inc JN Electric 11/22/16 06/25/17 Mayer Electric Supply Inc JN Electric 12/12/16 06/25/17 Sunbelt Rentals JN Electric 11/23/16 06/25/17 World Electric Supply Inc JN Electric 01/27/17 06/25/17 World Electric Supply Inc JN Electric 01/27/17 06/25/17 MEDIC AIR The Douglas Company 11/18/16 06/25/17 Ferguson Enterprises Medic Air 05/16/17 06/25/17 General Insulation Medic Air 01/17/17 06/25/17 Hughes Supply Medic Air 01/17/17	EAST COAST APPLICATORS	The Douglas Company	05/07/17	06/25/17
Gator Gypsum FRS Construction 04/26/17 05/25/17 JN ELECTRIC The Douglas Company 01/09/17 06/25/17 Advance Cable Comm JN Electric 03/15/17 06/25/17 City Electric Supply Inc JN Electric 01/18/17 06/25/17 Critical System Solutions Ilc JN Electric 02/24/17 06/25/17 Electric Supply Inc JN Electric 11/22/16 06/25/17 Mayer Electric Supply Inc JN Electric 12/30/16 06/25/17 Sunbelt Rentals JN Electric 01/27/17 06/25/17 World Electric Supply Inc JN Electric 01/27/17 06/25/17 MEDIC AIR The Douglas Company 11/18/16 06/25/17 Ferguson Enterprises Medic Air 05/16/17 06/25/17 General Insulation Medic Air 05/16/17 06/25/17 Hughes Supply Medic Air 01/17/17 06/25/17 Sunbelt Rentals Medic Air 01/17/17 06/25/17 MIDSTATE CAULKING The Douglas Company 04/25/17	FABRICATED PRODUCTS	The Douglas Company	11/18/17	04/25/17
The Douglas Company	FRS CONSTRUCTION	The Douglas Company	04/14/17	06/25/17
Advance Cable Comm JN Electric 03/15/17 06/25/17 City Electric Supply Inc JN Electric 01/18/17 06/25/17 Critical System Solutions Ilc JN Electric 02/24/17 06/25/17 Electric Supply Inc JN Electric 11/22/16 06/25/17 Mayer Electric Supply Inc JN Electric 12/30/16 06/25/17 Sunbelt Rentals JN Electric 11/27/17 06/25/17 World Electric Supply Inc JN Electric 01/27/17 06/25/17 World Electric Supply Inc JN Electric 01/27/17 06/25/17 MEDIC AIR The Douglas Company 11/18/16 06/25/17 Ferguson Enterprises Medic Air 11/21/16 06/25/17 General Insulation Medic Air 05/16/17 06/25/17 Hughes Supply Medic Air 01/17/17 06/25/17 Sunbelt Rentals Medic Air 01/17/17 06/25/17 NEFF Rentals Medic Air 01/17/17 06/25/17 MIDSTATE CAULKING The Douglas Company 04/25/17	Gator Gypsum	FRS Construction	04/26/17	05/25/17
City Electric Supply Inc Cifical System Solutions IIc Cifical System Solutions IIc Electric Supply Inc JN Electric JN Electric 11/22/16 06/25/17 Electric Supply Inc JN Electric JN Electric 11/22/16 06/25/17 Mayer Electric Supply JN Electric 12/30/16 06/25/17 Sunbelt Rentals JN Electric 12/30/16 06/25/17 World Electric Supply Inc JN Electric 01/27/17 06/25/17 MEDIC AIR The Douglas Company 11/18/16 06/25/17 Ferguson Enterprises Medic Air Hughes Supply Medic Air Medic Air NEFF Rentals Medic Air NEFF Rentals Medic Air NEFF Rentals Medic Air NEFF Rentals Medic Air 01/17/17 06/25/17 MIDSTATE CAULKING The Douglas Company Coastal Construction Prod. Mid State Caulking 12/20/16 FINAL ROOF RENOVATION FL. SPACE COAST FIRE & SAFE. The Douglas Company 11/15/16 06/25/17 Ferguson Fire Fab Space Coast Fire&Safe 02/22/17 06/25/17 BROOFING AND CONSTR. The Douglas Company 11/15/16 03/25/17 TB ROOFING AND CONSTR. The Douglas Company 11/15/16 03/25/17 TB Roofing & Construct. 12/19/16 FINAL HD Supply Construction TB Roofing & Construct. 12/19/16 FINAL HD Supply Construction TB Roofing & Construct. 12/20/16 02/25/17 Preferred Materials TB Roofing & Construct. 12/20/16 06/30/17 Sunbelt Rentals TB Roofing & Construct. 12/20/16 06/30/17	JN ELECTRIC	The Douglas Company	01/09/17	06/25/17
Critical System Solutions IIc JN Electric 02/24/17 06/25/17 Electric Supply Inc JN Electric 11/22/16 06/25/17 Mayer Electric Supply JN Electric 12/10/16 06/25/17 Sunbelt Rentals JN Electric 12/30/16 06/25/17 World Electric Supply Inc JN Electric 01/27/17 06/25/17 MEDIC AIR The Douglas Company 11/18/16 06/25/17 Ferguson Enterprises Medic Air 11/21/16 06/25/17 General Insulation Medic Air 05/16/17 06/25/17 Hughes Supply Medic Air 11/18/17 06/25/17 Sunbelt Rentals Medic Air 01/17/17 06/25/17 NEFF Rentals Medic Air 01/17/17 06/25/17 NEFF Rentals Medic Air 02/15/17 06/25/17 MIDSTATE CAULKING The Douglas Company 04/25/17 Coastal Construction Prod. Mid State Caulking 12/20/16 FINAL ROOF RENOVATION FL. The Douglas Company 03/09/17 06/25/17 SPACE COAST FIRE & SAFE. The Douglas Company 11/15/16 06/25/17 Ferguson Fire Fab Space Coast Fire&Safe 02/22/17 06/25/17 Reliable Sprinkler Space Coast Fire&Safe 02/17/17 06/25/17 TB ROOFING AND CONSTR. The Douglas Company 11/15/16 03/25/17 TB ROOFING AND CONSTR. The Douglas Company 11/15/16 03/25/17 Cast-Crete USA TB Roofing & Construct. 01/17/17 02/25/17 Cemex TB Roofing & Construct. 12/19/16 FINAL HD Supply Construction TB Roofing & Construct. 12/19/16 FINAL HD Supply Construction TB Roofing & Construct. 12/20/16 02/25/17 Preferred Materials TB Roofing & Construct. 12/30/16 06/30/17 Sunbelt Rentals TB Roofing & Construct. 12/30/16 06/30/17	Advance Cable Comm	JN Electric	03/15/17	06/25/17
Electric Supply Inc Mayer Electric Supply JN Electric Mayer Electric Supply JN Electric JN	City Electric Supply Inc	JN Electric	01/18/17	06/25/17
Mayer Electric Supply Sunbelt Rentals JN Electric 12/30/16 06/25/17 World Electric Supply Inc MEDIC AIR Ferguson Enterprises Medic Air Hughes Supply Medic Air Neff Rentals Medic Air Med	Critical System Solutions IIc	JN Electric	02/24/17	06/25/17
Sunbelt Rentals JN Electric 12/30/16 06/25/17 World Electric Supply Inc MEDIC AIR The Douglas Company 11/18/16 06/25/17 Ferguson Enterprises Medic Air Hughes Supply Medic Air Medic Air 11/21/16 06/25/17 Hughes Supply Medic Air 11/18/17 06/25/17 Sunbelt Rentals Medic Air NEFF Rentals Medic Air 01/17/17 06/25/17 NEFF Rentals Medic Air 01/17/17 06/25/17 NEFF Rentals Medic Air 02/15/17 06/25/17 MIDSTATE CAULKING The Douglas Company 04/25/17 Coastal Construction Prod. Mid State Caulking 12/20/16 FINAL ROOF RENOVATION FL. SPACE COAST FIRE & SAFE. The Douglas Company 11/15/16 06/25/17 Ferguson Fire Fab Space Coast Fire&Safe 02/22/17 06/25/17 Reliable Sprinkler Space Coast Fire&Safe 02/17/17 06/25/17 TB ROOFING AND CONSTR. The Douglas Company 11/15/16 03/25/17 TB Roofing & Construct. 11/18/17 02/25/17 TB Roofing & Construct. 11/18/17 11/18/18 11/18/18 11/18/18 11/18/18 11/18/18 11/18/18 11/18/18 11/18/18 11/18/18 11/18	Electric Supply Inc	JN Electric	11/22/16	06/25/17
World Electric Supply IncJN Electric01/27/1706/25/17MEDIC AIRThe Douglas Company11/18/1606/25/17Ferguson EnterprisesMedic Air11/21/1606/25/17General InsulationMedic Air05/16/1706/25/17Hughes SupplyMedic Air11/18/1706/25/17Sunbelt RentalsMedic Air01/17/1706/25/17NEFF RentalsMedic Air02/15/1706/25/17MIDSTATE CAULKINGThe Douglas Company04/25/17Coastal Construction Prod.Mid State Caulking12/20/16FINALROOF RENOVATION FL.The Douglas Company03/09/1706/25/17SPACE COAST FIRE & SAFE.The Douglas Company11/15/1606/25/17Ferguson Fire FabSpace Coast Fire&Safe02/22/1706/25/17High Reach 2Space Coast Fire&Safe06/08/1706/25/17Reliable SprinklerSpace Coast Fire&Safe02/17/1706/25/17TB ROOFING AND CONSTR.The Douglas Company11/15/1603/25/17Cast-Crete USATB Roofing & Construct.01/17/1702/25/17CemexTB Roofing & Construct.12/19/16FINALHD Supply ConstructionTB Roofing & Construct.12/20/1602/25/17Preferred Materials Inc.TB Roofing & Construct.12/20/1602/25/17Sunbelt RentalsTB Roofing & Construct.01/06/1702/25/17	Mayer Electric Supply	JN Electric	12/12/16	06/25/17
MEDIC AIRThe Douglas Company11/18/1606/25/17Ferguson EnterprisesMedic Air11/21/1606/25/17General InsulationMedic Air05/16/1706/25/17Hughes SupplyMedic Air11/18/1706/25/17Sunbelt RentalsMedic Air01/17/1706/25/17NEFF RentalsMedic Air02/15/1706/25/17MIDSTATE CAULKINGThe Douglas Company04/25/17Coastal Construction Prod.Mid State Caulking12/20/16FINALROOF RENOVATION FL.The Douglas Company03/09/1706/25/17SPACE COAST FIRE & SAFE.The Douglas Company11/15/1606/25/17Ferguson Fire FabSpace Coast Fire&Safe02/22/1706/25/17High Reach 2Space Coast Fire&Safe06/08/1706/25/17Reliable SprinklerSpace Coast Fire&Safe02/17/1706/25/17TB ROOFING AND CONSTR.The Douglas Company11/15/1603/25/17Cast-Crete USATB Roofing & Construct.01/17/1702/25/17CemexTB Roofing & Construct.12/19/16FINALHD Supply ConstructionTB Roofing & Construct.12/20/1602/25/17Preferred Materials Inc.TB Roofing & Construct.12/30/1606/30/17Sunbelt RentalsTB Roofing & Construct.01/06/1702/25/17	Sunbelt Rentals	JN Electric	12/30/16	06/25/17
Ferguson Enterprises Medic Air 11/21/16 06/25/17 General Insulation Medic Air 05/16/17 06/25/17 Hughes Supply Medic Air 11/18/17 06/25/17 Sunbelt Rentals Medic Air 01/17/17 06/25/17 NEFF Rentals Medic Air 02/15/17 06/25/17 MIDSTATE CAULKING The Douglas Company 04/25/17 Coastal Construction Prod. Mid State Caulking 12/20/16 FINAL ROOF RENOVATION FL. The Douglas Company 03/09/17 06/25/17 SPACE COAST FIRE & SAFE. The Douglas Company 11/15/16 06/25/17 Ferguson Fire Fab Space Coast Fire&Safe 02/22/17 06/25/17 High Reach 2 Space Coast Fire&Safe 06/08/17 06/25/17 Reliable Sprinkler Space Coast Fire&Safe 02/17/17 06/25/17 TB ROOFING AND CONSTR. The Douglas Company 11/15/16 03/25/17 Cast-Crete USA TB Roofing & Construct. 01/17/17 02/25/17 Cemex TB Roofing & Construct. 12/19/16 FINAL HD Supply Construction TB Roofing & Construct. 12/20/16 02/25/17 Preferred Materials Inc. TB Roofing & Construct. 12/30/16 06/30/17 Sunbelt Rentals TB Roofing & Construct. 01/06/17 02/25/17	World Electric Supply Inc	JN Electric	01/27/17	06/25/17
General Insulation Medic Air 05/16/17 06/25/17 Hughes Supply Medic Air 11/18/17 06/25/17 Sunbelt Rentals Medic Air 01/17/17 06/25/17 NEFF Rentals Medic Air 02/15/17 06/25/17 MIDSTATE CAULKING The Douglas Company 04/25/17 Coastal Construction Prod. Mid State Caulking 12/20/16 FINAL ROOF RENOVATION FL. The Douglas Company 03/09/17 06/25/17 SPACE COAST FIRE & SAFE. The Douglas Company 11/15/16 06/25/17 Ferguson Fire Fab Space Coast Fire&Safe 02/22/17 06/25/17 High Reach 2 Space Coast Fire&Safe 06/08/17 06/25/17 Reliable Sprinkler Space Coast Fire&Safe 02/17/17 06/25/17 The Douglas Company 11/15/16 03/25/17 The Douglas Company 11/15/16 03/25/17 Cast-Crete USA TB Roofing & Construct. 01/17/17 02/25/17 Cemex TB Roofing & Construct. 12/19/16 FINAL HD Supply Construction TB Roofing & Construct. 12/05/16 02/25/17 Preferred Materials Inc. TB Roofing & Construct. 12/20/16 02/25/17 Preferred Materials Inc. TB Roofing & Construct. 12/30/16 06/30/17 Sunbelt Rentals TB Roofing & Construct. 01/06/17 02/25/17	MEDIC AIR	The Douglas Company	11/18/16	06/25/17
Hughes Supply Medic Air Sunbelt Rentals Medic Air Medic Air 01/17/17 06/25/17 NEFF Rentals Medic Air 02/15/17 06/25/17 MIDSTATE CAULKING The Douglas Company 04/25/17 Coastal Construction Prod. Mid State Caulking 12/20/16 FINAL ROOF RENOVATION FL. The Douglas Company 03/09/17 06/25/17 SPACE COAST FIRE & SAFE. The Douglas Company 11/15/16 06/25/17 Ferguson Fire Fab Space Coast Fire&Safe 02/22/17 06/25/17 High Reach 2 Space Coast Fire&Safe 06/08/17 Reliable Sprinkler Space Coast Fire&Safe 02/17/17 TB ROOFING AND CONSTR. The Douglas Company 11/15/16 03/25/17 TB Roofing & Construct. 01/17/17 02/25/17 Cemex TB Roofing & Construct. 12/19/16 FINAL HD Supply Construction TB Roofing & Construct. 12/05/16 02/25/17 Preferred Materials Inc. TB Roofing & Construct. 12/30/16 06/30/17 Sunbelt Rentals TB Roofing & Construct. 01/06/17 02/25/17	Ferguson Enterprises	Medic Air	11/21/16	06/25/17
Sunbelt Rentals Medic Air NEFF Rentals Medic Air NEFF Rentals Medic Air O2/15/17 O6/25/17 MIDSTATE CAULKING The Douglas Company O4/25/17 Coastal Construction Prod. Mid State Caulking ROOF RENOVATION FL. The Douglas Company O3/09/17 SPACE COAST FIRE & SAFE. The Douglas Company The Douglas Construct. The Touglas Company The Toug	General Insulation	Medic Air	05/16/17	06/25/17
MEFF Rentals Medic Air MIDSTATE CAULKING The Douglas Company Coastal Construction Prod. Mid State Caulking ROOF RENOVATION FL. The Douglas Company SPACE COAST FIRE & SAFE. The Douglas Company The Douglas Company 11/15/16 11/1	Hughes Supply	Medic Air	11/18/17	06/25/17
MIDSTATE CAULKINGThe Douglas Company04/25/17Coastal Construction Prod.Mid State Caulking12/20/16FINALROOF RENOVATION FL.The Douglas Company03/09/1706/25/17SPACE COAST FIRE & SAFE.The Douglas Company11/15/1606/25/17Ferguson Fire FabSpace Coast Fire&Safe02/22/1706/25/17High Reach 2Space Coast Fire&Safe06/08/1706/25/17Reliable SprinklerSpace Coast Fire&Safe02/17/1706/25/17TB ROOFING AND CONSTR.The Douglas Company11/15/1603/25/17Cast-Crete USATB Roofing & Construct.01/17/1702/25/17CemexTB Roofing & Construct.12/19/16FINALHD Supply ConstructionTB Roofing & Construct.12/05/1602/25/17Pioneer Concrete PumpTB Roofing & Construct.12/20/1602/25/17Preferred Materials Inc.TB Roofing & Construct.12/30/1606/30/17Sunbelt RentalsTB Roofing & Construct.01/06/1702/25/17	Sunbelt Rentals	Medic Air	01/17/17	06/25/17
Coastal Construction Prod. Mid State Caulking ROOF RENOVATION FL. The Douglas Company O3/09/17 O6/25/17 SPACE COAST FIRE & SAFE. The Douglas Company The Roofing & Construct. The Roofin	NEFF Rentals	Medic Air	02/15/17	06/25/17
ROOF RENOVATION FL.The Douglas Company03/09/1706/25/17SPACE COAST FIRE & SAFE.The Douglas Company11/15/1606/25/17Ferguson Fire FabSpace Coast Fire&Safe02/22/1706/25/17High Reach 2Space Coast Fire&Safe06/08/1706/25/17Reliable SprinklerSpace Coast Fire&Safe02/17/1706/25/17TB ROOFING AND CONSTR.The Douglas Company11/15/1603/25/17Cast-Crete USATB Roofing & Construct.01/17/1702/25/17CemexTB Roofing & Construct.12/19/16FINALHD Supply ConstructionTB Roofing & Construct.12/05/1602/25/17Pioneer Concrete PumpTB Roofing & Construct.12/20/1602/25/17Preferred Materials Inc.TB Roofing & Construct.12/30/1606/30/17Sunbelt RentalsTB Roofing & Construct.01/06/1702/25/17	MIDSTATE CAULKING	The Douglas Company		04/25/17
SPACE COAST FIRE & SAFE.The Douglas Company11/15/1606/25/17Ferguson Fire FabSpace Coast Fire&Safe02/22/1706/25/17High Reach 2Space Coast Fire&Safe06/08/1706/25/17Reliable SprinklerSpace Coast Fire&Safe02/17/1706/25/17TB ROOFING AND CONSTR.The Douglas Company11/15/1603/25/17Cast-Crete USATB Roofing & Construct.01/17/1702/25/17CemexTB Roofing & Construct.12/19/16FINALHD Supply ConstructionTB Roofing & Construct.12/05/1602/25/17Pioneer Concrete PumpTB Roofing & Construct.12/20/1602/25/17Preferred Materials Inc.TB Roofing & Construct.12/30/1606/30/17Sunbelt RentalsTB Roofing & Construct.01/06/1702/25/17	Coastal Construction Prod.	Mid State Caulking	12/20/16	FINAL
Ferguson Fire Fab Space Coast Fire&Safe 02/22/17 06/25/17 High Reach 2 Space Coast Fire&Safe 06/08/17 06/25/17 Reliable Sprinkler Space Coast Fire&Safe 02/17/17 06/25/17 TB ROOFING AND CONSTR. The Douglas Company 11/15/16 03/25/17 Cast-Crete USA TB Roofing & Construct. 12/19/16 FINAL HD Supply Construction TB Roofing & Construct. 12/05/16 02/25/17 Pioneer Concrete Pump TB Roofing & Construct. 12/20/16 02/25/17 Preferred Materials Inc. TB Roofing & Construct. 12/30/16 06/30/17 Sunbelt Rentals TB Roofing & Construct. 01/06/17 02/25/17	ROOF RENOVATION FL.	The Douglas Company	03/09/17	06/25/17
High Reach 2 Space Coast Fire&Safe 06/08/17 06/25/17 Reliable Sprinkler Space Coast Fire&Safe 02/17/17 06/25/17 TB ROOFING AND CONSTR. The Douglas Company 11/15/16 03/25/17 Cast-Crete USA TB Roofing & Construct. 01/17/17 02/25/17 Cemex TB Roofing & Construct. 12/19/16 FINAL HD Supply Construction TB Roofing & Construct. 12/05/16 02/25/17 Pioneer Concrete Pump TB Roofing & Construct. 12/20/16 02/25/17 Preferred Materials Inc. TB Roofing & Construct. 12/30/16 06/30/17 Sunbelt Rentals TB Roofing & Construct. 01/06/17 02/25/17	SPACE COAST FIRE & SAFE.	The Douglas Company	11/15/16	06/25/17
Reliable Sprinkler Space Coast Fire & Safe 02/17/17 06/25/17 TB ROOFING AND CONSTR. The Douglas Company 11/15/16 03/25/17 Cast-Crete USA TB Roofing & Construct. 01/17/17 02/25/17 TB Roofing & Construct. 12/19/16 FINAL HD Supply Construction TB Roofing & Construct. 12/05/16 02/25/17 Pioneer Concrete Pump TB Roofing & Construct. 12/20/16 02/25/17 Preferred Materials Inc. TB Roofing & Construct. 12/30/16 06/30/17 Sunbelt Rentals TB Roofing & Construct. 01/06/17 02/25/17	Ferguson Fire Fab	Space Coast Fire&Safe	02/22/17	06/25/17
TB ROOFING AND CONSTR.The Douglas Company11/15/1603/25/17Cast-Crete USATB Roofing & Construct.01/17/1702/25/17CemexTB Roofing & Construct.12/19/16FINALHD Supply ConstructionTB Roofing & Construct.12/05/1602/25/17Pioneer Concrete PumpTB Roofing & Construct.12/20/1602/25/17Preferred Materials Inc.TB Roofing & Construct.12/30/1606/30/17Sunbelt RentalsTB Roofing & Construct.01/06/1702/25/17	High Reach 2	Space Coast Fire&Safe	06/08/17	06/25/17
Cast-Crete USA TB Roofing & Construct. 12/19/16 TINAL HD Supply Construction TB Roofing & Construct. TB Roofing & Construct. 12/05/16 02/25/17 Pioneer Concrete Pump TB Roofing & Construct. TB Roofing & Construct. 12/20/16 02/25/17 Preferred Materials Inc. TB Roofing & Construct. 12/30/16 06/30/17 Sunbelt Rentals TB Roofing & Construct. 01/06/17 02/25/17	Reliable Sprinkler	Space Coast Fire&Safe	02/17/17	06/25/17
Cemex TB Roofing & Construct. 12/19/16 FINAL HD Supply Construction TB Roofing & Construct. 12/05/16 02/25/17 Pioneer Concrete Pump TB Roofing & Construct. 12/20/16 02/25/17 Preferred Materials Inc. TB Roofing & Construct. 12/30/16 06/30/17 Sunbelt Rentals TB Roofing & Construct. 01/06/17 02/25/17	TB ROOFING AND CONSTR.	The Douglas Company	11/15/16	03/25/17
HD Supply Construction TB Roofing & Construct. 12/05/16 02/25/17 Pioneer Concrete Pump TB Roofing & Construct. 12/20/16 02/25/17 Preferred Materials Inc. TB Roofing & Construct. 12/30/16 06/30/17 Sunbelt Rentals TB Roofing & Construct. 01/06/17 02/25/17	Cast-Crete USA	TB Roofing & Construct.	01/17/17	02/25/17
Pioneer Concrete Pump TB Roofing & Construct. 12/20/16 02/25/17 Preferred Materials Inc. TB Roofing & Construct. 12/30/16 06/30/17 Sunbelt Rentals TB Roofing & Construct. 01/06/17 02/25/17	Cemex	TB Roofing & Construct.	12/19/16	FINAL
Preferred Materials Inc. TB Roofing & Construct. 12/30/16 06/30/17 Sunbelt Rentals TB Roofing & Construct. 01/06/17 02/25/17	HD Supply Construction	TB Roofing & Construct.	12/05/16	02/25/17
Sunbelt Rentals TB Roofing & Construct. 01/06/17 02/25/17	Pioneer Concrete Pump	TB Roofing & Construct.	12/20/16	02/25/17
-	Preferred Materials Inc.	TB Roofing & Construct.	12/30/16	06/30/17
THYSSUNKRUPP ELEVATOR The Douglas Company 06/22/17 06/25/17	Sunbelt Rentals	TB Roofing & Construct.	01/06/17	02/25/17
	THYSSUNKRUPP ELEVATOR	The Douglas Company	06/22/17	06/25/17

TIBBETT'S LUMBER	The Douglas Company	02/15/17	
TORRES TOTAL FLOORING	The Douglas Company		
Dal Tile Distribution Inc	Torres Total Flooring	06/15/17	06/25/17

PARTIAL RELEASES RECEIVED (Attachment):

PARTIAL UNCONDITIONAL WAIVER OF LIEN PARTIAL CONDITIONAL WAIVER OF LIEN Owner: PSL Wiregrass Owner: PSL Wiregrass Contractor: The Douglas Company Contractor: The Douglas Company Project: Beach House at Wiregrass Project: Beach House at Wiregrass Contract Date: 9/9/2016 Contract Date: 9/9/2016 Contractor, The Douglas Company, hereby represents and acknowledges it has received payment in the amount of \$ 1,164,263.00 for Application #10 for work through 7731/2017 from the Owner as partial payment for labor material and services provided by Contractor in connection with the above referenced Project and Contract. Contractor hereby waives any and all rights that it may have to file a mechanic's lien to the extent of the sums received as stated hereinabove. Contractor, <u>The Douglas Company</u>, upon the receipt of \$1,164,263.00 for Application # 10_ related to work through <u>July 31, 2017</u> and <u>\$906,070.00</u> for Application #11 related to work through <u>August 31, 2017</u> for labor, material, and services provided by Contractor in connection with the above referenced Project and Contract, Contractor will waive any and all rights that it may have to file a mechanic's lien to the extent of the sums received. THE DOUGLAS COMPANY THE DOUGLAS COMPANY By: Kevin Green E.I. Title: Senior Project Manager By: Kevin Green Title: Senior Project Manager STATE OF FLORIDA COUNTY OF ORANGE STATE OF FLORIDA COUNTY OF ORANGE Swgrn to before me this day of day of Sworm to before me this 25 day of Lugust, 2017 James a Cossels Notary Migdatia Acetas My commission expires: MY COMMISSION # FF930225 EXPIRES October 22, 2019 My commission expires:

PARTIAL UNCONDITIONAL WAIVER OF LIEN

Owner: PSL Wiregrass

Contractor: The Douglas Company Project: Beach House at Wiregrass

Contract Date: 9/9/2016

Contractor, The Douglas Company, hereby represents and acknowledges it has received payment in the amount of \$\frac{906.070.00}{906.070.00}\$ for Application #11 for work through 8/31/2017 from the Owner as partial payment for labor material and services provided by Contractor in connection with the above referenced Project and Contract. Contractor hereby waives any and all rights that it may have to file a mechanic's lien to the extent of the sums received as stated hereinabove.

THE DOUGLAS COMPANY

By: Kevin Green E.I.
Title: Senior Project Manager

STATE OF FLORIDA COUNTY OF ORANGE

Sworn to before me this 12 day of Septem 20 17

Notary Laureen A. Josselyn My commission expires:

LAUREEN A JOSSEL YN
MY COMMISSION & F P930225
EXPIRES October 22, 2019

FINAL RELEASES RECEIVED (Attachment):

WAIVER AND RELEASE OF LIEN UPON FINAL PAYMENT

The undersigned lienor, in consideration of the final amount of \$10 hereby walves and releases its lien and right to claim a ten for lobor, services, or materials furnished to ASSOCIATED CONSTRUCTION PROQ-1011055159 on the job of PSL WIREGRASS L/P to the following described property:

NTO: 9441-2315 in PASCO COUNTY, FLORIDA Recorded: 10/13/2016 Street: 30070 SR 56, WESLEY CHAPEL Lot: 1 Subdiv: WIREGRASS PCL M24 PB 73 PG 84

DATED on February 08, 2017

OLDCASTLE APC SOUTH, INC.

By:

Perhod Banke: Mart Motthews
Ties: Wed + Wenaye

Sworn to and subscribed before me on February 08, 2017, who is personally known to me



NOTE: This electricy form is preceded by Section 713.20, FLORICA STATUTES, and a fenor is not required to turrief a waiver or release of less that is officered from this electricy form.

THOMPSON PUMP
POST OFFICE BOX 291370
PORT ORANGE FL USA 32129-1370
800/767-7310 fax: 386/ 761-0362
www.thompsonpump.com



FULL AND FINAL RELEASE

The undersigned lienor, in consideration of the final payment in the amount of Ten and 00/100 Dollars (\$10.00), hereby waives and releases its lien and right to claim a lien for labor, services or materials furnished to A Plus Sock Installation Specialists LLC on the job of PSL Wiregrass LP, to the following described property:

Earth Trados / Beach House 30070 State Road 56 Approx. 95,000 SF 2 Story Assisted Living Facility Wesley Chapel, Florida

Dated on 21 February 2017.

THOMPSON PUMP & MFG. CO., INC.

Shawn Mackey, VP Finance

STATE OF FLORIDA COUNTY OF VOLUSIA

The foregoing instrument was sworn to and subscribed before me this 21st day of February 2017 by Shawn Mackey, VP Finance of Thompson Pump & Manufacturing Co., Inc., a Florida corporation. She is personally known to me and did take an oath.



Oldy Woodby Notary Public, State of Florida

This is a statutory form prescribed by Section 713.20, Florida Statutes (1996). Effective October 1, a person may not require a lienor to furnish a waiver or release of lien that a different from the statutory

FINAL WAIVER AND RELEASE

In consideration of psymems made and for other good and valuable consideration, the receipt and sufficiency of which is hereby acknowledged, the undersigned does hereby weive, release and retinquish any and all rights, claims, demands, liers, claims for relief, causes of action and the like, whether arising at law, under a contract, in tort, in equity, or otherwise, which the undersigned has now or may have arising out of the performance of work or the furnishing of labor or materials by the undersigned pursuant to a subcontract or purchase order with the subcontract or purchase order with the subcontract or purchase order with the laboration of the subcontract or purchase order with the subcontract or purchase or purchase order with the subcontract or purchase order with the subcontract or purchase or pu all those acting on their behalf.

This Waiver and Release applies to all facts, acts, events, circumstances, changes, constructive or actual, delays, accelerations, extra work, disruptions, interferences and the like which have occurred or may be claimed to have occurred prior to the effective date hereof. This Waiver and Release is intended to apply to and protect THE DOUGLAS COMPANYS payment and performance bond surety, if any, as well as anyone claiming by or through THE DOUGLAS COMPANY, the Owner, or the surety in connection with any claim, demend, lien, claim for relief, cause of action and the like waived, released and relinquished by the terms of this Agreemont.

This Weiver and Selease is freely and voluntarily given and the undersigned acknowledges, warrants and represents that it has fully reviewed the terms and conditions of this Waiver and Release, that it is fully informed with respect to the legal effect of this Waiver and Release and that it has voluntarily chosen to accept the terms and conditions of this Waiver and Release in return for the payment recited above.

The undersigned further represents that all employees, laborers, materialmen and subcontractors employed by the undersigned in connection with the Project and all bills for labor, materials, and supplies furnished by others to the undersigned in connection with construction of improvements upon the Project have been fully peal and that no obligations, legal, equitable or otherwise are owned by the undersigned in connection with its work on the Project. With respect to this representation and warranty, the undersigned does bereiby agree to indemnify and hold harmless THE DOUGLAS COMPANY, its payment and performance bond surely, if any, the Ower and any others claiming by or through them, from any and all claims, damages, losses, expenses and the like incurred by season of any claim that the undersigned has not fully paid for all labor, materials and expenses incurred in connection with its work on the Project.

The undersigned further agrees that making and receipt of payment and execution of this Waiver and Release shall in no way release the undersigned from its continuing, the obligations with respect to the completion of any work remaining undone, punch int work, warranty and guaranty work, and my other obligations of the undersigned on THE DOUGLAS.

COMPANY. Moreover, if the undersigned has furnished a bond in connection with the performance of its work, the sworty for the undersigned does beereby consent to and agree on the bound by the tenns and conditions of this Waiver and Release and does hereby agree to guarantee the performance of the undersigned with respect to each and every term and conditions of this Agreement and to continue in effect the obligations assumed with respect to the original subcontract or purchase order between the undersigned and

Earth Trades of Central Ft, inc. (vendor).

STATE OF FLORIDE

Subcontractor/Supplier,

COUNTY OF VEMINAL

Sworn to and subscribed before me this 21 day of Flavor, 2017.

A Plus SOCK Instructation specialist is.

Title Pranded

FINAL WAIVER AND LIEN RELEASE

In consciention of payments make, and for other good and valuable consideration, the receipt and authority of lad brady accordingly. On which the property of the payments of

The Wilson and Retease applies to all focts, and, noters, circumstances, changes, commissible or established, accelerations, ent's work, disruptions, sometimess and the late which have occurred; or may be delimed to leven occurred point the efficient deliments of the have of the same of the sa

The undersigned for their agrees that ensign an energy of anymora in description of the Visions and Release that his in an entire of the Visions and Release that his no a release the undersigned from its undersigned from the Undersigned fro

BL WITHESS WHEREOF, Individually and on Setuil of the underlighted, with full authority. Here executed this is effective the 2181 day of \underline{March} 2017.

STATE OF Florida

COLATY OF Voltasia

WHE Environmental, Inc. (Sa Flanda Sit Fencing

Sevent and substracted televier and the 21.8 day of an American Superior Sevent and Seve

March 2012

March 2014 Me His Sur Communico Espirite

Notary Public November 15, 2017

JENNEFER ANN MECKLEY MY COMMESION #7700087

TITLE: President

FINAL WAIVER AND LIEN RELEASE

on consideration of payments made, and for other good and valuable consideration, the receipt and sufficiency of which is hearing action-integral, the underligated does hereby value, release and velocipals and year of integral, cleans, convenue, bear the particular of internance the list substant particular particul

The continues of the significant properties of the continues of the contin

This Water and failures in freely and valuationly gives and the undersigned acknowledges, warrants and represents that it in fully exiltence the terms and conditions of this Water and failures, that it is fully inflammed with respect to the legal effect of this Water and Referes and that it has valuationly decises to accept the terms and conditions of this Water and Referes in resum for the general rectaind above.

The undersigned factor represents that all ensplayers, between, which is a materials, more and subcontractors amplished by the undersigned in connection with the Project and all this connects due for take, method, supplies, and states familiarly socials to the undersigned in connection with the Project and all this connects, and in the undersigned in the undersigned familiar that the undersign

The indeedgened livriter agrees that making and except of payment and execution of this Walver and Balease shall be not written as the understand from the continuence of the continuenc

IN WITHEST WITHEST A distribution and on behalf of the undersigned, with hill authority, I have executed this instrument effective the $\frac{1}{12}$ 4th of $\frac{1}{12}$ ACCC 25 2013.

STATE FORde

Mack Concrete Industries, Inc.

Sworn to and subscribed before me this 13th day of

Bug Kristy

March 2017 Pr. D. Arathula of March and Commission Explores 9/11/6/18

me Agent



CEMEX

CEMEX, Inc. and/or CEMEX Construction Materials Florida LLC WAIVER AND RELEASE OF RIGHT TO CLAIM AGAINST THE PAYMENT BOND (FINAL PAYMENT)

The undersigned, in consideration of the final payment in the amount of \$10,00 hereby waives and release; its right to claim against then payment bond for labor, services or materials furnished to TR ROD'ING CONSTRUCTION LLC, on the job of PSL WIREGRASS LP (owner), for improvements to the following described property:

LOT 1, WIREGRASS PARCEL M24, BEACH HOUSE AT WIREGRASS ASSISTED LOT 1, WIREGRASS PARCEL M24, BEACH HOUSE AT WIREGRASS ASSISTED LIVING AND MEMORY CARE, PS. WIREGRASS LP, BOND NUMBER 014667835, PARCEL NUMBERS 20-26-20-0000-00100-0010; 21-26-20; AND 20-26-20-0000-00000, AS PER PLAT BOOK 73 PAGES 48, 58, AND 68 AND BIRING MORE PARTICULARLY DESCRIBED IN NOTICE OF COMMENCEMENT RECORDED IN 08 BOOK 9441 PAGE 2315 PUBLIC RECORDS PASCO COUNTY, FLORIDA. NOC EXPIRES ON 0715/18.

DATED on APRIL 5, 2017

Claimart's Name. CEMEX. Inc audior CEMEX Continuction Materialy-Florida, LLC CREDIT SERVICES, 800-398/2869 3820 Northdide Blog # 10f6 Tumpa FL 3/624

By: MAXCINE LINJON Credit Services Representative

The foregoing instrument was signed in my presence this date of APRIL 5, 2017 by MAXCINE LINTON who is personally known to me, who did take an eath, and is Credit Services Representative of Claimant

Notary Public

WAIVER AND RELEASE OF LIEN UPON FINAL PAYMENT

The undersigned lienor, in consideration of the sum of \$ 10.00 . ("" Ten and 0 / 100 dollars "")
receipt is hereby acknowledged, waives and releases its iten end right to
claim a ilen or claim on the bond for labor, services or materials furnished to MIDSTATE CAULKING & CONSTRUCTION SERVICES LLC

on the job of PSL WIREGRASS LP

to the following described property:

BEACH HOUSE WIRE GRASS ASSISTED LIVING CENTER PASCO COUNTY

This is a Final Release of Lien by the undersigned for meteriels furnished to the company mentioned above only.



Dated on 05/05/2017 Coastal Construction Products

W Vessia Baid

State of Florida County of DUVAL

The foregoing instrument was acknowledged before me this 05 day of MAY , 2017 , by JESSICA BOYD as AGENT of Coestal Construction Products a Florida corporation. SHE is personally known to me.



Solic Curry Notary Public State of Florida

NOTE: This is a statutory form prescribed by Section 713.20, Florida Statutes (1995), effective October 1, 1996, a person may not require a flenor to furnish a walver or release of lien that is different from the statutory form.

MIDSTATE CAULKING & CONSTRUCTION SERVICES LLC 1600 KELLEY AVE KISSIMMEE, FL 34744

407-350-5968

WAIVER AND RELEASE OF LIEN UPON FINAL PAYMENT

T001840

The undersigned lienor, in consideration of the final payment in the amount of \$10.00 hereby waives and releases its lien and right to claim a lien for labor, services or materials, furnished to ASAP SHELL CONTRACTING on the job of PSL WIREGRASS LP (owner), to the following described property:

LOT 1 WIREGRASS PARCEL M24; APPROX 95,000 SQ FT, 2-STORY ASSISTED LIVING CENTER; 30070 SR 56, WESLEY CHAPPE, PER PROPERTY APPRAISER (1/15/2018) LOT 1 WIREGRASS PARCEL M24, PLAT BOOK 73 PAGES 84-86, PASCO COUNTY FL MORE PARTICULARLY DESCRIBED IN O.R. BOOK 9441 PAGE 2315;

DATED on JULY 12, 2017

CONTRACTORS ACCESS EQUIPMENT 8524 E ADAMO DR

TAMPA FL 33619

By ROBERT N. FOX JR.

Sworn to and subscribed before me this JULY 12, 2017

Signapure of Notary Public Commissioned State of Florida

Service State of Frame Services of August Services of August Services of August Services of August Services of 120218

Print, Type or Stamp Name of Notary Public

Personally Known XX OR, Produced

Type of Identification Produced

NOTE: This is a statutory form prescribed by Section 713.20, Florida Statutes 1996. Effective October 1, 1996, a person may not require a lienor to famish a waiver or release of lien that is different from the statutory form.

WAIVER AND RELEASE OF LIEN FINAL PAYMENT

The undersigned lience, is consideration of the finel payment in the sum of \$85,158.27 hereby walves and releases its lies and right to claim a lien for labor, services or materials furnished in BACH LOGISICS, INC on the pilot of \$5, WINEXCRAS 20.

30070 SR 56, WESLEY CHAPEL
BEACH HOUSE ASSISTED LIVING CENTER
BOOK: 9441 PAGE: 2315
PASCO COUNTY
TPC WORKSITE: 2460022823

DATED ON: May 2, 2017

Tampa Pavement Constructors, A Division of Hubbard Construction Co. 918 East Buach Boulevard Tampa, FL 33612

STATE OF FLORIDA COUNTY OF ORANGE

Sworn to and Subscribed before me this 2 al day of 1/AY , 2017 by Dark D. Story, Assistant

NOTE: This is a sixtuary form prescribed by Socilor 713-30, Floride Stateon (1996). Effect require a linear in Jambil a nuclin or reliant that is different from the statutory form. toe Cotober 1, 1996, is person may ac-

> Bay City Metals of Florida, Inc. 615 So Missouri Ave, #F Clearwater FL 33756-5963 Phone 727-441-2312 Fax 727-461-6189 baycitymetals@yahoo.com

WAIVER AND RELEASE OF LIEN **FINAL PAYMENT**

The undersigned lienor, in consideration of the final payment in the amount of \$11,800.00, hereby waives and releases its lien and right to claim a lien for labor, services or materials furnished to Fabricated Products of Tampa, Inc. to the following property:

> Beach House 30070 SR 56 Wesley Chapel FL

Dated on June 30, 2017

Lienor's Name: Address:

Bay City Metals of Florida, Inc.

615 So. Missouri Avenue, #F Clearwater, FL 33756-5963

Printed Name:

Lisar Smith Leslie Smith, Secretary


State of Florida

County of Pinellas

The foregoing instrument was acknowledged before me this 30th day of June, 2017 by Leslie Smith who is Secretary of Bay City Metals of Florida, Inc. She is personally known to me or has produced proper Identification in the form of a Florida driver's license.

8/24/20 My commission expires on


Notary Public: Printed Name:

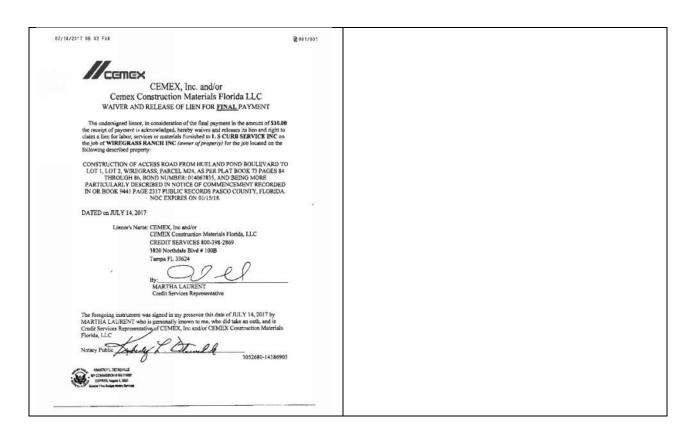

8 CHANGE ORDERS


Change Order #	Description	Order Date	Amount
OCO #01	Access Road (aka Sand Dune Road) Contractual Exclusion	12/09/16	\$270,224.00
OCO #02	Relocate low voltage conduits Reconcile roof drain system Irrigation Sleeves (Sand Dune Rd) Provide Tan painted elect panels in resid. T&M of offsite dewatering of M23CRD-2		\$2,465.99 \$(9,407.40) \$1,924.56 \$1,200.00 \$9,133.45 \$8,857.97
OCO #03	Omit Flag Pole and Base Urgent HVAC and Electrical pricing from construction set Constr. set generator changes Low Voltage Changes(constr. set) Provide High output Type Z light Night Lights/ LV in Revision #6 Omit Shower Curtains Change Metal brackets to foam Landscape and Irrigation VE (04/11/17) Omit MC Cue Boxes Change Unit Feeds to SER cable Omit door security conduits Use of Hardi prevail siding over specified		\$(5,133.11) \$65,593.17 \$0.00 \$23,478.00 \$0.00 \$4,937.66 \$(3,900.70) \$(9,153.09) \$(44,427.09) \$(5,453.87) \$(12532.89) \$(9,896.58) \$(3511.56) \$0.00

CHANGE ORDER #1

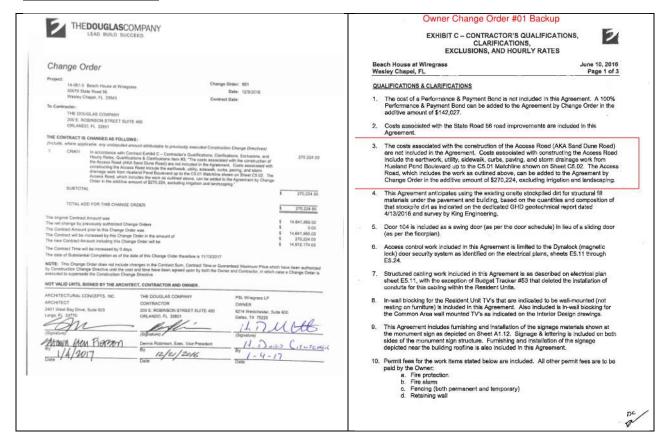


<u>OCO#1-</u> Per Exhibit C, exclusions, of the contract between owner and contractor, a change order for \$272,373.60 was required to complete the access road to the site which is to be reimbursed by the land seller as indicated to the CM at closing by the owner and underwriter. This cost is being applied against the contingency which will be reimbursed by the seller. This change order was approved by the owner.

CHANGE ORDER #2

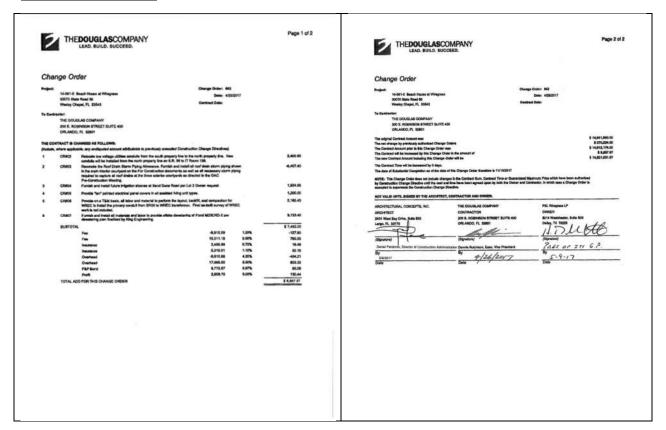

<u>OCO#2-</u> Costs associated with the completion of low voltage design, electrical transformer location, owner requested change in electrical panel color and cost saving measures to aid in project irrigation of Sand Dune Road. Additional costs owner under took to prevent the delay of the project based on dewatering of pond for storm water tie-in. Owner should be able to recoup dewatering costs. Savings obtained by reengineering the roof drainage in a more efficient manner.

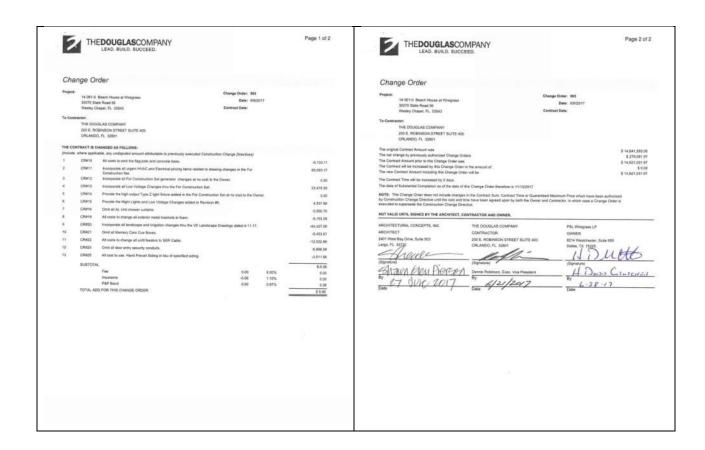

<u>OCO#3-</u> VE and additional costs zero out to \$0.00 Change Order. Major costs of HVAC, electrical and Low Voltage changes to the construction set were offset by VE savings found in landscape and irrigation as well as bracket material and change to SER as feeders.

Potential Change Order List (08/30/17)

The Design Build Team is still visiting VE which have/had the ability to offset many of the costs that have been proposed and implemented to date. The CM will continue to monitor the add costs/VE to aid in the control of the project costs as revision set pricing is zeroed in on.

		4	Beach House at Wiregrass Potential Change Order List as of 8-29-17	at Wiregrass	2.30.17		
			Pendine	Pending			
	0.71		"Scope Changes"	Coordination	Pending	2	10 100
. 008	Constitute Business Board Board School State Constitutes	Rejected	Not in Contract	Changes	Proposed VE	Amended	Comment Contents Subplies Clause all Octo Material
- 2	Low Voltage Utility Conduit Change					5 2,765,71	Monk Completed, Need Surned OCR DCD 8002
m	Roof Drain Storm Piping Allawance Reconciliation		đo o	1888	S	~	Work Completed, Allowance Closed Need Signed OCR OCO #002
47	Additional Utility Stub-Duts at Access Road to Lot 2					5 2,165.98	Approval revised to sleeves only. Utilities not included, OCO 9002
10 40	Upgrade Resident Unit Bestrice Princis WINDS Britain Bestrick Commentation					П	Change to Tan Color OCO #002
0 0-	Alternate Pend Dewarering Method for Turbidity					5 10,279.15	Submitting Documentation to SWFWWD OCD #002
90	Furnish and least (199) Bake Cheterin Leakeste					П	
6	Access Control Changes System for (9) Intentions			=			
9	Oreit flag Pole and Concrete Foundation					5 (5,777.00)	DOO MOB3
11	in terms	20 44 40 40				73,822.34	
77	Ī	20777701				20000000	OLO Moto, ID. Accepted responsibility
2 2	For Constitution Set Low Variable Changes Hallow Durwald St. Count Libral 1	7.438.02				69,463.07	DOCUMENT THE Assessment Resources (No.
37		П				5 552 04	DICO BOOK
191	Ornit AL Unit Shower Curtains					(4.390.00)	000 0003
17	Omit All Exterior Decorative Brackets (\$44,700)						0.00
18		\$ (17,500.00)					* To be Adjusted with Final Quantity of Brackets Removed
19	Change All Experior Decorative Brackets to Foam (\$10,000)			200		\$ (10,301.25)	DICO #003
30	VE Landscaping and Imigation					(50,000.00)	DICC MOB3
22	Omit Memory Cue Boxes		.10 0	223			000 000
77	Change Feeders to SER Cable					(14,105,00)	000.003
2	Stingues auth County					5 (11,138.00)	000 8003
3 %		0 (7,436,43)				S (3 652 00)	notatire to Americal Unionice
36	For Constr. Set "Change Memory Care Unit Rooming from Carpet to LVT		200		100		Only tholuses (8) Units Changing to Vinyl Floering
22	Door and Door Hardware Changes Thru Reveiland ELIA?				31	5 6,626.34	Includes Temperary Doors at (8) Locations
2.8	RR 836 Added Drop Cellings to (7) 388 Units		3		200	5 8,691,42	Spooy Flooring VE to Help Off Set
2						5 1,524.98	
35	Provide (ut hear mines westering to (us) hear for protections Chair Concerned from Batherene Other Californ at Seas Tile	0000000					
2						S 10 380 60	higher IIV-R Lint Trace at Serident Laundin Warhers
33	Onit Memory care Day Claset Bi-Fold Boors Add Swing Doors with Stonesoom Lack						included in OCR #27.
34	Sevalor: 95,2,97 Maglodis and Door Nardware Controllers (Electrical Changes)		F 4			5 2,627,60	
35	Final Door Access Control Changes (Approximately, \$50,000).						
92	Use Alternative sparer Pleaning Praduct	Ī				5 5000,000	Locations and 6" Base To Remain as Schedule.
2 2	United string Shakkons and Froetin Sciences at Internet County and the Francisco At Intel Think Vande Microsot At County and					S 15.057.77	Annual set Covered for Condition the Common Area Bathroom Missons
3.0	Automatic Opening Described		2 4 032 65				
07	Pentir Cachery Column Bales Changes per RB #86					5 2,228.57	
177	Use Corol Standront ILO Specified (12% Savings)		Section 1			5 (6,840,00)	
7	Added Day Closet Hooks in (33) Memory Care Units with Shelving Credit		7.63			100	includes Oredit for Closet Shelving.
7	Deer Handware Dredit to Use Domina	5 (9.338.77)				3,500,000	
4.5			E			\$ 11,763,630	
46	Action Exhapst Fan Ductaion's per RM #113					5 869.91	
43	Reliab Paraper Wall Steel per Rev. 6 Sheet 2.51	100.000.000		5 1,841,22			
9 9	Christian Contract Charles Charles	0.0000000000000000000000000000000000000	5 13 339 58				
	Miss Tile to 1917 Granges Pulls						
	Chongo Plastic Shurbor as Power Form						
	Onei Tile Bookspioch at Activity Bros. Milliampasses, Colley, Theates, Wil Riley		ins i	Art			* 4" Beckephock to Motth Countertage Will Be Local
	Committee in the Committee of the Commit						The management and the second
	Channel Dans Manager Milesans Chann						Also address of the beautiful and decreated by The
	Activities Consentrate Destance						No. Calendaria and a second of the second of
	1						Aller reviews the condition dees not exist.
		П		14			
	Total	\$ (37,881,78)	\$ 17,379,66	\$ 1.841.22		\$ 278,807,72	

52 Total Coutstanding Change Req

PAY APPLICATIONS (AIA G702): #11 Dated 08/31/17

CONTINUATION SHEET (AIA G703):

PAYR	PAYMENT APPLICATION	NOI				Page 1
TO FROM	PSI, Wregrass LP 8214 Westchester, Suite 600 Datas, TX 75225 After, Scott Walker THE DOUGLAS COMPANY 200 E. ROBINSON, SUITE 400 ORLANDO, FLORIDA 32601 Beach House & Wingstass	8 -	PROJECT NAME AND LOCATION ARCHITECT:	14051. Beach House @ Wiegrass PSI, Wingprass LP 30070 State Road 56 Westey Chapel, FL, 13543 Architectural Concepts 2401 Wiss Bay CL, Suite 503 Largo, FL 33770	APPLICATION 8 PERIOD THRU: PROJECT 85: DATE OF CONTRACT:	11
CONT	CONTRACTOR'S SUMMARY OF WORK Application is made for payment as shown below.	RY OF WORK		Contractor's signature below is his assurance to Owner, concerning the payment herein applied for, that Work has been performed as required in the Contract Decuments, (2) all sums preveusly paid to Contract Contract have been used to pay Contractor's costs for labor, materials and other obligations under the Contract for Work previously paid for, and (3) Contractor is legally entitled to this payment.	assurance to Owner, concerning med as required in the Contract D act have been used to pay Contra intract for Work previously paid for	The payment herein applied for, occurrents, (2) all sums preveusly clores casts for labor, materials, and (3) Contractor is legally
1. CONT	1. CONTRACT AMOUNT 2. SUM OF ALL CHANGE ORDERS		\$14,641,950.00	197 By	SK	Date: 8/25/17
3. CURR 4. TOTA scolor	CURRENT CONTRACT AMOUNT TOTAL COMPLETED AND STORED Column 5 on Contractor Page)	(Line 1 +/- 2)	\$14,921,031.97	State of FLORIDA County of CRANGE	evin Green	
4 T T T T T T T T T T T T T T T T T T T	RETAINACE: (Columbs of Completed Work (Columbs O + E on Continuation Page) b. 10,00% of Material Storic (Column F on Continuation Page) Total Retainage (Line Sa + Sb or		\$5,123,457.00	Subscribed and swem to before me this 15 th day by Aug. Notary Public. Laureng A. Josseyn My Commission Engines. October 22, 20	Many Constant	LAUREEN A JOSSELYN NY COMMISSION # FF80225 ENPIRES CARBON 22, 2019 Application
S	Column Fon Continuation Page)		\$1,123,437.00	ARCHITECT'S CERTIFICATION	FICATION	
6. TOTA Frine 7. LESS	TOTAL COMPLETED AND STORED LESS RETAINAGE Fine 4 minus Line 5 Total) LESS PREVIOUS PAYMENT APPLICATIONS	CATIONS	\$10,110,942.97	1 1	essurance to Owner, concerning the Work represented by this Application, and the quality nexts, (3) this Application for Paym	is payment herein applied for, cation, (2) such Work has been of workmanship and makenish nent accurately states the amount
8. PAYN	PAYMENT DUE		\$985,070.00		lue therefor, and (4) Architect kno-	ws of no reason why payment
9. BALA	BALANCE TO COMPLETION (Line 3 minus Line 6)	54,810,089.00	اه	(if the cariford amount is different from the payment due, you should attach an explanation indial all the County has been asset to provide the provided amount of the provided to provide the provided amount of the provided to provide the provided amount of the provided amoun	from the payment due, you should	Jettach an explanation Initial ail
Sultimed Total of	SUMMARY OF CHANGE ORDERS Total changes approved in powdows months	ADDITIONS \$396,023 63	DEDUCTIONS (\$115,941.66)	<u>\$</u>		The hours
Total as	ins month	\$0.00		_	U. Service for herein is assignab	Nether this Application not playment applies for herein is assignable or neoclastic. Payment shall be
	TOTALS	\$200,023.63	(3115,941.00)	_	made only to Contractor, and is without prejudice to any rights of Owner or Contractor undeliffie Contract Documents or otherwise.	Juner or Contractor under the

CONTINUATION PAGE Page 2 of 10

001111101111011				
	PROJECT:	14061- Beach House @ Wiregrass	APPLICATION #:	11
		PSL Wiregrass LP	DATE OF APPLICATION:	08/25/2017
Payment Application containing Contractor's signature is attached.			PERIOD THRU:	08/31/2017
			PROJECT #s:	14-061-0

				-	F	-			
ΑΑ	В	С	D	E	· ·	G		н	
ITEM #	WORK DESCRIPTION	SCHEDULED AMOUNT	AMOUNT PREVIOUS PERIODS	AMOUNT THIS PERIOD	STORED MATERIALS (NOT IN D OR E)	TOTAL COMPLETED AND STORED (D + E + F)	% COMP. (G / C)	BALANCE TO COMPLETION (C-G)	RETAINAGE (If Variable)
1	Survey/ Earthwork/ As Builts	\$224,349.00	\$213,132.00	\$0.00	\$0.00	\$213,132.00	95%	\$11,217.00	\$21,313.00
2	Sanitary Sewer	\$46,898.00	\$46,898.00	\$0.00	\$0.00	\$46,898.00	100%	\$0.00	\$4,690.00
3	Storm Sewer	\$157,324.00	\$157,324.00	\$0.00	\$0.00	\$157,324.00	100%	\$0.00	\$15,732.00
4	Downspout Tie In: ALLOWANCE	\$50,000.00	\$50,000.00	\$0.00	\$0.00	\$50,000.00	100%	\$0.00	\$5,000.00
5	Water Service	\$186,459.00	\$186,459.00	\$0.00	\$0.00	\$186,459.00	100%	\$0.00	\$18,646.00
6	Asphalt Paving	\$268,990.00	\$231,331.00	\$0.00	\$0.00	\$231,331.00	86%	\$37,659.00	\$23,133.00
7	SR 56 Offsite Paving	\$96,612.00	\$96,612.00	\$0.00	\$0.00	\$96,612.00	100%	\$0.00	\$9,661.00
8	Putting Green	\$5,226.00	\$0.00	\$0.00	\$0.00	\$0.00	0%	\$5,226.00	\$0.00
9	Shuffle Board: ALLOWANCE	\$7,000.00	\$0.00	\$0.00	\$0.00	\$0.00	0%	\$7,000.00	\$0.00
10	Flagpole	\$5,360.00	\$0.00	\$0.00	\$0.00	\$0.00	0%	\$5,360.00	\$0.00
11	Fountain: ALLOWANCE	\$5,000.00	\$0.00	\$0.00	\$0.00	\$0.00	0%	\$5,000.00	\$0.00
12	Landscaping	\$210,426.00	\$0.00	\$0.00	\$0.00	\$0.00	0%	\$210,426.00	\$0.00
13	Irrigation	\$42,600.00	\$1,278.00	\$0.00	\$0.00	\$1,278.00	3%	\$41,322.00	\$128.00
14	Site Concrete	\$63,205.00	\$6,321.00	\$0.00	\$0.00	\$6,321.00	10%	\$56,884.00	\$632.00
15	Dumpster Enclosure	\$16,250.00	\$13,325.00	\$0.00	\$0.00	\$13,325.00	82%	\$2,925.00	\$1,333.00
16	Brick Pavers	\$19,668.00	\$0.00	\$0.00	\$0.00	\$0.00	0%	\$19,668.00	\$0.00
	SUB-TOTALS	\$1,405,367.00	\$1,002,680.00	\$0.00	\$0.00	\$1,002,680.00	71%	\$402,687.00	\$100,268.00

CONTINUATION PAGE Quantum Software Solutions, Inc. Document

CONTINUATION PAGE Page 3 of 10

CONTINUATION FAGE			-	
	PROJECT:	14061- Beach House @ Wiregrass	APPLICATION #:	11
		PSL Wiregrass LP	DATE OF APPLICATION:	08/25/2017
Payment Application containing Contractor's signature is attached.			PERIOD THRU:	08/31/2017
			PROJECT #s:	14-061-0

							PROJ	ECT#s:	14-061-0
Α	В	С	D	E	F	G		Н	1
ITEM#	WORK DESCRIPTION	SCHEDULED AMOUNT	AMOUNT PREVIOUS PERIODS	AMOUNT THIS PERIOD	STORED MATERIALS (NOT IN D OR E)	TOTAL COMPLETED AND STORED (D + E + F)	% COMP. (G / C)	BALANCE TO COMPLETION (C-G)	RETAINAGE (If Variable)
17	Retaining Wall	\$27,302.00	\$27,302.00	\$0.00	\$0.00	\$27,302.00	100%	\$0.00	\$2,730.00
18	Misc. Site Metals	\$3,192.00	\$3,192.00	\$0.00	\$0.00	\$3,192.00	100%	\$0.00	\$319.00
19	Fencing & Dumpster Gates	\$26,344.00	\$0.00	\$0.00	\$0.00	\$0.00	0%	\$26,344.00	\$0.00
20	Monument & Building Signage	\$11,305.00	\$0.00	\$0.00	\$0.00	\$0.00	0%	\$11,305.00	\$0.00
21	Site Electrical	\$36,197.00	\$3,620.00	\$0.00	\$0.00	\$3,620.00	10%	\$32,577.00	\$362.00
22	Soil Poisoning	\$4,231.00	\$4,231.00	\$0.00	\$0.00	\$4,231.00	100%	\$0.00	\$423.00
23	Building Concrete	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00		\$0.00	\$0.00
25	Submittals/ Mobilization	\$4,500.00	\$4,500.00	\$0.00	\$0.00	\$4,500.00	100%	\$0.00	\$450.00
26	Foundations	\$249,320.00	\$249,320.00	\$0.00	\$0.00	\$249,320.00	100%	\$0.00	\$24,932.00
27	Slab on Grade	\$312,547.00	\$312,547.00	\$0.00	\$0.00	\$312,547.00	100%	\$0.00	\$31,255.00
28	Columns and Beams	\$103,585.00	\$103,585.00	\$0.00	\$0.00	\$103,585.00	100%	\$0.00	\$10,359.00
29	2nd Floor Topping	\$125,657.00	\$125,657.00	\$0.00	\$0.00	\$125,657.00	100%	\$0.00	\$12,566.00
30	2nd Floor C & B	\$12,515.00	\$12,515.00	\$0.00	\$0.00	\$12,515.00	100%	\$0.00	\$1,252.00
31	Precast Concrete	\$321,190.00	\$321,190.00	\$0.00	\$0.00	\$321,190.00	100%	\$0.00	\$32,119.00
32	Building Masonry	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00		\$0.00	\$0.00
33	1st Floor	\$325,750.00	\$325,750.00	\$0.00	\$0.00	\$325,750.00	100%	\$0.00	\$32,575.00
	SUB-TOTALS	\$2,969,002.00	\$2,496,089.00	\$0.00	\$0.00	\$2,496,089.00	84%	\$472,913.00	\$249,610.00

CONTINUATION PAGE Page 4 of 10

PROJECT: 14061- Beach House @ Wiregrass APPLICATION #: 11
PSL Wiregrass LP DATE OF APPLICATION: 08/25/2017
Payment Application containing Contractor's signature is attached. PERIOD THRU: 08/31/2017
PROJECT #s: 14-061-0

A	В	С	D	E	F	G		Н	1
ITEM#	WORK DESCRIPTION	SCHEDULED AMOUNT	AMOUNT PREVIOUS PERIODS	ED WORK AMOUNT THIS PERIOD	STORED MATERIALS (NOT IN D OR E)	TOTAL COMPLETED AND STORED (D + E + F)	% COMP. (G / C)	BALANCE TO COMPLETION (C-G)	RETAINAGE (If Variable)
34	2nd Floor	\$130,500.00	\$130,500.00	\$0.00	\$0.00	\$130,500.00	100%	\$0.00	\$13,050.00
35	Stone Veneer	\$129,000.00	\$116,100.00	\$6,450.00	\$0.00	\$122,550.00	95%	\$6,450.00	\$12,255.00
36	Structural Steel	\$30,535.00	\$30,535.00	\$0.00	\$0.00	\$30,535.00	100%	\$0.00	\$3,054.00
37	Galvanized Ladders	\$6,250.00	\$6,250.00	\$0.00	\$0.00	\$6,250.00	100%	\$0.00	\$625.00
38	Steel Stairs & Railings	\$33,100.00	\$33,100.00	\$0.00	\$0.00	\$33,100.00	100%	\$0.00	\$3,310.00
39	Aluminum Railings	\$14,475.00	\$0.00	\$0.00	\$0.00	\$0.00	0%	\$14,475.00	\$0.00
40	Rough Carpentry	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00		\$0.00	\$0.00
41	Submittals/Mobilization	\$7,500.00	\$7,500.00	\$0.00	\$0.00	\$7,500.00	100%	\$0.00	\$750.00
42	1st Floor Materials	\$60,200.00	\$60,200.00	\$0.00	\$0.00	\$60,200.00	100%	\$0.00	\$6,020.00
43	1st Floor Labor	\$62,800.00	\$62,800.00	\$0.00	\$0.00	\$62,800.00	100%	\$0.00	\$6,280.00
44	2nd Floor Materials	\$92,500.00	\$92,500.00	\$0.00	\$0.00	\$92,500.00	100%	\$0.00	\$9,250.00
45	2nd Floor Labor	\$94,000.00	\$94,000.00	\$0.00	\$0.00	\$94,000.00	100%	\$0.00	\$9,400.00
46	Roof Materials	\$142,000.00	\$142,000.00	\$0.00	\$0.00	\$142,000.00	100%	\$0.00	\$14,200.00
47	Roof Labor	\$167,000.00	\$167,000.00	\$0.00	\$0.00	\$167,000.00	100%	\$0.00	\$16,700.00
48	Truss Material	\$121,422.00	\$121,422.00	\$0.00	\$0.00	\$121,422.00	100%	\$0.00	\$12,142.00
49	Cabinets & Tops- Units	\$316,792.00	\$91,870.00	\$98,205.00	\$0.00	\$190,075.00	60%	\$126,717.00	\$19,008.00
	SUB-TOTALS	\$4,377,076.00	\$3,651,866.00	\$104,655.00	\$0.00	\$3,756,521.00	86%	\$620,555.00	\$375,654.00

CONTINUATION PAGE

Quantum Software Solutions, Inc. Document

CONTINUATION PAGE	Page 5 of 10

CONTINUATION FAGE			-0	
	PROJECT:	14051- Beach House @ Wiregrass	APPLICATION #:	11
		PSL Wiregrass LP	DATE OF APPLICATION:	08/25/2017
Payment Application containing Contractor's signature is attached.			PERIOD THRU:	08/31/2017
			PROJECT #s:	14-061-0

A	В	С	D	E	E	G		Н	
Α	8		COMPLET						
TEM #	WORK DESCRIPTION	SCHEDULED AMOUNT	AMOUNT PREVIOUS PERIODS	AMOUNT THIS PERIOD	STORED MATERIALS (NOT IN D OR E)	TOTAL COMPLETED AND STORED (D + E + F)	COMP. (G/C)	BALANCE TO COMPLETION (C-G)	RETAINAC (If Variable
50	Cabinets & Tops- Common	\$349,250.00	\$0.00	\$0.00	\$0.00	\$0.00	0%	\$349,250.00	\$0.
51	Interior Wood Trim	\$453,789.00	\$36,303.00	\$109,909.00	\$0.00	\$145,212.00	32%	\$308,577.00	\$14,521.
52	FRP & Accessories	\$11,996.00	\$0.00	\$0.00	\$0.00	\$0.00	0%	\$11,996.00	\$0.
53	Waterproofing	\$2,900.00	\$2,900.00	\$0.00	\$0.00	\$2,900.00	100%	\$0.00	\$290.
54	Insulation	\$79,205.00	\$64,948.00	\$6,337.00	\$0.00	\$71,285.00	90%	\$7,920.00	\$7,129.
55	Roofing	\$367,500.00	\$349,125.00	\$0.00	\$0.00	\$349,125.00	95%	\$18,375.00	\$34,913
56	Fiber Cement Siding	\$169,000.00	\$126,750.00	\$42,250.00	\$0.00	\$169,000.00	100%	\$0.00	\$16,900
57	Soffits and Fascia	\$42,000.00	\$21,000.00	\$20,160.00	\$0.00	\$41,160.00	98%	\$840.00	\$4,116
58	Gutters & Downspouts	\$17,569.00	\$0.00	\$4,392.00	\$0.00	\$4,392.00	25%	\$13,177.00	\$439
59	Fireproofing	\$5,400.00	\$5,400.00	\$0.00	\$0.00	\$5,400.00	100%	\$0.00	\$540
60	Caulking, Sealants, Traffic Coatings	\$29,900.00	\$11,960.00	\$2,990.00	\$0.00	\$14,950.00	50%	\$14,950.00	\$1,495
61	Concrete Moisture Barrier	\$35,259.00	\$0.00	\$0.00	\$0.00	\$0.00	0%	\$35,259.00	\$0.
62	Doors & Frames	\$186,742.00	\$65,360.00	\$9,337.00	\$0.00	\$74,697.00	40%	\$112,045.00	\$7,470
63	Finish Hardware	\$99,055.00	\$0.00	\$0.00	\$0.00	\$0.00	D%	\$99,055.00	\$0
64	Door & Hardware Install	\$98,500.00	\$11,820.00	\$12,805.00	\$0.00	\$24,625.00	25%	\$73,875.00	\$2,463
65	Windows	\$113,595.00	\$113,595.00	\$0.00	\$0.00	\$113,595.00	100%	\$0.00	\$11,360
	SUB-TOTALS	\$6,438,736.00	\$4,481,027.00	\$311,835.00	\$0.00	\$4,772,862.00	74%	\$1,665,874.00	\$477,290

CONTINUATION PAGE Page 6 of 10

PROJECT: 14061- Beach House @ Wiregrass APPLICATION #: 11
PSL Wiregrass LP DATE OF APPLICATION: 09/25/2017
Payment Application containing Contractor's signature is attached. PERIOD THRU: 08/31/2017
PROJECT #s: 14-061-0

A	В	С	D	E	F	G		Н	1
			COMPLET	ED WORK	STORED	TOTAL	%	BALANCE	
ITEM#	WORK DESCRIPTION	SCHEDULED AMOUNT	AMOUNT PREVIOUS PERIODS	AMOUNT THIS PERIOD	MATERIALS (NOT IN D OR E)	STORED (D + E + F)	COMP. (G / C)	COMPLETION (C-G)	RETAINAGE (If Variable)
66	Storefront	\$57,000.00	\$2,850.00	\$0.00	\$0.00	\$2,850.00	5%	\$54,150.00	\$285.00
67	Glass & Glazing	\$41,463.00	\$0.00	\$0.00	\$0.00	\$0.00	0%	\$41,463.00	\$0.00
68	Automatic Doors	\$13,637.00	\$682.00	\$0.00	\$0.00	\$682.00	5%	\$12,955.00	\$68.00
69	Mirrors	\$14,565.00	\$0.00	\$0.00	\$0.00	\$0.00	0%	\$14,565.00	\$0.00
70	Stucco	\$203,000.00	\$127,890.00	\$24,360.00	\$0.00	\$152,250.00	75%	\$50,750.00	\$15,225.00
71	Drywall, Metal Soffits	\$717,000.00	\$616,620.00	\$50,190.00	\$0.00	\$666,810.00	93%	\$50,190.00	\$66,681.00
72	Ceramic & Quarry Tile	\$267,873.00	\$107,149.00	\$64,290.00	\$0.00	\$171,439.00	64%	\$96,434.00	\$17,144.00
73	Acoustical Ceilings	\$66,000.00	\$0.00	\$7,920.00	\$0.00	\$7,920.00	12%	\$58,080.00	\$792.00
74	Carpeting & Vinyl Flooring	\$356,632.00	\$7,133.00	\$0.00	\$0.00	\$7,133.00	2%	\$349,499.00	\$713.00
75	Painting & Wallcoverings	\$238,049.00	\$57,132.00	\$45,229.00	\$0.00	\$102,361.00	43%	\$135,688.00	\$10,236.00
76	Epoxy/ Sealed Concrete	\$18,650.00	\$0.00	\$0.00	\$0.00	\$0.00	0%	\$18,650.00	\$0.00
77	Corner Guards	\$5,775.00	\$0.00	\$0.00	\$0.00	\$0.00	0%	\$5,775.00	\$0.00
78	Shower Curtains	\$9,072.00	\$0.00	\$0.00	\$0.00	\$0.00	0%	\$9,072.00	\$0.00
79	Fire Extinguishers	\$8,811.00	\$0.00	\$0.00	\$0.00	\$0.00	0%	\$8,811.00	\$0.00
80	Window Treatments	\$27,233.00	\$0.00	\$0.00	\$0.00	\$0.00	0%	\$27,233.00	\$0.00
81	Fireplaces	\$4,488.00	\$0.00	\$0.00	\$0.00	\$0.00	0%	\$4,488.00	\$0.00
	SUB-TOTALS	\$8,487,984.00	\$5,380,483.00	\$503,824.00	\$0.00	\$5,884,307.00	69%	\$2,603,677.00	\$588,434.00

CONTINUATION PAGE
Quantum Software Solutions, Inc. Document

CONTINUATION PAGE Page 7 of 10

 PROJECT:
 14061- Beach House @ Wiregrass
 APPLICATION #
 11

 Payment Application containing Contractor's signature is attached.
 PSL Wiregrass LP
 DATE OF APPLICATION | 08/25/2017

 Payment Application containing Contractor's signature is attached.
 PERIOD THRU: 08/31/2017

 PROJECT #s: 14-081-0
 14-081-0

A	В	С	D	E	F	G		н	
^	- "		COMPLET	4				<u>''</u>	, _
ITEM#	WORK DESCRIPTION	SCHEDULED AMOUNT	AMOUNT PREVIOUS PERIODS	AMOUNT THIS PERIOD	STORED MATERIALS (NOT IN D OR E)	TOTAL COMPLETED AND STORED (D + E + F)	% COMP. (G / C)	BALANCE TO COMPLETION (C-G)	RETAINAGE (If Variable)
82	Mailtoxes	\$5,670.00	\$0.00	\$0.00	\$0.00	\$0.00	0%	\$5,670.00	\$0.00
83	Lockers	\$3,420.00	\$0.00	\$0.00	\$0.00	\$0.00	0%	\$3,420.00	\$0.00
84	Vinyl Wire Shelving	\$12,392.00	\$0.00	\$0.00	\$0.00	\$0.00	0%	\$12,392.00	\$0.00
85	Bathroom Accessories & Specialties	\$71,046.00	\$0.00	\$42,628.00	\$0.00	\$42,628.00	60%	\$28,418.00	\$4,263.00
86	Access Panels	\$6,230.00	\$0.00	\$3,115.00	\$0.00	\$3,115.00	50%	\$3,115.00	\$312.00
87	Residential Appliances	\$55,339.00	\$0.00	\$0.00	\$0.00	\$0.00	0%	\$55,339.00	\$0.00
88	Comm. Kitchen Equip.	\$255,888.00	\$89,561.00	\$0.00	\$0.00	\$89,561.00	35%	\$166,327.00	\$8,956.00
89	Laundry Equipment	\$19,090.00	\$19,090.00	\$0.00	\$0.00	\$19,090.00	100%	\$0.00	\$1,909.00
90	Elevators	\$149,300.00	\$14,930.00	\$101,524.00	\$0.00	\$116,454.00	78%	\$32,846.00	\$11,645.00
91	HVAC	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00		\$0.00	\$0.00
92	Submittals/ Mobilization	\$28,105.00	\$28,105.00	\$0.00	\$0.00	\$28,105.00	100%	\$0.00	\$2,811.00
93	Equipment	\$510,035.00	\$484,533.00	\$15,301.00	\$0.00	\$499,834.00	98%	\$10,201.00	\$49,983.00
94	Layout/Coordination	\$14,900.00	\$14,900.00	\$0.00	\$0.00	\$14,900.00	100%	\$0.00	\$1,490.00
95	1st Floor Rough	\$204,877.00	\$192,584.00	\$2,049.00	\$0.00	\$194,633.00	95%	\$10,244.00	\$19,463.00
96	1st Floor Finish	\$21,478.00	\$3,222.00	\$644.00	\$0.00	\$3,866.00	18%	\$17,612.00	\$387.00
97	2nd Floor Rough	\$184,689.00	\$184,689.00	\$0.00	\$0.00	\$184,689.00	100%	\$0.00	\$18,459.00
	SUB-TOTALS	\$10,030,443.00	\$6,412,097.00	\$669,085.00	\$0.00	\$7,081,182.00	71%	\$2,949,261.00	\$708,122.00

CONTINUATION PAGE Page 8 of 10

CONTINUATION				
	PROJECT:	14061- Beach House @ Wiregrass	APPLICATION #:	11
		PSL Wiregrass LP	DATE OF APPLICATION:	08/25/2017
Payment Application containing Contractor's signature is attached			PERIOD THRU:	08/31/2017
			PROJECT #s:	14-061-0

A	8	С	D	E	F	G		Н	I
ITEM #	WORK DESCRIPTION	SCHEDULED AMOUNT	AMOUNT PREVIOUS	ED WORK AMOUNT THIS PERIOD	STORED MATERIALS (NOT IN D OR E)	TOTAL COMPLETED AND STORED (D + E + F)	% COMP. (G / C)	BALANCE TO COMPLETION (C-G)	RETAINAG (If Variable
98	2nd Floor Finish	\$18.483.00	PERIODS \$3.697.00	\$2,772.00	\$0.00	\$6.469.00	35%	, ,	\$647.0
99	Plumbing	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00		\$0.00	\$0.0
100	Submittals/ Mobilization	\$10,000.00	\$10,000.00	\$0.00	\$0.00	\$10,000.00	100%	\$0.00	\$1,000.0
101	Equipment/ Fixtures	\$230,743.00	\$71,530.00	\$89,990.00	\$0.00	\$161.520.00	70%	E \$69,223.00	\$16,152.0
102	Underground	\$202,968.00	\$202,968.00	\$0.00	\$0.00	\$202,968.00	100%		\$20,297.0
103	1st Floor 2nd Floor	\$336,795.00 \$181,349.00	\$336,795.00 \$181.349.00	\$0.00	\$0.00 \$0.00	\$336,795.00 \$181,349.00	100%		\$33,680.0
105	Fire Protection	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00	100%	\$0.00	\$0.0
106	Design/ Permitting	\$32,500.00	\$32,500.00	\$0.00	\$0.00	\$32,500.00	100%	\$0.00	\$3,250
107	Material	\$96,800.00	\$96,800.00	\$0.00	\$0.00	\$95,800.00	100%	\$0.00	\$9,680
108	Labor	\$110,000.00	\$93,500.00	\$5,500.00	\$0.00	\$99,000.00	90%	****	\$9,900
109	Electrical & Low Voltage Submittals/ Mobilization	\$0.00	\$35,000.00	\$0.00 \$0.00	\$0.00	\$0.00	100%	\$0.00	\$3,500
110	Sitework	\$85,000.00	\$25,500.00	\$0.00	\$0.00	\$25,500.00	30%		\$2,550
112	Generator	\$70,000.00	\$70,000.00	\$0.00	\$0.00	\$70,000.00	100%	\$0.00	\$7,000.
113	Underground	\$110,754.00	\$110,754.00	\$0.00	\$0.00	\$110,754.00	100%	\$0.00	\$11,075
	SUB-TOTALS	\$11,550,835.00	\$7,682,490.00	\$767,347.00	\$0.00	\$8,449,837.00	73%	\$3,100,998.00	\$844,988

CONTINUATION PAGE Quantum Seftware Solutions, Inc. Document

CONTINUATION PAGE Page 9 of 10

CONTINUATION PAGE			, ago o o,	
	PROJECT:	14061- Beach House @ Wiregrass	APPLICATION #:	11
		PSL Wiregrass LP	DATE OF APPLICATION:	08/25/2017
Payment Application containing Contractor's signature is attached.			PERIOD THRU:	08/31/2017
			PROJECT #s:	14-061-0

							PROJ	ECT#8:	14-061-0
A	В	С	D	E	F	G		н	I
ITEM #	WORK DESCRIPTION	SCHEDULED AMOUNT	AMOUNT PREVIOUS PERIODS	AMOUNT THIS PERIOD	STORED MATERIALS (NOT IN D OR E)	TOTAL COMPLETED AND STORED (D + E + F)	% COMP. (G / C)	BALANCE TO COMPLETION (C-G)	RETAINAGE (If Variable)
114	1st Floor Rough	\$340,065.00	\$323,062.00	\$3,400.00	\$0.00	\$326,462.00	96%	\$13,603.00	\$32,646.00
115	1st Floor Finish	\$221,253.00	\$66,376.00	\$22,125.00	\$0.00	\$88,501.00	40%	\$132,752.00	\$8,850.00
116	2nd Floor Slab	\$53,786.00	\$53,786.00	\$0.00	\$0.00	\$53,786.00	100%	\$0.00	\$5,379.00
117	2nd Floor Rough	\$323,874.00	\$323,874.00	\$0.00	\$0.00	\$323,874.00	100%	\$0.00	\$32,387.00
118	2nd Floor Finish	\$220,471.00	\$110,236.00	\$33,070.00	\$0.00	\$143,306.00	65%	\$77,165.00	\$14,331.00
119	General Conditions	\$1,156,284.00	\$879,567.00	\$79,062.00	\$0.00	\$958,629.00	83%	\$197,655.00	\$95,863.00
120	Overhead & Profit	\$775,382.00	\$531,524.00	\$52,106.00	\$0.00	\$583,630.00	75%	\$191,752.00	\$58,363.00
121	Change Order #01 Access Road	\$270,224.00	\$229,690.00	\$0.00	\$0.00	\$229,690.00	85%	\$40,534.00	\$22,969.00
122	Change Order #2	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00		\$0.00	\$0.00
123	Low Voltage Utility Conduit Change	\$2,765.71	\$2,765.71	\$0.00	\$0.00	\$2,765.71	100%	\$0.00	\$277.00
124	Roof Drain Storm Piping Allowance Reconcilliaton	(\$10,140.41)	(\$10,140.41)	\$0.00	\$0.00	(\$10,140.41)	100%	\$0.00	(\$1,014.00)
125	Additional Utility Stub-Outs at Access Road to Lot 2	\$2,165.98	\$2,165.98	\$0.00	\$0.00	\$2,165.98	100%	\$0.00	\$217.00
126	Upgrade Resident Unit Electrical Panels	\$1,350.52	\$1,350.52	\$0.00	\$0.00	\$1,350.52	100%	\$0.00	\$135.00
127	WREC Primary Backfill and Compaction	\$2,437.02	\$2,437.02	\$0.00	\$0.00	\$2,437.02	100%	\$0.00	\$244.00
128	Alternate Pond Dewatering Method for Turbidity	\$10,279.15	\$10,279.15	\$0.00	\$0.00	\$10,279.15	100%	\$0.00	\$1,028.00
129	Change Order #3	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00		\$0.00	\$0.00
	SUB-TOTALS	\$14,921,031.97	\$10,209,462.97	\$957,110.00	\$0.00	\$11,166,572.97	75%	\$3,754,459.00	\$1,116,663.00

CONTINUATION PAGE Page 10 of 10

PROJECT: 14061- Beach House @ Wiregrass APPLICATION #: 11

Payment Application containing Contractor's signature is attached.

PROJECT: 14061- Beach House @ Wiregrass APPLICATION #: 11

DATE OF APPLICATION: 08/25/2017

PERIOD THRU: 08/31/2017

PROJECT #s: 14-061-0

A B C D E F G H I

COMPLETED WORK STORED TOTAL % BALANCE

A	В	С	D	E	F	G		н	1
ITEM#	WORK DESCRIPTION	SCHEDULED AMOUNT	AMOUNT PREVIOUS PERIODS	AMOUNT THIS PERIOD	STORED MATERIALS (NOT IN D OR E)	TOTAL COMPLETED AND SYORED (D + E + F)	% COMP. (G / C)	BALANCE TO COMPLETION (C-G)	RETAINAGE (If Variable)
130	Omit Flag Pole and Concrete Base	(\$5,777.00)	\$0.00	\$0.00	\$0.00	\$0.00	0%	(\$5,777.00)	\$0.00
	For Construction Set Thru Revision 5 (Urgent Items)	\$73,821.14	\$30,267.00	\$36,910.00	\$0.00	\$67,177.00	91%	\$6,644.14	\$6,718.00
	For Construction Set Generator Changes	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00		\$0.00	\$0.00
133	For Construction Set Low Voltage Changes	\$26,423.07	\$13,212.00	\$11,890.00	\$0.00	\$25,102.00	95%	\$1,321.07	\$2,510.00
	For Construction Set Added Z Light Fixture Higher Output	\$0.00	\$0.00	\$0.00	\$0.00	\$0.00		\$0.00	\$0.00
	Rev. #3 Low Voltage Changes and Added Night Lights	\$5,557.04	\$3,890.00	\$833.00	\$0.00	\$4,723.00	85%	\$834.04	\$472.00
136	Ornit AL Unit Shower Curtains	(\$4,390.00)	\$0.00	\$0.00	\$0.00	\$0.00	0%	(\$4,390.00)	\$0.00
	Change All Exterior Brackets to Foam	(\$10,301.25)	\$0.00	\$0.00	\$0.00	\$0.00	0%	(\$10,301.25)	\$0.00
138	VE Landscape and Irrigation Drawings	(\$50,000.00)	\$0.00	\$0.00	\$0.00	\$0.00	0%	(\$50,000.00)	\$0.00
139	Omit Memory Cue Boxes	(\$6,138.00)	\$0.00	\$0.00	\$0.00	\$0.00	0%	(\$6,138.00)	\$0.00
140	Change Feeders to SER Cable	(\$14,105.00)	(\$14,105.00)	\$0.00	\$0.00	(\$14,105.00)	100%	\$0.00	(\$1,410.00)
141	Omit Door Entry Conduits	(\$11,138.00)	(\$11,138.00)	\$0.00	\$0.00	(\$11,138.00)	100%	\$0.00	(\$1,113.00)
	Use Hardi Prevail ILO Specified Hardi	(\$3,952.00)	(\$3,952.00)	\$0.00	\$0.00	(\$3,952.00)	100%	\$0.00	(\$395.00)
	TOTALS	\$14,921,031.97	\$10,227,636.97	\$1,006,743.00	\$0.00	\$11,234,379.97	75%	\$3,686,652.00	\$1,123,437.00

CONTINUATION PAGE Quentum Software Solutions, Inc. Document

CERTIFICATIONS:

ATTACHMENT A CERTIFICATE OF CONTRACTOR

[Required for Disbursement Requests for Hard Costs under Section 3.2(b) of the Disbursement Agreement and Section 502 of the Indenture]

Approved by Contractor

The 29 day of August . 20/7.

The undersigned, as Contractor, certifies to the Trustee that

(1) the representations made in paragraphs 5 (with respect to Hard Costs only), 6, 7, 8 (to the extent of Contractor's actual knowledge as of the date hereof), 9 (to the extent of Contractor's actual knowledge as of the date hereof) and 18 (to the extent of the Contractor's actual knowledge as of the date hereof) in the Disbursement Request dated 8/31..., 20/7 (the "Disbursement Request") are true, correct and complete; and

(2) the items set forth on Schedule A (with respect to Hard Costs only) to the Disbursement Request are true, correct and complete.

THE DOUGLAS COMPANY

By: Mist Name: MICAH HOSKINSON Title: PROJECT MANAGER

copy to: Greenwich Investment Management, Inc., as Bondholder Representative

BEACH HOUSE AT WIREGRASS PROJECT

EXHIBIT A-6

ATTACHMENT C CERTIFICATE OF ARCHITECT

[Required for Disbursement Requests for Hard Costs under Section 3.2(d) of the Disbursement Agreement and Section 502 of the Indenture]

Approved by Architect

The Lag of August 2017

The undersigned, as Architect, hereby certifies that to the best of its knowledge, based upon and to the extent of the duty of care standards in the Architect Contract and on such site visits as are required under the Architect Contract, that:

- (1) the attached Disbursement Request dated 2217 20_ (the "Disbursement Request") is recommended for payment;
- (2) the obligations on account of which payment is to be made were properly incurred and the amount requested is due and unpaid to the Contractor;
- (3) the cost of completing the Series 2016 Project under the Construction Contract (excluding costs not covered under the Construction Contract) is \$4.00,000
- (4) insofar as the payment is to be made for labor, materials, services or equipment, the work has progressed to the point indicated and the materials, services and equipment have been installed in the Series 2016 Project or have been delivered either to the Premises or at the proper place for fabrication and the actual value thereof is not less than the amount requested hereunder;
- the quality of the work is in accordance with the Plans and Specifications and the Construction Contract and progress thereof is such that the Series 2016 Project can reasonably be expected to be substantially completed by the Completion Date assuming that such progress continues at a pace consistent with the construction schedule:
- (6) application for all approvals, licenses and permits required for the construction, completion and intended use of the Series 2016 Project have been made in the ordinary course and there currently is no reason to believe that they will not be approved in due course;
- the amount of Hard Costs included in Disbursement Request is not greater than the actual value of labor, materials, services or equipment incorporated in the Series 2016 Project (or stored in accordance with Section 3.5(c) of the Disbursement Agreement) up to the date of this Disbursement Request (in the case of

EXHIBIT A-8

ATTACHMENT B CERTIFICATE OF CONSTRUCTION MONITOR

[Required for Disbursement Requests for Hard Costs under Section 3.2(c) of the sement Agreement and Section 502 of the Indenture]

Approved by the Construction Monitor

The 1st day of September 2017.

The undersigned, as the Construction Monitor, certifies to the Trustee that

- the statements made in paragraphs 4 (with respect to Hard Costs only), 5 (with respect to Hard Costs only), 6 and 10(b) in the Disbursement Request dated August 31, 20187(the "Disbursement Request") are true, correct and complete to the best of its knowledge;
- (2) the Construction Monitor has received copies of the requisitions and annex the Construction Monitor has received copies of the requisitions and annox thereto or other evidence to its satisfaction supporting each item of the Hard Costs covered by the Disbursement Request, and satisfactory lien releases and waivers from the Contractor and subcontractors for the work for which funds are requested (which may be subject to receipt of payment of the funds requested);
- to the extent such provisions are applicable, the conditions precedent in Sections 3.4, 3.5 or 3.6 hereof have been satisfied; and (3)
- the undersigned hereby approves the Disbursement Request

APPONO CONSULTING, LLC

Title

copy to: Greenwich Investment Management, Inc., as Bondholder Representative

BEACH HOUSE AT WIREGRASS PROJECT

EXHIBIT A-7

Disbursement Request Number 1) or to the date of such Disbursement Request from the date of the previous Disbursement Request (in the case of any subsequent Disbursement Requests), less Retainage;

- (8) there are no material impediments that would present a threat to completion of construction at the costs contemplated in present a finear to competition of construction at the costs contemplated in the Itemized Statement of Costs, approved Change Orders and the Construction Contract, as amended to date, and on the schedule contemplated in the construction progress schedule, as amended to date;
- attached hereto as Exhibit A is a chart specifying the stage and percentages of completion which has been achieved by each of the various trades engaged in the construction of the Series 2016 Project;
- (10) the amount certified by the Company in Section 10(a) of the strached Disbursement Request as the Total Estimated Series 2016 Construction Account of the Project Fund Balance is sufficient to pay the expected remaining costs of completing construction of the Series 2016 Project in accordance with the Plans and Specifications and the Construction Computer Series 2016 Project in accordance with the Plans and Specifications and the Construction Contract, as amended to date: and
- (11) in the case of payments under the Construction Contract, Forms G702 and G703 executed by the Company and the Contractor are attached.

ARCHITECTURAL CONCEPTS, INC.

Name: All Common Auny

copy to: Greenwich Investment Management, Inc., as Bondholder Representative

BEACH HOUSE AT WIREGRASS PROJECT

EXHIBIT A-9

RFI Summary:

Printed on Tue Aug 15, 2017 at 05:18 pm EDT

Joh #: 14-061-0 Beach House at Wiregrass Assisted Living and Memory Care 30070 St. Rd. 56
Wesley Chapel Florida. 33543

Open RFI Log

THEDOUGLASCOMPANY
LENG. BULD. SUCCESO.
The Douglas Company
2002 Recisions Street, Suite 400
Orlando, Prozia 23001
United States
(407) 370-2001

Date Initiated	Date Due Date Date Unitable	Due Date Variance	Subject	Overation	Drawing Number
21/51/80	98/18/47	-3 days VWC-		L. Pleuse confirm which will in each of the public toilets, 131, 147, 146, 118A, 111, 146, 190, 191, 216A, 220, 236, 226, and 227, should receive VWC-1, 2, Pleuse confirm that the back of house public toilets 174A and 178A do not require VWC-1, 2, Pleuse confirm which paint should be used in the public toilets.	
08/14/17	08/12/17	-2 days	Waterproof Balcoay Deck	Please confirm specification section 675/20 Witerproof Balcony Deck Surfacing applies to the 3000 poi concrete decked govered over a 60 mil elastramenic valentyroofing menthrane between the basa kinetic december approved. Agreemed, effect information provided in this specification relates to physical decimal manual and print that belong and per that that confings are social shown as manual manual and per that the confings are social shown as decimal anywhere of the plant.	A8.11
08/14/17	akriéri? -1 day		Mostens and Living Room Calling Reight	As shown on the stackness, the Liking Secon 186 and Rectors 188 call out an Little colling. TBC has determined that the colling height must be lowered to 18-6" to accommodate the planning and fire sprinklers in the ceiling, To keep the ceiling and crown molding look the same the soffice should be lowered to 5-6". Please confirm that TDC can preced with a Little ceiling and 3-6" or fills in these areas.	A6.14
08/08/17	51/11/30	4 days	Carridar Double Boom	As shown in the attachment, there are nine double-doors, RC105, RC105, RC105, RC105, RC112, RC119, RC205, noil RC205, located in the corridors that receive a pair of Act 110,	A4.11B, A4.12B, 4.13B, 4.22B, 4.23B
71/80/80	08/11/17	4 days	Dining Room 184A	As shown in the strachment, there is a beam that spans seroes the entrance to Dining Room 1844. The columns under 12 wide and the beam is 12 wide to match them. The columns to each joint to provide a uniform lost errors the space. Please review and confirm to provide a uniform lost errors the space. Please review and	A6.14

Submittal Summary:

* As of 08/31/17, there are 8 open submittals of which 1 is overdue. Submittals are being answered by priority in relationship to schedule of the building process as approved by the G.C.

PROJECT OVERVIEW



Printed on Tue Aug 15, 2017 at 05:16 pm EDT Job #: 14-061-9 Seach House at Wiregrass Assisted Living and Memory Care 2007 05; Rd. 56 Westey Chapel Florida. 33543

TDC - Open Submittal Log

THEDOUGLASCOMPANY LEAG. BUILD, BUCCEED.

•	Rev.	Title	Submit By	Approvers	Response	Approvers Bue Date
2.00		Dumpacer Gates	2017	Meyer, Jedi (MDI Selutions, Inc.) Contacti, Joshus (The Bouglas Company) Performs, Dashel (Mrchilochural Concepts Inc.)	Submitted Funtamed Funding	06/11/ 2017 06/11/ 2017 2017
4.40	a	Abundasın Rafilings	08/07/ 2017	Meyer, Jed (MIV Shitzbons, Inc.) Content, Johns of Peoples (Company) Mitchellar, Lisa Aus (Peoples (Company) Perdoma, Daskel Mchithectural Concepts Inc.)	Submitted Service of Perding Pending	08/07/ 2017 08/07/ 2017 08/21/ 2017 2017
10	a	Common Area Cabinets	2017	De la Tierru, Johan (IV) fractalisticos Cocp. J. Concesti, Johan (IV) bractalisticos Cocp. J. Prociona, Johan (Architectura Company) MACCeban, Lien Ann (Stradin:SEX)	Submitted Submitted Reviewed An Notes! Pending	07/06/2 2017 07/06/2 2017 02/13/2 2017 2017
2	8	Finished Bracket Mock-Up	08/08/ 2017	Quistero, Joque (AT Catafrortes, Inc.) Contacti, Joshus The Bougles Company) Periosas, Insaid utrithechast Company Inc.)	Submitted For Record Only Pending	08/08/ 2017 2017 2017 2017 2017
3	a	Door Hardware	2417	psyciet, male ICOMMERCIAL DODGE 6: PRAME SERVICES, INC.) Contactă, Joshan The Bouglas Company Person, Shavin (Architecturi) Concepts Inc.)	Submitted Raviewed Fending	06/06/ 2017 08/08/ 2017 06/22/ 2017
27		Dour Mandaure	7117 2017	Lopez, Steve (DV ELE/CTBE OF TAMPA BAYE DNC.) Cotenals, Joshua (The Bouglan Company) Perdona, Daniel dArchitechural transcepts Inc.)	Submitted Reviewed. Fending	2017 2017 2017 2017 2017 2017
9-00	8	The Samphos	710E	Lorentic, Notel (Tores-Tehal Picering, Inc.) Constati, Joshav (The Bouglass Company) Art Celtain, List Ann (Studio/STXS) Performs, Daskel (Arthitectural Cencepts Inc.)	Submitted Fer Record Cody Pending Pending	08/10/ 2017 2017 2017 08/24/ 2017

to 1 of



Job #: 14-061-0 Beach House at Wiregrass Assisted Living and Momony Care 30070 St. Rd. 56 Wesley Chapel Florida. 33543

•	Ben.	Title	Submit By	Approvess	Response	Approvers Due Date
						2017
89 65 00-5		Flooring Transitions	08/14/ 2017	Lorente, Neel Clorves Total Flooring, Inc.) Connect, Destry (The Possible Company) McGeshan, Lisa Ann (StudienStS) Predomo, Daniel (Architectural Concepts Inc.)	Submitted Submitted Submitted Prading Prading	08/14/ 2017 2017 2017 08/28/ 2017 2017 2017
074634-1		Shutters	98/1L/ 2017	Quinteen, Jooge MFI Construction, Inc.) Connect, Joodes (The Boughts Company) Perdonno, Daried (Architectural Concupts Inc.)	Submitted Resissaved Pending	08/11/ 2017 2017 2017 08/22/ 2017
0102800-1	o o	Shower Curtain Rado	08/15/ 2017	Socroman, Ken (Roffling Dak Supply; Inc.) Connect, Johns (The Poughes Crepany) McKeshan, Lisa Ann (Statistics May) Perdomo, Daniel (Architectural Concepts Inc.)	Submitted Submitted Practing Pending	08/15/ 2017 08/15/ 2017 08/24/ 06/24/ 2017
0230593-2	0	Testing, Adjusting, and Balancing HVAC				
323123-1		Vingi Pence Shop Derawing	2017	Mayor, jest (MDI Solutions, Inc.) Commit, Joohn (The Bougles Company) Perdonno, Daniel (Architectural Concepts Inc.)	Submitted Rentewed Pending	08/10/ 2017 2017 2017 08/24/ 2017

11 LICENSES

The following professional and entity/authorization licenses were found to be active in review of the State of Florida Department of Professional Regulation, Sunbiz and County public records as applicable.

License	Legal Name	Number	Expires
Architect Professional	Emmett Walsh	AA0013930	02/28/19
Architect Corp. Auth.	Architectural Concepts Inc	AAC001251	02/28/19
Mechanical Engineer	William Scott Crawford, P.E.	PE39436	02/28/19
Mech. Corp. Auth	Crawford Williams Engineering, Inc.	7029	02/28/19
Electrical Engineer	Michael Paul Spychala, P.E.	PE31533	02/28/19
Electrical Corp. Auth.	M.P. Spychala & Assoc. Inc.	3967	02/28/19
Structural Engineer	Richard Dean Wilson	PE37784	02/28/19
Structural Corp. Auth	Wilson Structural Consultants	9099	02/28/19
Civil Engineer	Matthew Joseph Angerosa	PE 60849	02/28/19
Civil Corp. Auth	King Engineering Associates. Inc	2610	02/28/19
General Contractor	Peter Douglas - The Douglas Co.	CGC1508034	08/31/18

12 INSURANCE

The following policies have been collected and found to meet the requirements of the respective agreement or contract.

Policy Holder	Type/Limits	Policy #	Expires
Architectural Concepts inc	General Liability 1,000,000/2,000,000	BPG68940	03/08/18
Architectural Concepts inc	Business Automobile Liability 1,000,000	BPG68940	03/08/18
Architectural Concepts inc	A/E Professional Liability 2,000,000	ARO0006091	12/02/17
The Douglas Comp.	General Liability 1,000,000/2,000,000	CMM1618491	04/01/18
The Douglas Comp.	Automobile Liability 1,000,000/each acc.	CMM1618491	04/01/18
The Douglas Comp.	Excess Liability 10,000,000	CMM1618491	04/01/18
The Douglas Comp.	Worker Compensation 1,000,000/each occ.	WCP5968580	04/01/18
The Douglas Comp.	Contractor's Equipment 150,000 per item (2,500 Ded.)	CMM1618491	04/01/18

APPENDIX 'A'- SITE PROGRESS AND PHOTOS

DATE: A site visit was performed on **August 30**, **2017 at 09:00 a.m. EST**. by the Construction Monitor.


OAC ATTENDEES: Scott Walker (PSL), Michael Hass (DDP), Shawn Pierson (ACI), Daniel Perdomo (ACI), Peter Douglas (TDC), Micah Hoskinson (TDC), Joshua Conradi (TDC), Steve Farnham (TDC), Darren Azdell (AC), Steven Rogers (AC),

SITE VISIT ATTENDEES: Scott Walker (PSL), Michael Hass (DDP), Shawn Pierson (ACI), Daniel Perdomo (ACI), Peter Douglas (TDC), Micah Hoskinson (TDC), Joshua Conradi (TDC Steve Farnham (TDC), Darren Azdell (AC), Steven Rogers (AC),

ENVIRONMENTAL CONDITIONS: Partly cloudy and warm, 88°.

GENERAL OBSERVATIONS:

No abnormalities were evident on site which might indicate an impending delay due to weather or coordination issues. The CM and the Architect noted that while the trades have adequate distribution and separation, the building was dirty, cluttered and found to be unsafe in some areas. The CM noted several items that were meant to be disposed of, but still present from the previous site walks. The architect brought this to the attention to the GC VP, project manager and site supervisor.

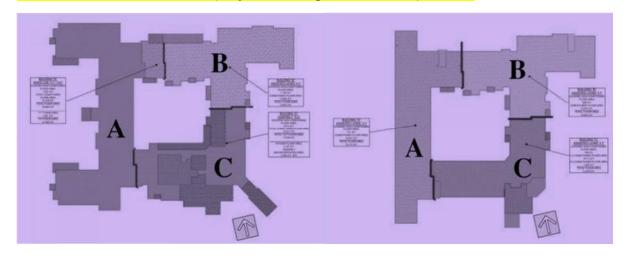

FIRST LEVEL SECOND LEVEL



Figure 1. Aerial from West of project.



Figure 2. Aerial showing South elevation.



Figure 3. Aerial of porte-cochere and interior elevations of courtyard.













Figure 4-11 Materials on site, doors and plumbing fixtures.













Figure 11-17 All three compartments of project exterior finishes.














Figure 17-23 Interior framing and MEP rough in in various stages of completion.





Figure 24-25. Bathroom Finishes.





Figure 26-27. Elevator installation well underway.





Figure 28-29. Typical trash and debris issues to be addressed.

APPENDIX 'B' - MEETING MINUTES

Owner, Architect, Contractor meetings are being held monthly on site on the first Wednesday of each month. The meeting is followed or preceded by a site walk and review of work and materials in place by the CM and the Architect. Meeting minutes will be taken by the GC and distributed to participants and the project team through Procore. The CM monitors Procore for communication and progress as well as inspections through the County Building Department website.

Insert meeting minutes for:

08/30/2017



Meeting #22

The Douglas Company 200 E. Robinson Street, Suite 400 Orlando, Florida 32801 Phone: (407) 370-2001 Fax: (407) 370-2005 Project: 14-061-0 - Beach House at Wiregrass Assisted Living and Memory Care 30070 St. Rd. 56 Wesley Chapel, Florida 33543

Owner/Architect/Contractor Weekly Coordination Meeting Minutes

MEETING DATE: 08/30/2017 MEETING TIME: 9:00 AM - 12:00 pm

MEETING LOCATION: Job Site Trailer

OVERVIEW:

OAC Coordination Meeting

NOTES:

ATTACHMENTS:

BHW - Owner Contract Scheduled Updated 8:29-17.pdf | BHW - Owner 4 Week Look Ahead Schedule 8:29-17.pdf | Open RFI Log 8:29-17.pdf | Open RFI Log 8:29-17.pdf | Open RFI Log 8:29-17.pdf | Submitted Log 8:29-2017.pdf | BHWC - Potential Change Order List 8:29-17.pdf

ATTENDEES:

Name	Company	Phone Number	Email	Attendance
Darren Azdell	Appono Consulting, LLC	Tel:	damen@apponoconsulting.com	Absent
Steve Rogers	Appone Consulting, LLC	Tel:	steve@apponoconsuting.com	Present
Daniel Perdomo	Architectural Concepts Inc.	Tel: (727) 584-7178	dperdomo@archconcept.com	Present
Shawn Pierson	Architectural Concepts Inc.	Tel: (727) 584-7178	spierson@archconcept.com	Present
Michael Hass	Orive Development Partners	Tel:	mh@drivedp.com	Present
Vinny Gallano	KING ENGINEERING	Tel: (813) 880-8881	vgallano@kingengineering.com	Absent
Scott Walker	PSL Wiregrass LP	Tel: (214) 736-7007	swaker@prevarian.com	Present
Lisa Ann McKeehan	StudioS0K5	Tel: (512) 579-5254	lisa@studiosix5.com	Absent
Joshua Conradi	The Douglas Company	Tel: (407) 370-2001	jconradi@douglascompany.com	Present
Peter Douglas, P.E.	The Douglas Company	Tel: (419) 865-8600 ext. 250	pdouglas@douglascompany.com	Present
Steve Famham	The Douglas Company	Tel:	sfamham@douglascompany.com	Present
Micah Hoskinson	The Douglas Company	Tel: (407) 370-2001	mhoskinson@douglascompany.com	Present
Matthew Lebright	The Douglas Company	Tel: (407) 370-2001	mlebright@douglascompany.com	Absent

No	Meeting Origin	Title	Assignment	Due Date	Priority	Status
1.1	1	Safety and Security				Open

These resulting minutes are believed to be an accurate reflection of those items also used and the conclusions that were reached during the referenced meeting.

Please contact the Douglas Company if there are any discrepancies or questions with the content of these minutes.



Previous Meeting Minutes:

Safety:

- The balcony doors have been installed. TDC is looking into options to secure doors before the rails arrive.
- 2. TDC has notified all of the subs that permanent power will be connected:

Official Documented Meeting Minutes:

Safety:

- Temporary doors are being installed the week of 8-29-17 and 9-5-17.
- PSL needs TDC to focus on maintaining the temporary hand rails at 2nd floor openings.
- Permanent Power is being connected by Withlacoochee today, 8-30-17,

Sch	nedule & Perm	its				
No	Meeting Origin	Title	Assignment	Due Date	Priority	Status
2.1	1	Schedule & Permits				Open
	100000000000000000000000000000000000000	Meeting Minutes: s to review the projects current	schedule and any required permits.			
	SCHEDU	LE				

- - 1. There is a permanent power inspection scheduled for 8/16/17. Once it is passed, WREC will be release to terminate the main feed in the transformer.
 - Compartment A RTUs are ready to be turned on once permanent power is achieved.
 - The 2nd floor will be climatized by 8/25/17.
- The Place and Vlace are currently being installed beginning in A2, then C2, followed by B2. All of the unit varieties, excluding the compartment B1 varieties, are on site.
- The balance of the prehung doors are arriving on site by 8/21/17.
 All of the bi-fold doors and sliding doors are on site.
- Compartment A2 casing and base will be finished by 8/21/17.
- C2 casing and base installation is scheduled to be complete by Friday, 8/21/17.
- All of the 2nd floor plumbing fixtures are on site.
- All of the units have a 1st coat of paint on walls and a 2nd coal on the ceilings.
 The electrician will complete their trim out in Compartment A2 by 8/17/17.
- The unit entry doors are tentatively scheduled to be on site on 9/4/17
- Prevarian, TDC, and Assa Abloy need to discuss who is responsible for unloading the Assa Abloy materials when they arrive on site and where the materials will be stored. TDC will identify a room onsite that can be secured to house the equipment.
- The Memory Care prehung doors will be installed by 8/21/17.
- The acoustical grid materials will arrive on site on 8/21/17.
- The C1 offices have ceilings and walls hung. The drywall has not been finished or sanded.
- There is a permit required for each kitchen hood. These permits have been submitted.
- The epoxy flooring will be installed in late September
- 20. All of the exterior stucco is complete and 98% of exterior stone and siding has been installed.
- ACI and Prevarian have chosen the smooth brackets.
- 22. There are electrical drawing sheets that need to be added to the plans currently being reviewed with the county. MPS has informed TDC that there are two updated sheets and TDC will submit them on (V17/1)
- The elevator equipment arrived on 8/15/17 and there is a crew working in each pit.
- The elevators cannot be inspected until POTS lines are installed with a dial tone
- 25. TDC was notified that Spectrum is 4-6 weeks away from their installation date.
- 26. PSL informed TDC that inviacom will be installing the POTS lines.
- 27. TDC is identifying and contacting individuals necessary to obtain TCOs and COs. A meeting will be scheduled for all parties involved.
- Substantial completion is scheduled for November 13th.
- SS5 and Prevarian plan to install furniture on Nov 14th.
- 30. TDC has requested that SS5, Prevarian, and ACI all walk through together for punch.
- 31. TDC's rough estimate for the first punch walk is between the last week of September and the first week of October.

These meeting minutes are believed to be an accurate reflection of those fiams stacussed and the conclusions that were reached during the referenced meeting.

Please contact The Douglas Company if there are any discrepancies or questions with the content of these minutes.

THEDOUGLASCOMPANY LEAD. BUILD. SUCCEED

Meeting #22

- Prevarian has requested a punch schedule from TDC. ACI will walk the facility prior to the scheduled dates to confirm that the secified areas are ready for punch
- 33. Prevarian has requested that TDC bring the keying schedule to the end of the month OAC.

PERMITS

Revision 6 will be completed once the revised electrical sheets are inserted.

Official Documented Meeting Minutes:

All parties to review the projects current schedule and any required permits.

- The first order of unit entry doors is scheduled to arrive on October 9th.
- A2 flooring is scheduled to start on 9-18-17.
- It will take 2-3 days to paint all unit entry doors when they arrive. CDFS can install 10-15 unit entry doors per day.
- Tomes can complete the flooring for 10-12 units per week.
- The A2 carpet will be the first flooring installed.
- The A2 door casing and trim is complete
- The door casing and trim painting is currently on going. The A2 window sills will be completed by 9-1-17.
- All of the A2 tops have been set.
- The common area accustical grid is currently being installed on the 2nd floor.
- The bathroom accessories are on site and being installed in A2.
- The C2 windowsits are scheduled to be complete on 9-1-17.

 The acoustical ceiling grid in C2 started 8-30-17 but may be delayed due to the switch to 2x2 tiles.
- The bathroom accessories in C2 will be installed by 9-8-17.
- The closet shelving will be onsite by 9/11
- The C2 viryl flooring will begin the week of 9-25-17.
- The B2 cabinets will be completed by 9-8-17
- The B2 walls are painted and the trim and casing have been installed.
- The comidor doors on the 2nd floor have been changed to 2'-10" due to comidor widths.
- The miscellaneous missing door trames on 2nd floor will be will be installed by 9-1-17.
- The Assa Abloy equipment is arriving on 9-7-17 and their personnel will be on site on 9-11-17.
- The common area bathroom tile is approved and on site.

 TDC plans on having the September 27th OAC in the on site trailer and then the trailer at the end of that week. The C1 MEP inspection is scheduled for 8-21-17.
- The brackets will be arriving the week of 9-4-17.
- 25.
- Shutters will arrive the week of 9-11-17,
- 28. Prevarian will schedule SS5 for a job site visit at the end of September to review the unit flooring.
- 29: TDC will mock-up each type of flooring for review.

PERMITS

- TDC is attempting to meeting with the members of Pasco county who will be inspecting to allow a TCO.
- 2. All drawings have been delivered to Pasco and TDC has the checks ready to turn in.
- The kitchen hood has not passed inspection. The inspector has stringent requirements and TDC is requesting ACIs help in interpreting the requirements
- 4. The monument sign will require its own permit.

No	Meeting Origin	Title	Assignment	Due Date	Priority	Status
3.1	1	Submittals & RFI's				Open
	Descript Submitta	ia .				

These meeting minutes are believed to be an accurate reflection of those items discussed and the conclusions that were reached during the referenced meeting Please contact The Douglas Company if there are any discrepancies or questions with the content of these minutes.

Printed On: 09/14/2017 02:37 PM The Douglas Company Page 3.of 5



- The Wii Alley cabinet issues have been resolved
- The border tile issue has been resolved. TDC will create an RFI concerning the Bar area cabinets.
- 4. ACI Will work with Wiregrass to figure out the fending requirements.

4.1 1 Ste & Buildien printing			5 DOMESTICAL STATE OF THE PROPERTY OF THE PROP	Title	Meeting Origin	No
Section 2 and a section of tradesics	Open	2 7		Site & Building Logistics	1	4.1
Description: All parties to review site and building logistics.			cs.	to review site and building logist		

Pric	Pricing							
No	Meeting Origin	Title	Assignment	Due Date	Priority	Status		
5.1	1	Pricing				Open		

Description:

All parties to review pricing requirements.

Previous Meeting Minutes:

PRICING

- Prevarian has requested that the individual change requests be broken out into line items with all of the appropriate backup included.
- Door hardware, decorative brackets, and storefront doors need to be resolved in order for TDC to proceed.
 Provenian, ACI, and DDP will review the open change orders on 8/17/17. TDC needs approvals by 8/18/17 in order to release materials on time.

No	Meeting Origin	Title	Assignment	Due Date	Priority	Status
6.1	7	Closeout Documents				Open
		s to review open closeout docur Meeting Minutes:	ment items.			

No	Meeting Origin	Title	Assignment	Due Date	Priority	Status
7.1	1	Open Discussion				Open

These meeting minutes are believed to be an accurate reflection of those items documend and the conclusions that were reached during the referenced meeting.

Please contact The Douglas Company if there are any discrepancies or questions with the content of these minutes

The Douglas Company Printed On: 09/14/2017 02:37 PM Page 4 of 5

Meeting #22



Previous Meeting Minutes:		
Open Discussion		

Nex	t Meeting					
No	Meeting Origin	Title	Assignment	Due Date	Priority	Status
8.1		Next Meeting				Open
	Descript All parties The next	s to confirm next meeting d	ste and time. a on WEDNESDAY, 8-30-17 at 9:00 AM.	12.		
		nted Meeting Minutes: eeting will a conference on	WEDNESDAY, 9-13-17 at 9:00 AM.			

These meeting minutes are believed to be an accurate reflection of those items discussed and the condusions that were reached during the referenced meeting.

Please contact The Douglas Company if there are any discrepancies or questions with the content of these minutes.

The Douglas Company Page 5 of 5 Printed On: 09/14/2017 02:37 PM



IV. OPERATIONS AND MARKETING

Linda Mena, Executive Director, and Callie Sears, Director of Community Relations are making great progress establishing Beach House in the Wesley Chapel market.

Relationships continue to strengthen with Wesley Chapel Chamber of Commerce, the WOW organization (Women of Wesley Chapel), and Emma Hemness, a prominent local elder law attorney. Ongoing affiliations continue with North Tampa Behavioral Center, the Shops at Wiregrass Ranch, Raymond James and Florida Hospital.





- ▲ Executive Director Linda Mena (left) and Director of Community Relations, Callie Sears (right)
- 20 Industry professionals attended the September 20th "Rock-n-Wine" event.

Beach House is striving to brand itself as valuable community resource. The team hosted several successful outreach events in August and September:

July 27 Upside of Downsizing
August 10 Knowing what your assets are worth
August 10 Hidden Treasures in Your Home
August 24 Common Sense Caregiving – Part 1
September 14 Legal Matters Seniors Need to Know
September 20 Rock-n-Wine
September 21 Common Sense Caregiving – Part 2

Beach House at Wiregrass Ranch Assisted Living + Memory Care MONTHLY STATEMENT OF BORROWER AUGUST 2017




Operations and Marketing (Continued)

The team is bolstering the community's social media presence with frequent Facebook posts, and several Facebook ads are currently circulating the platform. Together with TEGNA, the team has developed a full digital marketing strategy to be rolled out on October 1^{st} .

The website continues to be a top lead source for the community, with steady activity growth over the past several weeks.

Community Website 12-Week Activity



Beach House currently has reservation deposits for 4 memory care units and 13 assisted living units. Two of the assisted living reservations are for couples, bringing the waiting list to 19 residents. All of the future assisted living residents have taken advantage of the Diamond Club membership, which offers benefits such as monthly discounts and fixed rates. The community continues to make great progress as it targets a January opening.







PSL Wiregrass, LP Profit & Loss

January through August 2017

In the second Account 2047			
January through August 2017		_	Accrual Basis
	Ptnr	Ops	Consolidated
	Jan - Aug 17	Jan - Aug 17	Jan - Aug 17
Income			
Bond Interest Income	18,306.53		18,306.53
Total Income	18,306.53	0.00	18,306.53
Gross Profit	18,306.53	0.00	18,306.53
Expense			
Advertising & Marketing		48,830.71	48,830.71
Bank Fees		217.85	217.85
Contract Labor		4,676.00	4,676.00
Copy Service		31.57	31.57
Employee Meals		82.03	82.03
Employment Screenings		90.00	90.00
IΤ		4,336.95	4,336.95
Late Fees		5.00	5.00
Licenses & Fees		150.00	150.00
Mangement Fee		20,000.00	20,000.00
Office Supplies		2,370.29	2,370.29
Postage & Delivery		52.54	52.54
Professional Fees		112.50	112.50
Rent Expense		15,726.32	15,726.32
Salaries & Benefits			
LCS Employees		54,568.91	54,568.91
Total Salaries & Benefits	0.00	54,568.91	54,568.91
Dues & Subscriptions		100.00	100.00
Telephone Expense		482.67	482.67
Travel Expense		3,424.22	3,424.22
Utilities		576.06	576.06
Amortization Expense	27,200.64		27,200.64
Total Expense	27,200.64	155,833.62	183,034.26
Net Income	-8,894.11	-155,833.62	-164,727.73

8:30 AM

10/11/2017

PSL Wiregrass, LP Balance Sheet

As of August 31, 2017				Accrual Basis
	Ptnr	Adj	Ops	Consolidated
	Aug 17	Aug 17	Aug 17	Aug 17
ASSETS				
Current Assets				
Checking/Savings				
Checking #1	78,641.96		39,224.99	117,866.95
Checking #3			5,000.00	5,000.00
Total Checking/Savings	78,641.96	0.00	44,224.99	122,866.95
Total Current Assets	78,641.96	0.00	44,224.99	122,866.95
Total Fixed Assets	26,036,015.92	0.00	0.00	26,036,015.92
Total Other Assets	583,999.66	-159,000.00	11,998.25	436,997.91
TOTAL ASSETS	26,698,657.54	-159,000.00	56,223.24	26,595,880.78
LIABILITIES & EQUITY				
Liabilities				
Total Accounts Payable	974,319.97	-159,000.00	207,556.86	1,022,876.83
Total Current Liabilities	974,319.97	-159,000.00	207,556.86	1,022,876.83
Total Long Term Liabilities	22,750,000.00	0.00	4,500.00	22,754,500.00
Total Liabilities	23,724,319.97	-159,000.00	212,056.86	23,777,376.83
Total Equity	2,974,337.57	0.00	-155,833.62	2,818,503.95
TOTAL LIABILITIES & EQUITY	26,698,657.54	-159,000.00	56,223.24	26,595,880.78

8:28 AM

10/11/2017

PSL Wiregrass, LP Statement of Cash Flows

January through August 2017 Consolidated Ptnr Adj Ops Jan - Aug 17 Jan - Aug 17 Jan - Aug 17 Jan - Aug 17 **OPERATING ACTIVITIES** Net Income -8,894.11 -155,833.62 -164,727.73 Adjustments to reconcile Net Income to net cash provided by operations: **Prepaid Expenses** -11,998.25 -11,998.25 **Accrued Expenses** 3,353.08 3,353.08 **Deferred Revenue** 4,500.00 4,500.00 -159,000.00 204,203.78 -97,847.57 **Accounts Payable** -143,051.35 Net cash provided by Operating Activities -151,945.46 -159.000.00 44,224.99 -266,720.47 **INVESTING ACTIVITIES Security Deposit** -2,475.00 -2,475.00 CONSTRUCTION HARD COSTS:ALF Construction (Hard Costs) -8.335.565.97 -8,335,565.97 **DEVELOPMENT SOFT COSTS** -1,785,736.21 -1,785,736.21 **Land:Operating Expenses During Const** -450.00 -450.00 Trustee Accounts:Project Fund:Series 2016:221993005 Construction Account 9,405,525.79 9,405,525.79 Trustee Accounts:Project Fund:Series 2016:221993011 Capitalized Issue Fee 17,062.47 17,062.47 Trustee Accounts:Project Fund:Series 2016A:221993009 Capitalized Int. Sub 799,048.61 799,048.61 Trustee Accounts:Project Fund:Series 2016A:221993015 Borrower Eq Cap Int -1,416.20 -1,416.20 Trustee Accounts:Project Fund:Series 2016B:221993010 Capitalized Int. Sub 61,244.44 61,244.44 Trustee Accounts:Project Fund:Series 2016B:221993016 Borrower Eq Cap Int -77.53 -77.53 Trustee Accounts: Working Capital Fund: Series 2016:221993006 Working Cap Fund 209,815.95 209,815.95 Trustee Accounts:Interest Fund:Series 2016A:221993000 Interest Account -15,221.51 -15,221.51 Trustee Accounts:Interest Fund:Series 2016B:221993002 Interest Account -78.23 -78.23 **Due from Operations** -159,000.00 159,000.00 0.00 **Accumulated Amortization** 27,200.64 27,200.64 219,877.25 159,000.00 Net cash provided by Investing Activities 0.00 538 955 23 Net cash increase for period 67,931.79 44,224.99 272,234.76 Cash at beginning of period 10,710.17 10,710.17 0.00 Cash at end of period 78,641.96 0.00 44,224.99 282,944.93

8:34 AM

10/11/2017



VI. BALANCES OF TRUSTEE-HELD FUNDS



U.S. Bank TrustNow Essentials Cash Balances - Settled By Status, Account

Page: 1 of 1

Print Date: 09/01/2017 at 12:31:56 am

Data As Of: 08/31/2017

Account #	Account Name	<u>Status</u>	Principal Cash	Income Cash	Total Cash	Cash Equivalents	Total Cash + Equivalents
221993000	CTA BEACH HOUSE 2016A INTEREST ACCT	Open	0.00	0.00	0.00	18,129.05	18,129.05
221993001	CTA BEACH HOUSE 2016A PRINCIPAL	Open	0.00	0.00	0.00	0.00	0.00
221993002	CTA BEACH HOUSE 2016B INTEREST ACCT	Open	0.00	0.00	0.00	94.25	94.25
221993003	CTA BEACH HOUSE 2016B PRINCIPAL	Open	0.00	0.00	0.00	0.00	0.00
221993004	CTA BEACH HOUSE 2016 REVENUE FUND	Open	0.00	0.00	0.00	0.00	0.00
221993005	CTA BEACH HOUSE 2016A CONSTRUCTION	Open	0.00	0.00	0.00	7,336,810.96	7,336,810.96
221993006	CTA BEACH HOUSE 2016 WORKING CAPITAL	Open	0.00	0.00	0.00	1,200,399.79	1,200,399.79
221993007	CTA BEACH HOUSE 2016 REP & REPL FUND	Open	0.00	0.00	0.00	0.00	0.00
221993008	CTA BEACH HOUSE 2016 INS & TAX ESC	Open	0.00	0.00	0.00	0.00	0.00
221993009	CTA BEACH HOUSE 2016A CAP INT ACCT	Open	0.00	0.00	0.00	577,727.22	577,727.22
221993010	CTA BEACH HOUSE 2016B CAP INT ACCT	Open	0.00	0.00	0.00	37,902.22	37,902.22
221993011	CTA BEACH HOUSE 2016 CAP ISSUERS FEE	Open	0.00	0.00	0.00	64,837.53	64,837.53
221993012	CTA BEACH HOUSE 2016 SURPLUS FUND	Open	0.00	0.00	0.00	0.00	0.00
221993013	CTA BEACH HOUSE 2016A COI ACCOUNT	Open	0.00	0.00	0.00	0.00	0.00
221993014	CTA BEACH HOUSE 2016B COI ACCOUNT	Open	0.00	0.00	0.00	4,046.74	4,046.74
221993015	CTA BEACH HOUSE 2016A BORR EQ CAP IN	Open	0.00	0.00	0.00	1,268,026.64	1,268,026.64
221993016	CTA BEACH HOUSE 2016B BORR EQ CAP IN	Open	0.00	0.00	0.00	69,421.48	69,421.48
	Gran	nd Total	0.00	0.00	0.00	10,577,395.88	10,577,395.88

**** End Of Report ****

Note: Balances shown reflect the results of prior-day transactions and do not reflect any sweep activity.



PSL WIREGRASS LP ATTN DODD CRUTCHER 8214 WESTCHESTERDR SUITE 600 DALLAS TX 75225-6112 00- -M -N -PC -244-01 0183414-00-03300-01

3766 Page 1 of 6

ACCOUNT NUMBER: 221993000 CAPITAL TRUST AGENCY SENIOR HOUSING REVENUEBONDS (BEACH HOUSE AT WIREGRASS RANCH PROJECT) SERIES 2016A AND TAXABLE 2016B A INTEREST ACCOUNT

This statement is for the period from August 1, 2017 to August 31, 2017

QUESTIONS?

If you have any questions regarding your account or this statement, please contact your Account Manager or Analyst.

Account Manager:
SHERYL LEAR
EX-FL-WWSJ
225 E. ROBINSON ST., SUITE 250
ORLANDO, FL 32801
Phone 904-358-5363
E-mail SHERYL.LEAR@USBANK.COM



00- -M -N -PC -244-01 00376601 3766 0183414-00-03300-01 Page 2 of 6

ACCOUNT NUMBER: 221993000 CAPITAL TRUST AGENCY SENIOR HOUSING REVENUEBONDS (BEACH HOUSE AT WIREGRASS RANCH PROJECT) SERIES 2016A AND TAXABLE 2016B A INTEREST ACCOUNT

This statement is for the period from August 1, 2017 to August 31, 2017

SPECIAL MESSAGES

Faster trade settlement begins September 5

To better meet the needs of all investors, the financial services industry is shortening the settlement cycle for stocks, corporate bonds, municipal bonds, unit investment trusts and financial products comprised of these security types (such as exchange-traded funds). The standard settlement cycle of three business days after the trade date will be changed to two business days on September 5, 2017.





00- -M -N -PC -244-01 00376601 3766 0183414-00-03300-01 Page 3 of 6

ACCOUNT NUMBER: 221993000
CAPITAL TRUST AGENCY SENIOR HOUSING
REVENUEBONDS (BEACH HOUSE AT
WIREGRASS RANCH PROJECT) SERIES
2016A AND TAXABLE 2016B
A INTEREST ACCOUNT

MARKET VALUE SUMMARY				
	Current Period 08/01/17 to 08/31/17			
Beginning Market Value	\$16,410.61			
Contributions	1,715.69			
Adjusted Market Value	\$18,126.30			
Investment Results				
Interest, Dividends and Other Income	2.75			
Total Investment Results	\$2.75			
Ending Market Value	\$18,129.05			



00- -M -N -PC -244-01 00376601 3766 0183414-00-03300-01 Page 4 of 6

ACCOUNT NUMBER: 221993000 CAPITAL TRUST AGENCY SENIOR HOUSING REVENUEBONDS (BEACH HOUSE AT WIREGRASS RANCH PROJECT) SERIES 2016A AND TAXABLE 2016B A INTEREST ACCOUNT

This statement is for the period from August 1, 2017 to August 31, 2017

ASSET DETAIL AS OF 08/31/17						
Shares or Face Amount	Security Description	Market Value/ Price	Tax Cost/ Unit Cost	% of Total Yield at Market	Est Ann Inc	
Cash Equ	ivalents					
18,129.050	US Bank Mmkt 5 - Ct 9AMMF05B2	18,129.05 1.0000	18,129.05 1.00	100.0 .20 *	36.26 *	
Total Casl	n Equivalents	\$18,129.05	\$18,129.05	100.0	\$36.26	
Total Ass	sets	\$18,129.05	\$18,129.05	100.0	\$36.26	

ASSET DETAIL MESSAGES

Time of trade execution and trading party (if not disclosed) will be provided upon request.

Publicly traded assets are valued in accordance with market quotations or valuation methodologies from financial industry services believed by us to be reliable. Assets that are not publicly traded may be reflected at values from other external sources. Assets for which a current value is not available may be reflected at a previous value or as not valued, at par value, or at a nominal value. Values shown do not necessarily reflect prices at which assets could be bought or sold. Values are updated based on internal policy and may be updated less frequently than statement generation.

For further information, please contact your Analyst.

** The Yield at Market set forth in this statement for any money market fund is based on the interest rate applicable to that money market fund as of the last business day of the statement period (or most recent daily rate available) and may not be relied upon as (i) a yield estimate for the statement period as a whole, or (ii) a guarantee of future performance.





00- -M -N -PC -244-01 00376601 3766 0183414-00-03300-01 Page 5 of 6

ACCOUNT NUMBER: 221993000
CAPITAL TRUST AGENCY SENIOR HOUSING
REVENUEBONDS (BEACH HOUSE AT
WIREGRASS RANCH PROJECT) SERIES
2016A AND TAXABLE 2016B
A INTEREST ACCOUNT

This statement is for the period from August 1, 2017 to August 31, 2017

CASH SUMMARY

	Income Cash	Principal Cash	Total Cash
Beginning Cash Balance as of 08/01/2017	\$.00	\$.00	\$.00
Taxable Interest	2.75		2.75
Cash Receipts		1,715.69	1,715.69
Transfers	- 2.75	2.75	
Net Money Market Activity		- 1,718.44	- 1,718.44
Ending Cash Balance as of 08/31/2017	\$0.00	\$0.00	\$0.00



00- -M -N -PC -244-01 00376601 3766 0183414-00-03300-01 Page 6 of 6

ACCOUNT NUMBER: 221993000
CAPITAL TRUST AGENCY SENIOR HOUSING
REVENUEBONDS (BEACH HOUSE AT
WIREGRASS RANCH PROJECT) SERIES
2016A AND TAXABLE 2016B
A INTEREST ACCOUNT

	TRAN	NSACTION DETAIL		
Date Posted	Description	Income Cash	Principal Cash	Tax Cost
	Beginning Balance 08/01/2017	\$.00	\$.00	\$16,410.61
08/01/17	Interest Earned On US Bank Mmkt 5 - Ct Interest From 7/1/17 To 7/31/17 9AMMF05B2	2.75		
08/02/17	Cash Disbursement Transfer To Principal Income Earnings	- 2.75		
08/02/17	Cash Receipt Transfer From Income Income Earnings		2.75	
08/02/17	Cash Receipt Transfer From Another Trust Paid From Account # 221993005 Income Earnings		1,603.19	
08/02/17	Cash Receipt Transfer From Another Trust Paid From Account # 221993009 Income Earnings		101.11	
08/02/17	Cash Receipt Transfer From Another Trust Paid From Account # 221993011 Income Earnings		11.39	
08/02/17	Purchased 1,718.44 Units Of US Bank Mmkt 5 - Ct Trade Date 8/2/17 9AMMF05B2		- 1,718.44	1,718.44
	Ending Balance 08/31/2017	\$0.00	\$0.00	\$18.129.05





PSL WIREGRASS LP ATTN DODD CRUTCHER 8214 WESTCHESTERDR SUITE 600 DALLAS TX 75225-6112 00- -M -N -PC -244-01 0183416-00-03300-01 3766 Page 1 of 4

ACCOUNT NUMBER: 221993001 CAPITAL TRUST AGENCY SENIOR HOUSING REVENUEBONDS (BEACH HOUSE AT WIREGRASS RANCH PROJECT) SERIES 2016A AND TAXABLE 2016B A PRINCIPAL ACCOUNT

This statement is for the period from August 1, 2017 to August 31, 2017

QUESTIONS?

If you have any questions regarding your account or this statement, please contact your Account Manager or Analyst.

Account Manager:
SHERYL LEAR
EX-FL-WWSJ
225 E. ROBINSON ST., SUITE 250
ORLANDO, FL 32801
Phone 904-358-5363
E-mail SHERYL.LEAR@USBANK.COM



00- -M -N -PC -244-01 00376601 3766 0183416-00-03300-01 Page 2 of 4

ACCOUNT NUMBER: 221993001 CAPITAL TRUST AGENCY SENIOR HOUSING REVENUEBONDS (BEACH HOUSE AT WIREGRASS RANCH PROJECT) SERIES 2016A AND TAXABLE 2016B A PRINCIPAL ACCOUNT

This statement is for the period from August 1, 2017 to August 31, 2017

SPECIAL MESSAGES

Faster trade settlement begins September 5

To better meet the needs of all investors, the financial services industry is shortening the settlement cycle for stocks, corporate bonds, municipal bonds, unit investment trusts and financial products comprised of these security types (such as exchange-traded funds). The standard settlement cycle of three business days after the trade date will be changed to two business days on September 5, 2017.





00- -M -N -PC -244-01 00376601 3766 0183416-00-03300-01 Page 3 of 4

ACCOUNT NUMBER: 221993001
CAPITAL TRUST AGENCY SENIOR HOUSING
REVENUEBONDS (BEACH HOUSE AT
WIREGRASS RANCH PROJECT) SERIES
2016A AND TAXABLE 2016B
A PRINCIPAL ACCOUNT

This statement is for the period from August 1, 2017 to August 31, 2017

MA	RKET VALUE SUMMARY	
	Current Period 08/01/17 to 08/31/17	
Beginning Market Value	\$0.00	
Ending Market Value	\$0.00	
MARKET	VALUE SUMMARY MESSAGES	

No activity qualifies for this statement period.



00- -M -N -PC -244-01 00376601 3766 0183416-00-03300-01 Page 4 of 4

ACCOUNT NUMBER: 221993001 CAPITAL TRUST AGENCY SENIOR HOUSING REVENUEBONDS (BEACH HOUSE AT WIREGRASS RANCH PROJECT) SERIES 2016A AND TAXABLE 2016B A PRINCIPAL ACCOUNT

This statement is for the period from August 1, 2017 to August 31, 2017

ASSET DETAIL MESSAGES

No reportable securities for this statement period





PSL WIREGRASS LP ATTN DODD CRUTCHER 8214 WESTCHESTERDR SUITE 600 DALLAS TX 75225-6112 00- -M -N -PC -244-01 0183418-00-03300-01 3766 Page 1 of 6

ACCOUNT NUMBER: 221993002 CAPITAL TRUST AGENCY SENIOR HOUSING REVENUEBONDS (BEACH HOUSE AT WIREGRASS RANCH PROJECT) SERIES 2016A AND TAXABLE 2016B B INTEREST ACCOUNT

This statement is for the period from August 1, 2017 to August 31, 2017

QUESTIONS?

If you have any questions regarding your account or this statement, please contact your Account Manager or Analyst.

Account Manager:
SHERYL LEAR
EX-FL-WWSJ
225 E. ROBINSON ST., SUITE 250
ORLANDO, FL 32801
Phone 904-358-5363
E-mail SHERYL.LEAR@USBANK.COM



00- -M -N -PC -244-01 00376601 3766 0183418-00-03300-01 Page 2 of 6

ACCOUNT NUMBER: 221993002 CAPITAL TRUST AGENCY SENIOR HOUSING REVENUEBONDS (BEACH HOUSE AT WIREGRASS RANCH PROJECT) SERIES 2016A AND TAXABLE 2016B B INTEREST ACCOUNT

This statement is for the period from August 1, 2017 to August 31, 2017

SPECIAL MESSAGES

Faster trade settlement begins September 5

To better meet the needs of all investors, the financial services industry is shortening the settlement cycle for stocks, corporate bonds, municipal bonds, unit investment trusts and financial products comprised of these security types (such as exchange-traded funds). The standard settlement cycle of three business days after the trade date will be changed to two business days on September 5, 2017.





00- -M -N -PC -244-01 00376601 3766 0183418-00-03300-01 Page 3 of 6

ACCOUNT NUMBER: 221993002
CAPITAL TRUST AGENCY SENIOR HOUSING
REVENUEBONDS (BEACH HOUSE AT
WIREGRASS RANCH PROJECT) SERIES
2016A AND TAXABLE 2016B
B INTEREST ACCOUNT

MARKET VALUE SUMMARY					
	Current Period 08/01/17 to 08/31/17				
Beginning Market Value	\$86.88				
Contributions	7.36				
Adjusted Market Value	\$94.24				
Investment Results					
Interest, Dividends and Other Income	0.01				
Total Investment Results	\$0.01				
Ending Market Value	\$94.25				



00- -M -N -PC -244-01 00376601 3766 0183418-00-03300-01 Page 4 of 6

ACCOUNT NUMBER: 221993002 CAPITAL TRUST AGENCY SENIOR HOUSING REVENUEBONDS (BEACH HOUSE AT WIREGRASS RANCH PROJECT) SERIES 2016A AND TAXABLE 2016B B INTEREST ACCOUNT

This statement is for the period from August 1, 2017 to August 31, 2017

ASSET DETAIL AS OF 08/31/17						
Shares or Face Amount	Security Description	Market Value/ Price	Tax Cost/ Unit Cost	% of Total Yield at Market	Est Ann Inc	
Cash Equ	ivalents					
94.250	US Bank Mmkt 5 - Ct 9AMMF05B2	94.25 1.0000	94.25 1.00	100.0 .20 *	0.19	
Total Cas	h Equivalents	\$94.25	\$94.25	100.0	\$.19	
Total As	sets	\$94.25	\$94.25	100.0	\$.19	

ASSET DETAIL MESSAGES

Time of trade execution and trading party (if not disclosed) will be provided upon request.

Publicly traded assets are valued in accordance with market quotations or valuation methodologies from financial industry services believed by us to be reliable. Assets that are not publicly traded may be reflected at values from other external sources. Assets for which a current value is not available may be reflected at a previous value or as not valued, at par value, or at a nominal value. Values shown do not necessarily reflect prices at which assets could be bought or sold. Values are updated based on internal policy and may be updated less frequently than statement generation.

For further information, please contact your Analyst.

** The Yield at Market set forth in this statement for any money market fund is based on the interest rate applicable to that money market fund as of the last business day of the statement period (or most recent daily rate available) and may not be relied upon as (i) a yield estimate for the statement period as a whole, or (ii) a guarantee of future performance.





00- -M -N -PC -244-01 00376601 3766 0183418-00-03300-01 Page 5 of 6

ACCOUNT NUMBER: 221993002
CAPITAL TRUST AGENCY SENIOR HOUSING
REVENUEBONDS (BEACH HOUSE AT
WIREGRASS RANCH PROJECT) SERIES
2016A AND TAXABLE 2016B
B INTEREST ACCOUNT

This statement is for the period from August 1, 2017 to August 31, 2017

CASH SUMMARY

	Income Cash	Principal Cash	Total Cash
Beginning Cash Balance as of 08/01/2017	\$.00	\$.00	\$.00
Taxable Interest	0.01		0.01
Cash Receipts		7.36	7.36
Transfers	- 0.01	0.01	
Net Money Market Activity		- 7.37	- 7.37
Ending Cash Balance as of 08/31/2017	\$0.00	\$0.00	\$0.00



 $\begin{array}{cccc} \text{00--M-N-PC-}244\text{-}01 & \text{00376601} & 3766 \\ \text{0183418-}00\text{-}03300\text{-}01 & \text{Page 6 of 6} \end{array}$

ACCOUNT NUMBER: 221993002
CAPITAL TRUST AGENCY SENIOR HOUSING
REVENUEBONDS (BEACH HOUSE AT
WIREGRASS RANCH PROJECT) SERIES
2016A AND TAXABLE 2016B
B INTEREST ACCOUNT

	TRANS	ACTION DETAIL		
Date Posted	Description	Income Cash	Principal Cash	Tax Cost
	Beginning Balance 08/01/2017	\$.00	\$.00	\$86.88
08/01/17	Interest Earned On US Bank Mmkt 5 - Ct Interest From 7/1/17 To 7/31/17 9AMMF05B2	0.01		
08/02/17	Cash Disbursement Transfer To Principal Income Earnings	- 0.01		
08/02/17	Cash Receipt Transfer From Income Income Earnings		0.01	
08/02/17	Cash Receipt Transfer From Another Trust Paid From Account # 221993010 Income Earnings		6.67	
08/02/17	Cash Receipt Transfer From Another Trust Paid From Account # 221993014 Income Earnings		0.69	
08/02/17	Purchased 7.37 Units Of US Bank Mmkt 5 - Ct Trade Date 8/2/17 9AMMF05B2		- 7.37	7.37
	Ending Balance 08/31/2017	\$0.00	\$0.00	\$94.25





PSL WIREGRASS LP ATTN DODD CRUTCHER 8214 WESTCHESTERDR SUITE 600 DALLAS TX 75225-6112 00- -M -N -PC -244-01 0183420-00-03300-01 3766 Page 1 of 4

ACCOUNT NUMBER: 221993003 CAPITAL TRUST AGENCY SENIOR HOUSING REVENUEBONDS (BEACH HOUSE AT WIREGRASS RANCH PROJECT) SERIES 2016A AND TAXABLE 2016B B PRINCIPAL ACCOUNT

This statement is for the period from August 1, 2017 to August 31, 2017

QUESTIONS?

If you have any questions regarding your account or this statement, please contact your Account Manager or Analyst.

Account Manager:
SHERYL LEAR
EX-FL-WWSJ
225 E. ROBINSON ST., SUITE 250
ORLANDO, FL 32801
Phone 904-358-5363
E-mail SHERYL.LEAR@USBANK.COM



00- -M -N -PC -244-01 00376601 3766 0183420-00-03300-01 Page 2 of 4

ACCOUNT NUMBER: 221993003 CAPITAL TRUST AGENCY SENIOR HOUSING REVENUEBONDS (BEACH HOUSE AT WIREGRASS RANCH PROJECT) SERIES 2016A AND TAXABLE 2016B B PRINCIPAL ACCOUNT

This statement is for the period from August 1, 2017 to August 31, 2017

SPECIAL MESSAGES

Faster trade settlement begins September 5

To better meet the needs of all investors, the financial services industry is shortening the settlement cycle for stocks, corporate bonds, municipal bonds, unit investment trusts and financial products comprised of these security types (such as exchange-traded funds). The standard settlement cycle of three business days after the trade date will be changed to two business days on September 5, 2017.





00- -M -N -PC -244-01 00376601 3766 0183420-00-03300-01 Page 3 of 4

ACCOUNT NUMBER: 221993003
CAPITAL TRUST AGENCY SENIOR HOUSING
REVENUEBONDS (BEACH HOUSE AT
WIREGRASS RANCH PROJECT) SERIES
2016A AND TAXABLE 2016B
B PRINCIPAL ACCOUNT

This statement is for the period from August 1, 2017 to August 31, 2017

MARKET VALUE SUMMARY				
	Current Period 08/01/17 to 08/31/17			
Beginning Market Value	\$0.00			
Ending Market Value	\$0.00			
MARKET	VALUE SUMMARY MESSAGES			

No activity qualifies for this statement period.



00- -M -N -PC -244-01 00376601 3766 0183420-00-03300-01 Page 4 of 4

ACCOUNT NUMBER: 221993003 CAPITAL TRUST AGENCY SENIOR HOUSING REVENUEBONDS (BEACH HOUSE AT WIREGRASS RANCH PROJECT) SERIES 2016A AND TAXABLE 2016B B PRINCIPAL ACCOUNT

This statement is for the period from August 1, 2017 to August 31, 2017

ASSET DETAIL MESSAGES

No reportable securities for this statement period





PSL WIREGRASS LP ATTN DODD CRUTCHER 8214 WESTCHESTERDR SUITE 600 DALLAS TX 75225-6112 00- -M -N -PC -244-01 0183422-00-03300-01 3766 Page 1 of 5

ACCOUNT NUMBER: 221993004 CAPITAL TRUST AGENCY SENIOR HOUSING REVENUEBONDS (BEACH HOUSE AT WIREGRASS RANCH PROJECT) SERIES 2016A AND TAXABLE 2016B REVENUEFUND

This statement is for the period from August 1, 2017 to August 31, 2017

QUESTIONS?

If you have any questions regarding your account or this statement, please contact your Account Manager or Analyst.

Account Manager:
SHERYL LEAR
EX-FL-WWSJ
225 E. ROBINSON ST., SUITE 250
ORLANDO, FL 32801
Phone 904-358-5363
E-mail SHERYL.LEAR@USBANK.COM



00- -M -N -PC -244-01 00376601 3766 0183422-00-03300-01 Page 2 of 5

ACCOUNT NUMBER: 221993004
CAPITAL TRUST AGENCY SENIOR HOUSING
REVENUEBONDS (BEACH HOUSE AT
WIREGRASS RANCH PROJECT) SERIES
2016A AND TAXABLE 2016B
REVENUEFUND

This statement is for the period from August 1, 2017 to August 31, 2017

SPECIAL MESSAGES

Faster trade settlement begins September 5

To better meet the needs of all investors, the financial services industry is shortening the settlement cycle for stocks, corporate bonds, municipal bonds, unit investment trusts and financial products comprised of these security types (such as exchange-traded funds). The standard settlement cycle of three business days after the trade date will be changed to two business days on September 5, 2017.





00- -M -N -PC -244-01 00376601 3766 0183422-00-03300-01 Page 3 of 5

ACCOUNT NUMBER: 221993004
CAPITAL TRUST AGENCY SENIOR HOUSING
REVENUEBONDS (BEACH HOUSE AT
WIREGRASS RANCH PROJECT) SERIES
2016A AND TAXABLE 2016B
REVENUEFUND

This statement is for the period from August 1, 2017 to August 31, 2017

	MARKET VALUE SUMMARY	
	Current Period 08/01/17 to 08/31/17	
Beginning Market Value	\$0.00	
Ending Market Value	\$0.00	
M	ARKET VALUE SUMMARY MESSA	GES

No activity qualifies for this statement period.



00- -M -N -PC -244-01 00376601 3766 0183422-00-03300-01 Page 4 of 5

ACCOUNT NUMBER: 221993004 CAPITAL TRUST AGENCY SENIOR HOUSING REVENUEBONDS (BEACH HOUSE AT WIREGRASS RANCH PROJECT) SERIES 2016A AND TAXABLE 2016B REVENUEFUND

This statement is for the period from August 1, 2017 to August 31, 2017

ASSET DETAIL AS OF 08/31/17						
Shares or Face Amount	Security Description	Market Value/ Price	Tax Cost/ Unit Cost	% of Total Yield at Market	Est Ann Inc	
Miscellan	eous					
1.000	Psl Wiregrass LP Series 2016A Note \$21,710,000 97MSCJZ82	0.00 0.0000	1.00 1.00	.00	0.00	
1.000	Psl Wiregrass LP Series 2016B Note \$1,040,000 97MSCJZ90	0.00 0.0000	1.00 1.00	0.0 .00	0.00	
Total Mis	cellaneous	\$0.00	\$2.00	0.0		
Total As	sets	\$0.00	\$2.00	0.0		

ASSET DETAIL MESSAGES

Time of trade execution and trading party (if not disclosed) will be provided upon request.

Publicly traded assets are valued in accordance with market quotations or valuation methodologies from financial industry services believed by us to be reliable. Assets that are not publicly traded may be reflected at values from other external sources. Assets for which a current value is not available may be reflected at a previous value or as not valued, at par value, or at a nominal value. Values shown do not necessarily reflect prices at which assets could be bought or sold. Values are updated based on internal policy and may be updated less frequently than statement generation.

For further information, please contact your Analyst.





 $\begin{array}{cccc} \text{00--M-N-PC-}244\text{-}01 & \text{00376601} & 3766 \\ \text{0183422-}00\text{-}03300\text{-}01 & \text{Page 5 of 5} \end{array}$

ACCOUNT NUMBER: 221993004
CAPITAL TRUST AGENCY SENIOR HOUSING
REVENUEBONDS (BEACH HOUSE AT
WIREGRASS RANCH PROJECT) SERIES
2016A AND TAXABLE 2016B
REVENUEFUND

TRANSACTION DETAIL					
Date Posted	Description	Income Cash	Principal Cash	Tax Cost	
	Beginning Balance 08/01/2017	\$.00	\$.00	\$2.00	
	Ending Balance 08/31/2017	\$0.00	\$0.00	\$2.00	





PSL WIREGRASS LP ATTN DODD CRUTCHER 8214 WESTCHESTERDR SUITE 600 DALLAS TX 75225-6112 00- -M -N -PC -244-01 0183424-00-03300-01

3766 Page 1 of 6

ACCOUNT NUMBER: 221993005 CAPITAL TRUST AGENCY SENIOR HOUSING REVENUEBONDS (BEACH HOUSE AT WIREGRASS RANCH PROJECT) SERIES 2016A AND TAXABLE 2016B A CONSTRUCTION ACCOUNT

This statement is for the period from August 1, 2017 to August 31, 2017

QUESTIONS?

If you have any questions regarding your account or this statement, please contact your Account Manager or Analyst.

Account Manager:
SHERYL LEAR
EX-FL-WWSJ
225 E. ROBINSON ST., SUITE 250
ORLANDO, FL 32801
Phone 904-358-5363
E-mail SHERYL.LEAR@USBANK.COM



00- -M -N -PC -244-01 00376601 3766 0183424-00-03300-01 Page 2 of 6

ACCOUNT NUMBER: 221993005 CAPITAL TRUST AGENCY SENIOR HOUSING REVENUEBONDS (BEACH HOUSE AT WIREGRASS RANCH PROJECT) SERIES 2016A AND TAXABLE 2016B A CONSTRUCTION ACCOUNT

This statement is for the period from August 1, 2017 to August 31, 2017

SPECIAL MESSAGES

Faster trade settlement begins September 5

To better meet the needs of all investors, the financial services industry is shortening the settlement cycle for stocks, corporate bonds, municipal bonds, unit investment trusts and financial products comprised of these security types (such as exchange-traded funds). The standard settlement cycle of three business days after the trade date will be changed to two business days on September 5, 2017.





00- -M -N -PC -244-01 00376601 3766 0183424-00-03300-01 Page 3 of 6

ACCOUNT NUMBER: 221993005
CAPITAL TRUST AGENCY SENIOR HOUSING
REVENUEBONDS (BEACH HOUSE AT
WIREGRASS RANCH PROJECT) SERIES
2016A AND TAXABLE 2016B
A CONSTRUCTION ACCOUNT

MARKET VALUE SUMMARY				
	Current Period 08/01/17 to 08/31/17			
Beginning Market Value	\$8,568,368.05			
Distributions	- 1,233,160.28			
Adjusted Market Value	\$7,335,207.77			
Investment Results				
Interest, Dividends and Other Income	1,603.19			
Total Investment Results	\$1,603.19			
Ending Market Value	\$7,336,810.96			



00- -M -N -PC -244-01 00376601 3766 0183424-00-03300-01 Page 4 of 6

ACCOUNT NUMBER: 221993005 CAPITAL TRUST AGENCY SENIOR HOUSING REVENUEBONDS (BEACH HOUSE AT WIREGRASS RANCH PROJECT) SERIES 2016A AND TAXABLE 2016B A CONSTRUCTION ACCOUNT

This statement is for the period from August 1, 2017 to August 31, 2017

ASSET DETAIL AS OF 08/31/17					
Shares or Face Amount	Security Description	Market Value/ Price	Tax Cost/ Unit Cost	% of Total Yield at Market	Est Ann Inc
Cash Equi	valents				
7,336,810.960	US Bank Mmkt 5 - Ct 9AMMF05B2	7,336,810.96 1.0000	7,336,810.96 1.00	100.0 .20 *	14,673.62
Total Cash	n Equivalents	\$7,336,810.96	\$7,336,810.96	100.0	\$14,673.62
Total Ass	sets	\$7,336,810.96	\$7,336,810.96	100.0	\$14,673.62

ASSET DETAIL MESSAGES

Time of trade execution and trading party (if not disclosed) will be provided upon request.

Publicly traded assets are valued in accordance with market quotations or valuation methodologies from financial industry services believed by us to be reliable. Assets that are not publicly traded may be reflected at values from other external sources. Assets for which a current value is not available may be reflected at a previous value or as not valued, at par value, or at a nominal value. Values shown do not necessarily reflect prices at which assets could be bought or sold. Values are updated based on internal policy and may be updated less frequently than statement generation.

For further information, please contact your Analyst.

** The Yield at Market set forth in this statement for any money market fund is based on the interest rate applicable to that money market fund as of the last business day of the statement period (or most recent daily rate available) and may not be relied upon as (i) a yield estimate for the statement period as a whole, or (ii) a guarantee of future performance.





00- -M -N -PC -244-01 00376601 3766 0183424-00-03300-01 Page 5 of 6

ACCOUNT NUMBER: 221993005
CAPITAL TRUST AGENCY SENIOR HOUSING
REVENUEBONDS (BEACH HOUSE AT
WIREGRASS RANCH PROJECT) SERIES
2016A AND TAXABLE 2016B
A CONSTRUCTION ACCOUNT

This statement is for the period from August 1, 2017 to August 31, 2017

CASH SUMMARY

	Income Cash	Principal Cash	Total Cash
Beginning Cash Balance as of 08/01/2017	\$.00	\$.00	\$.00
Taxable Interest	1,603.19		1,603.19
Cash Disbursements	- 1,603.19	- 1,231,557.09	- 1,233,160.28
Net Money Market Activity		1,231,557.09	1,231,557.09
Ending Cash Balance as of 08/31/2017	\$0.00	\$0.00	\$0.00



00- -M -N -PC -244-01 00376601 3766 0183424-00-03300-01 Page 6 of 6

ACCOUNT NUMBER: 221993005
CAPITAL TRUST AGENCY SENIOR HOUSING
REVENUEBONDS (BEACH HOUSE AT
WIREGRASS RANCH PROJECT) SERIES
2016A AND TAXABLE 2016B
A CONSTRUCTION ACCOUNT

	TRAN	SACTION DETAIL		
Date Posted	Description	Income Cash	Principal Cash	Tax Cost
	Beginning Balance 08/01/2017	\$.00	\$.00	\$8,568,368.05
08/01/17	Interest Earned On US Bank Mmkt 5 - Ct Interest From 7/1/17 To 7/31/17 9AMMF05B2	1,603.19		
08/02/17	Cash Disbursement Paid To Account # 221993000 Transfer To Another Trust Income Earnings	- 1,603.19		
08/28/17	Cash Disbursement Paid To Douglas Company Wire Transfer Wire To Douglas Company Per Requsition 11 Mtlewi3		- 1,164,263.00	
08/28/17	Cash Disbursement Paid To Psl Wiregrass Wire Transfer Wire To Psl Wiregrass Per Requsition 11 Mtlewi3		- 67,294.09	
08/28/17	Sold 1,231,557.09 Units Of US Bank Mmkt 5 - Ct Trade Date 8/28/17 9AMMF05B2		1,231,557.09	- 1,231,557.09
	Ending Balance 08/31/2017	\$0.00	\$0.00	\$7,336,810.96





PSL WIREGRASS LP ATTN DODD CRUTCHER 8214 WESTCHESTERDR SUITE 600 DALLAS TX 75225-6112 00- -M -N -PC -244-01 0183426-00-03300-01 3766 Page 1 of 6

ACCOUNT NUMBER: 221993006 CAPITAL TRUST AGENCY SENIOR HOUSING REVENUEBONDS (BEACH HOUSE AT WIREGRASS RANCH PROJECT) SERIES 2016A AND TAXABLE 2016B WORKING CAPITAL FUND

This statement is for the period from August 1, 2017 to August 31, 2017

QUESTIONS?

If you have any questions regarding your account or this statement, please contact your Account Manager or Analyst.

Account Manager:
SHERYL LEAR
EX-FL-WWSJ
225 E. ROBINSON ST., SUITE 250
ORLANDO, FL 32801
Phone 904-358-5363
E-mail SHERYL.LEAR@USBANK.COM



00- -M -N -PC -244-01 00376601 3766 0183426-00-03300-01 Page 2 of 6

ACCOUNT NUMBER: 221993006 CAPITAL TRUST AGENCY SENIOR HOUSING REVENUEBONDS (BEACH HOUSE AT WIREGRASS RANCH PROJECT) SERIES 2016A AND TAXABLE 2016B WORKING CAPITAL FUND

This statement is for the period from August 1, 2017 to August 31, 2017

SPECIAL MESSAGES

Faster trade settlement begins September 5

To better meet the needs of all investors, the financial services industry is shortening the settlement cycle for stocks, corporate bonds, municipal bonds, unit investment trusts and financial products comprised of these security types (such as exchange-traded funds). The standard settlement cycle of three business days after the trade date will be changed to two business days on September 5, 2017.





00- -M -N -PC -244-01 00376601 3766 0183426-00-03300-01 Page 3 of 6

ACCOUNT NUMBER: 221993006
CAPITAL TRUST AGENCY SENIOR HOUSING
REVENUEBONDS (BEACH HOUSE AT
WIREGRASS RANCH PROJECT) SERIES
2016A AND TAXABLE 2016B
WORKING CAPITAL FUND

MARKET	VALUE SUMMARY	
	Current Period 08/01/17 to 08/31/17	
Beginning Market Value	\$1,220,189.64	
Distributions	- 20,000.00	
Adjusted Market Value	\$1,200,189.64	
Investment Results		
Interest, Dividends and Other Income	210.15	
Total Investment Results	\$210.15	
Ending Market Value	\$1,200,399.79	



00- -M -N -PC -244-01 00376601 3766 0183426-00-03300-01 Page 4 of 6

ACCOUNT NUMBER: 221993006 CAPITAL TRUST AGENCY SENIOR HOUSING REVENUEBONDS (BEACH HOUSE AT WIREGRASS RANCH PROJECT) SERIES 2016A AND TAXABLE 2016B WORKING CAPITAL FUND

This statement is for the period from August 1, 2017 to August 31, 2017

ASSET DETAIL AS OF 08/31/17					
Shares or Face Amount	Security Description	Market Value/ Price	Tax Cost/ Unit Cost	% of Total Yield at Market	Est Ann Inc
Cash Equi	valents				
1,200,399.790	US Bank Mmkt 5 - Ct 9AMMF05B2	1,200,399.79 1.0000	1,200,399.79 1.00	100.0 .20 *	2,400.80
Total Cash	n Equivalents	\$1,200,399.79	\$1,200,399.79	100.0	\$2,400.80
Total Ass	sets	\$1,200,399.79	\$1,200,399.79	100.0	\$2,400.80

ASSET DETAIL MESSAGES

Time of trade execution and trading party (if not disclosed) will be provided upon request.

Publicly traded assets are valued in accordance with market quotations or valuation methodologies from financial industry services believed by us to be reliable. Assets that are not publicly traded may be reflected at values from other external sources. Assets for which a current value is not available may be reflected at a previous value or as not valued, at par value, or at a nominal value. Values shown do not necessarily reflect prices at which assets could be bought or sold. Values are updated based on internal policy and may be updated less frequently than statement generation.

For further information, please contact your Analyst.

** The Yield at Market set forth in this statement for any money market fund is based on the interest rate applicable to that money market fund as of the last business day of the statement period (or most recent daily rate available) and may not be relied upon as (i) a yield estimate for the statement period as a whole, or (ii) a guarantee of future performance.





00- -M -N -PC -244-01 00376601 3766 0183426-00-03300-01 Page 5 of 6

ACCOUNT NUMBER: 221993006
CAPITAL TRUST AGENCY SENIOR HOUSING
REVENUEBONDS (BEACH HOUSE AT
WIREGRASS RANCH PROJECT) SERIES
2016A AND TAXABLE 2016B
WORKING CAPITAL FUND

This statement is for the period from August 1, 2017 to August 31, 2017

CASH SUMMARY

	Income Cash	Principal Cash	Total Cash
Beginning Cash Balance as of 08/01/2017	\$.00	\$.00	\$.00
Taxable Interest	210.15		210.15
Cash Disbursements		- 20,000.00	- 20,000.00
Transfers	- 210.15	210.15	
Net Money Market Activity		19,789.85	19,789.85
Ending Cash Balance as of 08/31/2017	\$0.00	\$0.00	\$0.00



ACCOUNT NUMBER: 221993006
CAPITAL TRUST AGENCY SENIOR HOUSING
REVENUEBONDS (BEACH HOUSE AT
WIREGRASS RANCH PROJECT) SERIES
2016A AND TAXABLE 2016B
WORKING CAPITAL FUND

This statement is for the period from August 1, 2017 to August 31, 2017

	TRANS	SACTION DETAIL		
Date Posted	Description	Income Cash	Principal Cash	Tax Cost
	Beginning Balance 08/01/2017	\$.00	\$.00	\$1,220,189.64
08/01/17	Interest Earned On US Bank Mmkt 5 - Ct Interest From 7/1/17 To 7/31/17 9AMMF05B2	210.15		
08/02/17	Cash Disbursement Transfer To Principal Income Earnings	- 210.15		
08/02/17	Cash Receipt Transfer From Income Income Earnings		210.15	
08/02/17	Purchased 210.15 Units Of US Bank Mmkt 5 - Ct Trade Date 8/2/17 9AMMF05B2		- 210.15	210.15
08/24/17	Cash Disbursement Paid To Psl Wiregrass LP Wire Transfer Wire For Work Cap 4 Mtlewi3		- 20,000.00	
08/24/17	Sold 20,000 Units Of US Bank Mmkt 5 - Ct Trade Date 8/24/17 9AMMF05B2		20,000.00	- 20,000.00
	Ending Balance 08/31/2017	\$0.00	\$0.00	\$1,200,399.79





PSL WIREGRASS LP ATTN DODD CRUTCHER 8214 WESTCHESTERDR SUITE 600 DALLAS TX 75225-6112 00- -M -N -PC -244-01 0183428-00-03300-01 3766 Page 1 of 4

ACCOUNT NUMBER: 221993007 CAPITAL TRUST AGENCY SENIOR HOUSING REVENUEBONDS (BEACH HOUSE AT WIREGRASS RANCH PROJECT) SERIES 2016A AND TAXABLE 2016B REPAIR AND REPLACEMENTFUND

This statement is for the period from August 1, 2017 to August 31, 2017

QUESTIONS?

If you have any questions regarding your account or this statement, please contact your Account Manager or Analyst.

Account Manager:
SHERYL LEAR
EX-FL-WWSJ
225 E. ROBINSON ST., SUITE 250
ORLANDO, FL 32801
Phone 904-358-5363
E-mail SHERYL.LEAR@USBANK.COM

Analyst: KEVIN FOX Phone 704-335-4588



00- -M -N -PC -244-01 00376601 3766 0183428-00-03300-01 Page 2 of 4

ACCOUNT NUMBER: 221993007 CAPITAL TRUST AGENCY SENIOR HOUSING REVENUEBONDS (BEACH HOUSE AT WIREGRASS RANCH PROJECT) SERIES 2016A AND TAXABLE 2016B REPAIR AND REPLACEMENTFUND

This statement is for the period from August 1, 2017 to August 31, 2017

SPECIAL MESSAGES

Faster trade settlement begins September 5

To better meet the needs of all investors, the financial services industry is shortening the settlement cycle for stocks, corporate bonds, municipal bonds, unit investment trusts and financial products comprised of these security types (such as exchange-traded funds). The standard settlement cycle of three business days after the trade date will be changed to two business days on September 5, 2017.

This should result in reduced credit risk, cash deployment efficiencies, increased market liquidity and lower collateral requirements. It also will align the U.S. market with other major international markets. For example, 23 European Union members moved to a two-day settlement cycle in October 2014. U.S. Bank has been participating in industry-wide testing to ensure readiness for the shortened settlement cycle.





00- -M -N -PC -244-01 00376601 3766 0183428-00-03300-01 Page 3 of 4

ACCOUNT NUMBER: 221993007
CAPITAL TRUST AGENCY SENIOR HOUSING
REVENUEBONDS (BEACH HOUSE AT
WIREGRASS RANCH PROJECT) SERIES
2016A AND TAXABLE 2016B
REPAIR AND REPLACEMENTFUND

This statement is for the period from August 1, 2017 to August 31, 2017

rent Period to 08/31/17
10 00/01/11
\$0.00
\$0.00

No activity qualifies for this statement period.



00- -M -N -PC -244-01 00376601 3766 0183428-00-03300-01 Page 4 of 4

ACCOUNT NUMBER: 221993007 CAPITAL TRUST AGENCY SENIOR HOUSING REVENUEBONDS (BEACH HOUSE AT WIREGRASS RANCH PROJECT) SERIES 2016A AND TAXABLE 2016B REPAIR AND REPLACEMENTFUND

This statement is for the period from August 1, 2017 to August 31, 2017

ASSET DETAIL MESSAGES

No reportable securities for this statement period





PSL WIREGRASS LP ATTN DODD CRUTCHER 8214 WESTCHESTERDR SUITE 600 DALLAS TX 75225-6112 00- -M -N -PC -244-01 0183430-00-03300-01 3766 Page 1 of 4

ACCOUNT NUMBER: 221993008
CAPITAL TRUST AGENCY SENIOR HOUSING
REVENUEBONDS (BEACH HOUSE AT
WIREGRASS RANCH PROJECT) SERIES
2016A AND TAXABLE 2016B
INSURANCE AND TAX ESCROW FUND

This statement is for the period from August 1, 2017 to August 31, 2017

QUESTIONS?

If you have any questions regarding your account or this statement, please contact your Account Manager or Analyst.

Account Manager:
SHERYL LEAR
EX-FL-WWSJ
225 E. ROBINSON ST., SUITE 250
ORLANDO, FL 32801
Phone 904-358-5363
E-mail SHERYL.LEAR@USBANK.COM

Analyst: KEVIN FOX Phone 704-335-4588



00- -M -N -PC -244-01 00376601 3766 0183430-00-03300-01 Page 2 of 4

ACCOUNT NUMBER: 221993008
CAPITAL TRUST AGENCY SENIOR HOUSING
REVENUEBONDS (BEACH HOUSE AT
WIREGRASS RANCH PROJECT) SERIES
2016A AND TAXABLE 2016B
INSURANCE AND TAX ESCROW FUND

This statement is for the period from August 1, 2017 to August 31, 2017

SPECIAL MESSAGES

Faster trade settlement begins September 5

To better meet the needs of all investors, the financial services industry is shortening the settlement cycle for stocks, corporate bonds, municipal bonds, unit investment trusts and financial products comprised of these security types (such as exchange-traded funds). The standard settlement cycle of three business days after the trade date will be changed to two business days on September 5, 2017.

This should result in reduced credit risk, cash deployment efficiencies, increased market liquidity and lower collateral requirements. It also will align the U.S. market with other major international markets. For example, 23 European Union members moved to a two-day settlement cycle in October 2014. U.S. Bank has been participating in industry-wide testing to ensure readiness for the shortened settlement cycle.





00- -M -N -PC -244-01 00376601 3766 0183430-00-03300-01 Page 3 of 4

ACCOUNT NUMBER: 221993008
CAPITAL TRUST AGENCY SENIOR HOUSING
REVENUEBONDS (BEACH HOUSE AT
WIREGRASS RANCH PROJECT) SERIES
2016A AND TAXABLE 2016B
INSURANCE AND TAX ESCROW FUND

This statement is for the period from August 1, 2017 to August 31, 2017

	MARKET VALUE SUMMARY	
	Current Period 08/01/17 to 08/31/17	
Beginning Market Value	\$0.00	
Ending Market Value	\$0.00	

No activity qualifies for this statement period.



00- -M -N -PC -244-01 00376601 3766 0183430-00-03300-01 Page 4 of 4

ACCOUNT NUMBER: 221993008
CAPITAL TRUST AGENCY SENIOR HOUSING
REVENUEBONDS (BEACH HOUSE AT
WIREGRASS RANCH PROJECT) SERIES
2016A AND TAXABLE 2016B
INSURANCE AND TAX ESCROW FUND

This statement is for the period from August 1, 2017 to August 31, 2017

ASSET DETAIL MESSAGES

No reportable securities for this statement period





PSL WIREGRASS LP ATTN DODD CRUTCHER 8214 WESTCHESTERDR SUITE 600 DALLAS TX 75225-6112 00- -M -N -PC -244-01 0183432-00-03300-01 3766 Page 1 of 6

ACCOUNT NUMBER: 221993009
CAPITAL TRUST AGENCY SENIOR HOUSING
REVENUEBONDS (BEACH HOUSE AT
WIREGRASS RANCH PROJECT) SERIES
2016A AND TAXABLE 2016B
A CAPITALIZED INTEREST ACCOUNT

This statement is for the period from August 1, 2017 to August 31, 2017

QUESTIONS?

If you have any questions regarding your account or this statement, please contact your Account Manager or Analyst.

Account Manager:
SHERYL LEAR
EX-FL-WWSJ
225 E. ROBINSON ST., SUITE 250
ORLANDO, FL 32801
Phone 904-358-5363
E-mail SHERYL.LEAR@USBANK.COM

Analyst: KEVIN FOX Phone 704-335-4588



00- -M -N -PC -244-01 00376601 3766 0183432-00-03300-01 Page 2 of 6

ACCOUNT NUMBER: 221993009
CAPITAL TRUST AGENCY SENIOR HOUSING
REVENUEBONDS (BEACH HOUSE AT
WIREGRASS RANCH PROJECT) SERIES
2016A AND TAXABLE 2016B
A CAPITALIZED INTEREST ACCOUNT

This statement is for the period from August 1, 2017 to August 31, 2017

SPECIAL MESSAGES

Faster trade settlement begins September 5

To better meet the needs of all investors, the financial services industry is shortening the settlement cycle for stocks, corporate bonds, municipal bonds, unit investment trusts and financial products comprised of these security types (such as exchange-traded funds). The standard settlement cycle of three business days after the trade date will be changed to two business days on September 5, 2017.

This should result in reduced credit risk, cash deployment efficiencies, increased market liquidity and lower collateral requirements. It also will align the U.S. market with other major international markets. For example, 23 European Union members moved to a two-day settlement cycle in October 2014. U.S. Bank has been participating in industry-wide testing to ensure readiness for the shortened settlement cycle.





00- -M -N -PC -244-01 00376601 3766 0183432-00-03300-01 Page 3 of 6

ACCOUNT NUMBER: 221993009
CAPITAL TRUST AGENCY SENIOR HOUSING
REVENUEBONDS (BEACH HOUSE AT
WIREGRASS RANCH PROJECT) SERIES
2016A AND TAXABLE 2016B
A CAPITALIZED INTEREST ACCOUNT

This statement is for the period from August 1, 2017 to August 31, 2017

MARKET VALUE SUMMARY				
	Current Period 08/01/17 to 08/31/17			
Beginning Market Value	\$577,727.22			
Distributions	- 101.11			
Adjusted Market Value	\$577,626.11			
Investment Results				
Interest, Dividends and Other Income	101.11			
Total Investment Results	\$101.11			
Ending Market Value	\$577,727.22			



00- -M -N -PC -244-01 00376601 3766 0183432-00-03300-01 Page 4 of 6

ACCOUNT NUMBER: 221993009
CAPITAL TRUST AGENCY SENIOR HOUSING
REVENUEBONDS (BEACH HOUSE AT
WIREGRASS RANCH PROJECT) SERIES
2016A AND TAXABLE 2016B
A CAPITALIZED INTEREST ACCOUNT

This statement is for the period from August 1, 2017 to August 31, 2017

ASSET DETAIL AS OF 08/31/17					
Shares or Face Amount	Security Description	Market Value/ Price	Tax Cost/ Unit Cost	% of Total Yield at Market	Est Ann Inc
Cash Equ	ivalents				
577,727.220	US Bank Mmkt 5 - Ct 9AMMF05B2	577,727.22 1.0000	577,727.22 1.00	100.0 .20 *	1,155.45 *
Total Casl	n Equivalents	\$577,727.22	\$577,727.22	100.0	\$1,155.45
Total Ass	sets	\$577,727.22	\$577,727.22	100.0	\$1,155.45

ASSET DETAIL MESSAGES

Time of trade execution and trading party (if not disclosed) will be provided upon request.

Publicly traded assets are valued in accordance with market quotations or valuation methodologies from financial industry services believed by us to be reliable. Assets that are not publicly traded may be reflected at values from other external sources. Assets for which a current value is not available may be reflected at a previous value or as not valued, at par value, or at a nominal value. Values shown do not necessarily reflect prices at which assets could be bought or sold. Values are updated based on internal policy and may be updated less frequently than statement generation.

For further information, please contact your Analyst.

** The Yield at Market set forth in this statement for any money market fund is based on the interest rate applicable to that money market fund as of the last business day of the statement period (or most recent daily rate available) and may not be relied upon as (i) a yield estimate for the statement period as a whole, or (ii) a guarantee of future performance.





00- -M -N -PC -244-01 00376601 3766 0183432-00-03300-01 Page 5 of 6

ACCOUNT NUMBER: 221993009
CAPITAL TRUST AGENCY SENIOR HOUSING
REVENUEBONDS (BEACH HOUSE AT
WIREGRASS RANCH PROJECT) SERIES
2016A AND TAXABLE 2016B
A CAPITALIZED INTEREST ACCOUNT

This statement is for the period from August 1, 2017 to August 31, 2017

CASH SUMMARY

	Income Cash	Principal Cash	Total Cash
Beginning Cash Balance as of 08/01/2017	\$.00	\$.00	\$.00
Taxable Interest	101.11		101.11
Cash Disbursements	- 101.11		- 101.11
Ending Cash Balance as of 08/31/2017	\$0.00	\$0.00	\$0.00



00- -M -N -PC -244-01 00376601 3766 0183432-00-03300-01 Page 6 of 6

ACCOUNT NUMBER: 221993009
CAPITAL TRUST AGENCY SENIOR HOUSING
REVENUEBONDS (BEACH HOUSE AT
WIREGRASS RANCH PROJECT) SERIES
2016A AND TAXABLE 2016B
A CAPITALIZED INTEREST ACCOUNT

This statement is for the period from August 1, 2017 to August 31, 2017

	TRANSACTION DETAIL				
Date Posted	Description	Income Cash	Principal Cash	Tax Cost	
	Beginning Balance 08/01/2017	\$.00	\$.00	\$577,727.22	
08/01/17	Interest Earned On US Bank Mmkt 5 - Ct Interest From 7/1/17 To 7/31/17 9AMMF05B2	101.11			
08/02/17	Cash Disbursement Paid To Account # 221993000 Transfer To Another Trust Income Earnings	- 101.11			
	Ending Balance 08/31/2017	\$0.00	\$0.00	\$577,727.22	





PSL WIREGRASS LP ATTN DODD CRUTCHER 8214 WESTCHESTERDR SUITE 600 DALLAS TX 75225-6112 00- -M -N -PC -244-01 0183434-00-03300-01

3766 Page 1 of 6

ACCOUNT NUMBER: 221993010
CAPITAL TRUST AGENCY SENIOR HOUSING
REVENUEBONDS (BEACH HOUSE AT
WIREGRASS RANCH PROJECT) SERIES
2016A AND TAXABLE 2016B
B CAPITALIZED INTEREST ACCOUNT

This statement is for the period from August 1, 2017 to August 31, 2017

QUESTIONS?

If you have any questions regarding your account or this statement, please contact your Account Manager or Analyst.

Account Manager:
SHERYL LEAR
EX-FL-WWSJ
225 E. ROBINSON ST., SUITE 250
ORLANDO, FL 32801
Phone 904-358-5363
E-mail SHERYL.LEAR@USBANK.COM

Analyst: KEVIN FOX Phone 704-335-4588



00- -M -N -PC -244-01 00376601 3766 0183434-00-03300-01 Page 2 of 6

ACCOUNT NUMBER: 221993010
CAPITAL TRUST AGENCY SENIOR HOUSING
REVENUEBONDS (BEACH HOUSE AT
WIREGRASS RANCH PROJECT) SERIES
2016A AND TAXABLE 2016B
B CAPITALIZED INTEREST ACCOUNT

This statement is for the period from August 1, 2017 to August 31, 2017

SPECIAL MESSAGES

Faster trade settlement begins September 5

To better meet the needs of all investors, the financial services industry is shortening the settlement cycle for stocks, corporate bonds, municipal bonds, unit investment trusts and financial products comprised of these security types (such as exchange-traded funds). The standard settlement cycle of three business days after the trade date will be changed to two business days on September 5, 2017.

This should result in reduced credit risk, cash deployment efficiencies, increased market liquidity and lower collateral requirements. It also will align the U.S. market with other major international markets. For example, 23 European Union members moved to a two-day settlement cycle in October 2014. U.S. Bank has been participating in industry-wide testing to ensure readiness for the shortened settlement cycle.





00- -M -N -PC -244-01 00376601 3766 0183434-00-03300-01 Page 3 of 6

ACCOUNT NUMBER: 221993010
CAPITAL TRUST AGENCY SENIOR HOUSING
REVENUEBONDS (BEACH HOUSE AT
WIREGRASS RANCH PROJECT) SERIES
2016A AND TAXABLE 2016B
B CAPITALIZED INTEREST ACCOUNT

This statement is for the period from August 1, 2017 to August 31, 2017

MARKET VALUE SUMMARY					
	Current Period 08/01/17 to 08/31/17				
Beginning Market Value	\$37,902.22				
Distributions	- 6.67				
Adjusted Market Value	\$37,895.55				
Investment Results					
Interest, Dividends and Other Income	6.67				
Total Investment Results	\$6.67				
Ending Market Value	\$37,902.22				



00- -M -N -PC -244-01 00376601 3766 0183434-00-03300-01 Page 4 of 6

ACCOUNT NUMBER: 221993010
CAPITAL TRUST AGENCY SENIOR HOUSING
REVENUEBONDS (BEACH HOUSE AT
WIREGRASS RANCH PROJECT) SERIES
2016A AND TAXABLE 2016B
B CAPITALIZED INTEREST ACCOUNT

This statement is for the period from August 1, 2017 to August 31, 2017

ASSET DETAIL AS OF 08/31/17					
Shares or Face Amount	Security Description	Market Value/ Price	Tax Cost/ Unit Cost	% of Total Yield at Market	Est Ann Inc
Cash Equ	ivalents				
37,902.220	US Bank Mmkt 5 - Ct 9AMMF05B2	37,902.22 1.0000	37,902.22 1.00	100.0 .20 *	75.80
Total Casl	h Equivalents	\$37,902.22	\$37,902.22	100.0	\$75.80
Total Ass	sets	\$37,902.22	\$37,902.22	100.0	\$75.80

ASSET DETAIL MESSAGES

Time of trade execution and trading party (if not disclosed) will be provided upon request.

Publicly traded assets are valued in accordance with market quotations or valuation methodologies from financial industry services believed by us to be reliable. Assets that are not publicly traded may be reflected at values from other external sources. Assets for which a current value is not available may be reflected at a previous value or as not valued, at par value, or at a nominal value. Values shown do not necessarily reflect prices at which assets could be bought or sold. Values are updated based on internal policy and may be updated less frequently than statement generation.

For further information, please contact your Analyst.

** The Yield at Market set forth in this statement for any money market fund is based on the interest rate applicable to that money market fund as of the last business day of the statement period (or most recent daily rate available) and may not be relied upon as (i) a yield estimate for the statement period as a whole, or (ii) a guarantee of future performance.





00- -M -N -PC -244-01 00376601 3766 0183434-00-03300-01 Page 5 of 6

ACCOUNT NUMBER: 221993010
CAPITAL TRUST AGENCY SENIOR HOUSING
REVENUEBONDS (BEACH HOUSE AT
WIREGRASS RANCH PROJECT) SERIES
2016A AND TAXABLE 2016B
B CAPITALIZED INTEREST ACCOUNT

This statement is for the period from August 1, 2017 to August 31, 2017

CASH SUMMARY

	Income Cash	Principal Cash	Total Cash
Beginning Cash Balance as of 08/01/2017	\$.00	\$.00	\$.00
Taxable Interest	6.67		6.67
Cash Disbursements	- 6.67		- 6.67
Ending Cash Balance as of 08/31/2017	\$0.00	\$0.00	\$0.00



00- -M -N -PC -244-01 00376601 3766 0183434-00-03300-01 Page 6 of 6

ACCOUNT NUMBER: 221993010
CAPITAL TRUST AGENCY SENIOR HOUSING
REVENUEBONDS (BEACH HOUSE AT
WIREGRASS RANCH PROJECT) SERIES
2016A AND TAXABLE 2016B
B CAPITALIZED INTEREST ACCOUNT

This statement is for the period from August 1, 2017 to August 31, 2017

TRANSACTION DETAIL				
Date Posted	Description	Income Cash	Principal Cash	Tax Cost
	Beginning Balance 08/01/2017	\$.00	\$.00	\$37,902.22
08/01/17	Interest Earned On US Bank Mmkt 5 - Ct Interest From 7/1/17 To 7/31/17 9AMMF05B2	6.67		
08/02/17	Cash Disbursement Paid To Account # 221993002 Transfer To Another Trust Income Earnings	- 6.67		
	Ending Balance 08/31/2017	\$0.00	\$0.00	\$37,902.22





PSL WIREGRASS LP ATTN DODD CRUTCHER 8214 WESTCHESTERDR SUITE 600 DALLAS TX 75225-6112 00- -M -N -PC -244-01 0183436-00-03300-01 3766 Page 1 of 6

ACCOUNT NUMBER: 221993011 CAPITAL TRUST AGENCY SENIOR HOUSING REVENUEBONDS (BEACH HOUSE AT WIREGRASS RANCH PROJECT) SERIES 2016A AND TAXABLE 2016B CAPITALIZED ISSUER'S FEE ACCOUNT

This statement is for the period from August 1, 2017 to August 31, 2017

QUESTIONS?

If you have any questions regarding your account or this statement, please contact your Account Manager or Analyst.

Account Manager:
SHERYL LEAR
EX-FL-WWSJ
225 E. ROBINSON ST., SUITE 250
ORLANDO, FL 32801
Phone 904-358-5363
E-mail SHERYL.LEAR@USBANK.COM

Analyst: KEVIN FOX Phone 704-335-4588



00- -M -N -PC -244-01 00376601 3766 0183436-00-03300-01 Page 2 of 6

ACCOUNT NUMBER: 221993011 CAPITAL TRUST AGENCY SENIOR HOUSING REVENUEBONDS (BEACH HOUSE AT WIREGRASS RANCH PROJECT) SERIES 2016A AND TAXABLE 2016B CAPITALIZED ISSUER'S FEE ACCOUNT

This statement is for the period from August 1, 2017 to August 31, 2017

SPECIAL MESSAGES

Faster trade settlement begins September 5

To better meet the needs of all investors, the financial services industry is shortening the settlement cycle for stocks, corporate bonds, municipal bonds, unit investment trusts and financial products comprised of these security types (such as exchange-traded funds). The standard settlement cycle of three business days after the trade date will be changed to two business days on September 5, 2017.

This should result in reduced credit risk, cash deployment efficiencies, increased market liquidity and lower collateral requirements. It also will align the U.S. market with other major international markets. For example, 23 European Union members moved to a two-day settlement cycle in October 2014. U.S. Bank has been participating in industry-wide testing to ensure readiness for the shortened settlement cycle.





00- -M -N -PC -244-01 00376601 3766 0183436-00-03300-01 Page 3 of 6

ACCOUNT NUMBER: 221993011
CAPITAL TRUST AGENCY SENIOR HOUSING
REVENUEBONDS (BEACH HOUSE AT
WIREGRASS RANCH PROJECT) SERIES
2016A AND TAXABLE 2016B
CAPITALIZED ISSUER'S FEE ACCOUNT

This statement is for the period from August 1, 2017 to August 31, 2017

MARKET V	ALUE SUMMARY	
	Current Period 08/01/17 to 08/31/17	
Beginning Market Value	\$64,837.53	
Distributions	- 11.39	
Adjusted Market Value	\$64,826.14	
Investment Results		
Interest, Dividends and Other Income	11.39	
Total Investment Results	\$11.39	
Ending Market Value	\$64,837.53	



00- -M -N -PC -244-01 00376601 3766 0183436-00-03300-01 Page 4 of 6

ACCOUNT NUMBER: 221993011 CAPITAL TRUST AGENCY SENIOR HOUSING REVENUEBONDS (BEACH HOUSE AT WIREGRASS RANCH PROJECT) SERIES 2016A AND TAXABLE 2016B CAPITALIZED ISSUER'S FEE ACCOUNT

This statement is for the period from August 1, 2017 to August 31, 2017

	ASSE	T DETAIL AS OF 08	3/31/17		
Shares or Face Amount	Security Description	Market Value/ Price	Tax Cost/ Unit Cost	% of Total Yield at Market	Est Ann Inc
Cash Equ	ivalents				
64,837.530	US Bank Mmkt 5 - Ct 9AMMF05B2	64,837.53 1.0000	64,837.53 1.00	100.0 .20 *	129.68
Total Casl	h Equivalents	\$64,837.53	\$64,837.53	100.0	\$129.68
Total Ass	sets	\$64,837.53	\$64,837.53	100.0	\$129.68

ASSET DETAIL MESSAGES

Time of trade execution and trading party (if not disclosed) will be provided upon request.

Publicly traded assets are valued in accordance with market quotations or valuation methodologies from financial industry services believed by us to be reliable. Assets that are not publicly traded may be reflected at values from other external sources. Assets for which a current value is not available may be reflected at a previous value or as not valued, at par value, or at a nominal value. Values shown do not necessarily reflect prices at which assets could be bought or sold. Values are updated based on internal policy and may be updated less frequently than statement generation.

For further information, please contact your Analyst.

** The Yield at Market set forth in this statement for any money market fund is based on the interest rate applicable to that money market fund as of the last business day of the statement period (or most recent daily rate available) and may not be relied upon as (i) a yield estimate for the statement period as a whole, or (ii) a guarantee of future performance.





00- -M -N -PC -244-01 00376601 3766 0183436-00-03300-01 Page 5 of 6

ACCOUNT NUMBER: 221993011
CAPITAL TRUST AGENCY SENIOR HOUSING
REVENUEBONDS (BEACH HOUSE AT
WIREGRASS RANCH PROJECT) SERIES
2016A AND TAXABLE 2016B
CAPITALIZED ISSUER'S FEE ACCOUNT

This statement is for the period from August 1, 2017 to August 31, 2017

CASH SUMMARY

	Income Cash	Principal Cash	Total Cash
Beginning Cash Balance as of 08/01/2017	\$.00	\$.00	\$.00
Taxable Interest	11.39		11.39
Cash Disbursements	- 11.39		- 11.39
Ending Cash Balance as of 08/31/2017	\$0.00	\$0.00	\$0.00



00- -M -N -PC -244-01 00376601 3766 0183436-00-03300-01 Page 6 of 6

ACCOUNT NUMBER: 221993011
CAPITAL TRUST AGENCY SENIOR HOUSING
REVENUEBONDS (BEACH HOUSE AT
WIREGRASS RANCH PROJECT) SERIES
2016A AND TAXABLE 2016B
CAPITALIZED ISSUER'S FEE ACCOUNT

This statement is for the period from August 1, 2017 to August 31, 2017

	TRANS	ACTION DETAIL		
Date Posted	Description	Income Cash	Principal Cash	Tax Cost
	Beginning Balance 08/01/2017	\$.00	\$.00	\$64,837.53
08/01/17	Interest Earned On US Bank Mmkt 5 - Ct Interest From 7/1/17 To 7/31/17 9AMMF05B2	11.39		
08/02/17	Cash Disbursement Paid To Account # 221993000 Transfer To Another Trust Income Earnings	- 11.39		
	Ending Balance 08/31/2017	\$0.00	\$0.00	\$64,837.53





PSL WIREGRASS LP ATTN DODD CRUTCHER 8214 WESTCHESTERDR SUITE 600 DALLAS TX 75225-6112 00- -M -N -PC -244-01 0183438-00-03300-01 3766 Page 1 of 4

ACCOUNT NUMBER: 221993012 CAPITAL TRUST AGENCY SENIOR HOUSING REVENUEBONDS (BEACH HOUSE AT WIREGRASS RANCH PROJECT) SERIES 2016A AND TAXABLE 2016B SURPLUS FUND

This statement is for the period from August 1, 2017 to August 31, 2017

QUESTIONS?

If you have any questions regarding your account or this statement, please contact your Account Manager or Analyst.

Account Manager:
SHERYL LEAR
EX-FL-WWSJ
225 E. ROBINSON ST., SUITE 250
ORLANDO, FL 32801
Phone 904-358-5363
E-mail SHERYL.LEAR@USBANK.COM

Analyst: KEVIN FOX Phone 704-335-4588



00- -M -N -PC -244-01 00376601 3766 0183438-00-03300-01 Page 2 of 4

ACCOUNT NUMBER: 221993012 CAPITAL TRUST AGENCY SENIOR HOUSING REVENUEBONDS (BEACH HOUSE AT WIREGRASS RANCH PROJECT) SERIES 2016A AND TAXABLE 2016B SURPLUS FUND

This statement is for the period from August 1, 2017 to August 31, 2017

SPECIAL MESSAGES

Faster trade settlement begins September 5

To better meet the needs of all investors, the financial services industry is shortening the settlement cycle for stocks, corporate bonds, municipal bonds, unit investment trusts and financial products comprised of these security types (such as exchange-traded funds). The standard settlement cycle of three business days after the trade date will be changed to two business days on September 5, 2017.

This should result in reduced credit risk, cash deployment efficiencies, increased market liquidity and lower collateral requirements. It also will align the U.S. market with other major international markets. For example, 23 European Union members moved to a two-day settlement cycle in October 2014. U.S. Bank has been participating in industry-wide testing to ensure readiness for the shortened settlement cycle.





00- -M -N -PC -244-01 00376601 3766 0183438-00-03300-01 Page 3 of 4

ACCOUNT NUMBER: 221993012
CAPITAL TRUST AGENCY SENIOR HOUSING
REVENUEBONDS (BEACH HOUSE AT
WIREGRASS RANCH PROJECT) SERIES
2016A AND TAXABLE 2016B
SURPLUS FUND

This statement is for the period from August 1, 2017 to August 31, 2017

	MARKET VALUE SUMMARY	
	Current Period 08/01/17 to 08/31/17	
Beginning Market Value	\$0.00	
Ending Market Value	\$0.00	
MARK	KET VALUE SUMMARY MESSAGES	

No activity qualifies for this statement period.



00- -M -N -PC -244-01 00376601 3766 0183438-00-03300-01 Page 4 of 4

ACCOUNT NUMBER: 221993012 CAPITAL TRUST AGENCY SENIOR HOUSING REVENUEBONDS (BEACH HOUSE AT WIREGRASS RANCH PROJECT) SERIES 2016A AND TAXABLE 2016B SURPLUS FUND

This statement is for the period from August 1, 2017 to August 31, 2017

ASSET DETAIL MESSAGES

No reportable securities for this statement period





PSL WIREGRASS LP ATTN DODD CRUTCHER 8214 WESTCHESTERDR SUITE 600 DALLAS TX 75225-6112 00- -M -N -PC -244-01 0183440-00-03300-01 3766 Page 1 of 4

ACCOUNT NUMBER: 221993013 CAPITAL TRUST AGENCY SENIOR HOUSING REVENUEBONDS (BEACH HOUSE AT WIREGRASS RANCH PROJECT) SERIES 2016A AND TAXABLE 2016B A COST OF ISSUANCE ACCOUNT

This statement is for the period from August 1, 2017 to August 31, 2017

QUESTIONS?

If you have any questions regarding your account or this statement, please contact your Account Manager or Analyst.

Account Manager:
SHERYL LEAR
EX-FL-WWSJ
225 E. ROBINSON ST., SUITE 250
ORLANDO, FL 32801
Phone 904-358-5363
E-mail SHERYL.LEAR@USBANK.COM

Analyst: KEVIN FOX Phone 704-335-4588



00- -M -N -PC -244-01 00376601 3766 0183440-00-03300-01 Page 2 of 4

ACCOUNT NUMBER: 221993013 CAPITAL TRUST AGENCY SENIOR HOUSING REVENUEBONDS (BEACH HOUSE AT WIREGRASS RANCH PROJECT) SERIES 2016A AND TAXABLE 2016B A COST OF ISSUANCE ACCOUNT

This statement is for the period from August 1, 2017 to August 31, 2017

SPECIAL MESSAGES

Faster trade settlement begins September 5

To better meet the needs of all investors, the financial services industry is shortening the settlement cycle for stocks, corporate bonds, municipal bonds, unit investment trusts and financial products comprised of these security types (such as exchange-traded funds). The standard settlement cycle of three business days after the trade date will be changed to two business days on September 5, 2017.

This should result in reduced credit risk, cash deployment efficiencies, increased market liquidity and lower collateral requirements. It also will align the U.S. market with other major international markets. For example, 23 European Union members moved to a two-day settlement cycle in October 2014. U.S. Bank has been participating in industry-wide testing to ensure readiness for the shortened settlement cycle.





00- -M -N -PC -244-01 00376601 3766 0183440-00-03300-01 Page 3 of 4

ACCOUNT NUMBER: 221993013
CAPITAL TRUST AGENCY SENIOR HOUSING
REVENUEBONDS (BEACH HOUSE AT
WIREGRASS RANCH PROJECT) SERIES
2016A AND TAXABLE 2016B
A COST OF ISSUANCE ACCOUNT

This statement is for the period from August 1, 2017 to August 31, 2017

rent Period to 08/31/17
10 00/31/17
\$0.00
\$0.00
N

No activity qualifies for this statement period.



00- -M -N -PC -244-01 00376601 3766 0183440-00-03300-01 Page 4 of 4

ACCOUNT NUMBER: 221993013 CAPITAL TRUST AGENCY SENIOR HOUSING REVENUEBONDS (BEACH HOUSE AT WIREGRASS RANCH PROJECT) SERIES 2016A AND TAXABLE 2016B A COST OF ISSUANCE ACCOUNT

This statement is for the period from August 1, 2017 to August 31, 2017

ASSET DETAIL MESSAGES

No reportable securities for this statement period





PSL WIREGRASS LP ATTN DODD CRUTCHER 8214 WESTCHESTERDR SUITE 600 DALLAS TX 75225-6112 00- -M -N -PC -244-01 0183442-00-03300-01 3766 Page 1 of 6

ACCOUNT NUMBER: 221993014
CAPITAL TRUST AGENCY SENIOR HOUSING
REVENUEBONDS (BEACH HOUSE AT
WIREGRASS RANCH PROJECT) SERIES
2016A AND TAXABLE 2016B
B COST OF ISSUANCE ACCOUNT

This statement is for the period from August 1, 2017 to August 31, 2017

QUESTIONS?

If you have any questions regarding your account or this statement, please contact your Account Manager or Analyst.

Account Manager:
SHERYL LEAR
EX-FL-WWSJ
225 E. ROBINSON ST., SUITE 250
ORLANDO, FL 32801
Phone 904-358-5363
E-mail SHERYL.LEAR@USBANK.COM

Analyst: KEVIN FOX Phone 704-335-4588



00- -M -N -PC -244-01 00376601 3766 0183442-00-03300-01 Page 2 of 6

ACCOUNT NUMBER: 221993014
CAPITAL TRUST AGENCY SENIOR HOUSING
REVENUEBONDS (BEACH HOUSE AT
WIREGRASS RANCH PROJECT) SERIES
2016A AND TAXABLE 2016B
B COST OF ISSUANCE ACCOUNT

This statement is for the period from August 1, 2017 to August 31, 2017

SPECIAL MESSAGES

Faster trade settlement begins September 5

To better meet the needs of all investors, the financial services industry is shortening the settlement cycle for stocks, corporate bonds, municipal bonds, unit investment trusts and financial products comprised of these security types (such as exchange-traded funds). The standard settlement cycle of three business days after the trade date will be changed to two business days on September 5, 2017.

This should result in reduced credit risk, cash deployment efficiencies, increased market liquidity and lower collateral requirements. It also will align the U.S. market with other major international markets. For example, 23 European Union members moved to a two-day settlement cycle in October 2014. U.S. Bank has been participating in industry-wide testing to ensure readiness for the shortened settlement cycle.





00- -M -N -PC -244-01 00376601 3766 0183442-00-03300-01 Page 3 of 6

ACCOUNT NUMBER: 221993014
CAPITAL TRUST AGENCY SENIOR HOUSING
REVENUEBONDS (BEACH HOUSE AT
WIREGRASS RANCH PROJECT) SERIES
2016A AND TAXABLE 2016B
B COST OF ISSUANCE ACCOUNT

MARKET VALUE SUMMARY				
	Current Period 08/01/17 to 08/31/17			
Beginning Market Value	\$4,046.74			
Distributions	- 0.69			
Adjusted Market Value	\$4,046.05			
Investment Results				
Interest, Dividends and Other Income	0.69			
Total Investment Results	\$0.69			
Ending Market Value	\$4.046.74			



00- -M -N -PC -244-01 00376601 3766 0183442-00-03300-01 Page 4 of 6

ACCOUNT NUMBER: 221993014
CAPITAL TRUST AGENCY SENIOR HOUSING
REVENUEBONDS (BEACH HOUSE AT
WIREGRASS RANCH PROJECT) SERIES
2016A AND TAXABLE 2016B
B COST OF ISSUANCE ACCOUNT

This statement is for the period from August 1, 2017 to August 31, 2017

ASSET DETAIL AS OF 08/31/17						
Shares or Face Amount	Security Description	Market Value/ Price	Tax Cost/ Unit Cost	% of Total Yield at Market	Est Ann Inc	
Cash Equ	ivalents					
4,046.740	US Bank Mmkt 5 - Ct 9AMMF05B2	4,046.74 1.0000	4,046.74 1.00	100.0 .20 *	* 8.09	
Total Casi	h Equivalents	\$4,046.74	\$4,046.74	100.0	\$8.09	
Total Ass	sets	\$4,046.74	\$4,046.74	100.0	\$8.09	

ASSET DETAIL MESSAGES

Time of trade execution and trading party (if not disclosed) will be provided upon request.

Publicly traded assets are valued in accordance with market quotations or valuation methodologies from financial industry services believed by us to be reliable. Assets that are not publicly traded may be reflected at values from other external sources. Assets for which a current value is not available may be reflected at a previous value or as not valued, at par value, or at a nominal value. Values shown do not necessarily reflect prices at which assets could be bought or sold. Values are updated based on internal policy and may be updated less frequently than statement generation.

For further information, please contact your Analyst.

** The Yield at Market set forth in this statement for any money market fund is based on the interest rate applicable to that money market fund as of the last business day of the statement period (or most recent daily rate available) and may not be relied upon as (i) a yield estimate for the statement period as a whole, or (ii) a guarantee of future performance.





00- -M -N -PC -244-01 00376601 3766 0183442-00-03300-01 Page 5 of 6

ACCOUNT NUMBER: 221993014
CAPITAL TRUST AGENCY SENIOR HOUSING
REVENUEBONDS (BEACH HOUSE AT
WIREGRASS RANCH PROJECT) SERIES
2016A AND TAXABLE 2016B
B COST OF ISSUANCE ACCOUNT

This statement is for the period from August 1, 2017 to August 31, 2017

CASH SUMMARY

	Income Cash	Principal Cash	Total Cash
Beginning Cash Balance as of 08/01/2017	\$.00	\$.00	\$.00
Taxable Interest	0.69		0.69
Cash Disbursements	- 0.69		- 0.69
Ending Cash Balance as of 08/31/2017	\$0.00	\$0.00	\$0.00



00- -M -N -PC -244-01 00376601 3766 0183442-00-03300-01 Page 6 of 6

ACCOUNT NUMBER: 221993014
CAPITAL TRUST AGENCY SENIOR HOUSING
REVENUEBONDS (BEACH HOUSE AT
WIREGRASS RANCH PROJECT) SERIES
2016A AND TAXABLE 2016B
B COST OF ISSUANCE ACCOUNT

	TRANSACTION DETAIL					
Date Posted	Description	Income Cash	Principal Cash	Tax Cost		
	Beginning Balance 08/01/2017	\$.00	\$.00	\$4,046.74		
08/01/17	Interest Earned On US Bank Mmkt 5 - Ct Interest From 7/1/17 To 7/31/17 9AMMF05B2	0.69				
08/02/17	Cash Disbursement Paid To Account # 221993002 Transfer To Another Trust Income Earnings	- 0.69				
	Ending Balance 08/31/2017	\$0.00	\$0.00	\$4,046.74		





PSL WIREGRASS LP ATTN DODD CRUTCHER 8214 WESTCHESTERDR SUITE 600 DALLAS TX 75225-6112 00- -M -N -PC -244-01 0183507-00-03300-01 3766 Page 1 of 6

ACCOUNT NUMBER: 221993015 CAPITAL TRUST AGENCY SENIOR HOUSING REVENUEBONDS (BEACH HOUSE AT WIREGRASS RANCH PROJECT) SERIES 2016A BORROWER EQUITY CAPITALIZED INTEREST ACCOUNT

This statement is for the period from August 1, 2017 to August 31, 2017

QUESTIONS?

If you have any questions regarding your account or this statement, please contact your Account Manager or Analyst.

Account Manager:
SHERYL LEAR
EX-FL-WWSJ
225 E. ROBINSON ST., SUITE 250
ORLANDO, FL 32801
Phone 904-358-5363
E-mail SHERYL.LEAR@USBANK.COM

Analyst: KEVIN FOX Phone 704-335-4588



00- -M -N -PC -244-01 00376601 3766 0183507-00-03300-01 Page 2 of 6

ACCOUNT NUMBER: 221993015 CAPITAL TRUST AGENCY SENIOR HOUSING REVENUEBONDS (BEACH HOUSE AT WIREGRASS RANCH PROJECT) SERIES 2016A BORROWER EQUITY CAPITALIZED INTEREST ACCOUNT

This statement is for the period from August 1, 2017 to August 31, 2017

SPECIAL MESSAGES

Faster trade settlement begins September 5

To better meet the needs of all investors, the financial services industry is shortening the settlement cycle for stocks, corporate bonds, municipal bonds, unit investment trusts and financial products comprised of these security types (such as exchange-traded funds). The standard settlement cycle of three business days after the trade date will be changed to two business days on September 5, 2017.

This should result in reduced credit risk, cash deployment efficiencies, increased market liquidity and lower collateral requirements. It also will align the U.S. market with other major international markets. For example, 23 European Union members moved to a two-day settlement cycle in October 2014. U.S. Bank has been participating in industry-wide testing to ensure readiness for the shortened settlement cycle.





00- -M -N -PC -244-01 00376601 3766 0183507-00-03300-01 Page 3 of 6

ACCOUNT NUMBER: 221993015
CAPITAL TRUST AGENCY SENIOR HOUSING
REVENUEBONDS (BEACH HOUSE AT
WIREGRASS RANCH PROJECT) SERIES
2016A BORROWER EQUITY CAPITALIZED
INTEREST ACCOUNT

MARKET VALUE SUMMARY				
	Current Period 08/01/17 to 08/31/17			
Beginning Market Value	\$1,267,811.29			
Investment Results				
Interest, Dividends and Other Income	215.35			
Total Investment Results	\$215.35			
Ending Market Value	\$1,268,026,64			



00- -M -N -PC -244-01 00376601 3766 0183507-00-03300-01 Page 4 of 6

ACCOUNT NUMBER: 221993015 CAPITAL TRUST AGENCY SENIOR HOUSING REVENUEBONDS (BEACH HOUSE AT WIREGRASS RANCH PROJECT) SERIES 2016A BORROWER EQUITY CAPITALIZED INTEREST ACCOUNT

This statement is for the period from August 1, 2017 to August 31, 2017

ASSET DETAIL AS OF 08/31/17					
Shares or Face Amount	Security Description	Market Value/ Price	Tax Cost/ Unit Cost	% of Total Yield at Market	Est Ann Inc
Cash Equi	valents				
1,268,026.640	US Bank Mmkt 5 - Ct 9AMMF05B2	1,268,026.64 1.0000	1,268,026.64 1.00	100.0 .20 *	2,536.05
Total Cash	n Equivalents	\$1,268,026.64	\$1,268,026.64	100.0	\$2,536.05
Total Ass	sets	\$1,268,026.64	\$1,268,026.64	100.0	\$2,536.05

ASSET DETAIL MESSAGES

Time of trade execution and trading party (if not disclosed) will be provided upon request.

Publicly traded assets are valued in accordance with market quotations or valuation methodologies from financial industry services believed by us to be reliable. Assets that are not publicly traded may be reflected at values from other external sources. Assets for which a current value is not available may be reflected at a previous value or as not valued, at par value, or at a nominal value. Values shown do not necessarily reflect prices at which assets could be bought or sold. Values are updated based on internal policy and may be updated less frequently than statement generation.

For further information, please contact your Analyst.

** The Yield at Market set forth in this statement for any money market fund is based on the interest rate applicable to that money market fund as of the last business day of the statement period (or most recent daily rate available) and may not be relied upon as (i) a yield estimate for the statement period as a whole, or (ii) a guarantee of future performance.





00- -M -N -PC -244-01 00376601 3766 0183507-00-03300-01 Page 5 of 6

ACCOUNT NUMBER: 221993015
CAPITAL TRUST AGENCY SENIOR HOUSING
REVENUEBONDS (BEACH HOUSE AT
WIREGRASS RANCH PROJECT) SERIES
2016A BORROWER EQUITY CAPITALIZED
INTEREST ACCOUNT

This statement is for the period from August 1, 2017 to August 31, 2017

CASH SUMMARY

	Income Cash	Principal Cash	Total Cash
Beginning Cash Balance as of 08/01/2017	\$.00	\$.00	\$.00
Taxable Interest	215.35		215.35
Transfers	- 215.35	215.35	
Net Money Market Activity		- 215.35	- 215.35
Ending Cash Balance as of 08/31/2017	\$0.00	\$0.00	\$0.00



00- -M -N -PC -244-01 00376601 3766 0183507-00-03300-01 Page 6 of 6

ACCOUNT NUMBER: 221993015
CAPITAL TRUST AGENCY SENIOR HOUSING
REVENUEBONDS (BEACH HOUSE AT
WIREGRASS RANCH PROJECT) SERIES
2016A BORROWER EQUITY CAPITALIZED
INTEREST ACCOUNT

	TRANSACTION DETAIL					
Date Posted	Description	Income Cash	Principal Cash	Tax Cost		
	Beginning Balance 08/01/2017	\$.00	\$.00	\$1,267,811.29		
08/01/17	Interest Earned On US Bank Mmkt 5 - Ct Interest From 7/1/17 To 7/31/17 9AMMF05B2	215.35				
08/02/17	Cash Disbursement Transfer To Principal Income Earnings	- 215.35				
08/02/17	Cash Receipt Transfer From Income Income Earnings		215.35			
08/02/17	Purchased 215.35 Units Of US Bank Mmkt 5 - Ct Trade Date 8/2/17 9AMMF05B2		- 215.35	215.35		
	Ending Balance 08/31/2017	\$0.00	\$0.00	\$1,268,026.64		





PSL WIREGRASS LP ATTN DODD CRUTCHER 8214 WESTCHESTERDR SUITE 600 DALLAS TX 75225-6112 00- -M -N -PC -244-01 0183518-00-03300-01 3766 Page 1 of 6

ACCOUNT NUMBER: 221993016
CAPITAL TRUST AGENCY SENIOR HOUSING
REVENUEBONDS (BEACH HOUSE AT
WIREGRASS RANCH PROJECT) SERIES
2016B BORROWER EQUITY CAPITALIZED
INTEREST ACCOUNT

This statement is for the period from August 1, 2017 to August 31, 2017

QUESTIONS?

If you have any questions regarding your account or this statement, please contact your Account Manager or Analyst.

Account Manager:
SHERYL LEAR
EX-FL-WWSJ
225 E. ROBINSON ST., SUITE 250
ORLANDO, FL 32801
Phone 904-358-5363
E-mail SHERYL.LEAR@USBANK.COM

Analyst: KEVIN FOX Phone 704-335-4588



00- -M -N -PC -244-01 00376601 3766 0183518-00-03300-01 Page 2 of 6

ACCOUNT NUMBER: 221993016
CAPITAL TRUST AGENCY SENIOR HOUSING
REVENUEBONDS (BEACH HOUSE AT
WIREGRASS RANCH PROJECT) SERIES
2016B BORROWER EQUITY CAPITALIZED
INTEREST ACCOUNT

This statement is for the period from August 1, 2017 to August 31, 2017

SPECIAL MESSAGES

Faster trade settlement begins September 5

To better meet the needs of all investors, the financial services industry is shortening the settlement cycle for stocks, corporate bonds, municipal bonds, unit investment trusts and financial products comprised of these security types (such as exchange-traded funds). The standard settlement cycle of three business days after the trade date will be changed to two business days on September 5, 2017.

This should result in reduced credit risk, cash deployment efficiencies, increased market liquidity and lower collateral requirements. It also will align the U.S. market with other major international markets. For example, 23 European Union members moved to a two-day settlement cycle in October 2014. U.S. Bank has been participating in industry-wide testing to ensure readiness for the shortened settlement cycle.





00- -M -N -PC -244-01 00376601 3766 0183518-00-03300-01 Page 3 of 6

ACCOUNT NUMBER: 221993016
CAPITAL TRUST AGENCY SENIOR HOUSING
REVENUEBONDS (BEACH HOUSE AT
WIREGRASS RANCH PROJECT) SERIES
2016B BORROWER EQUITY CAPITALIZED
INTEREST ACCOUNT

MARKET VALUE SUMMARY				
	Current Period 08/01/17 to 08/31/17			
Beginning Market Value	\$69,409.69			
Investment Results				
Interest, Dividends and Other Income	11.79			
Total Investment Results	\$11.79			
Ending Market Value	\$69,421.48			



00- -M -N -PC -244-01 00376601 3766 0183518-00-03300-01 Page 4 of 6

ACCOUNT NUMBER: 221993016
CAPITAL TRUST AGENCY SENIOR HOUSING
REVENUEBONDS (BEACH HOUSE AT
WIREGRASS RANCH PROJECT) SERIES
2016B BORROWER EQUITY CAPITALIZED
INTEREST ACCOUNT

This statement is for the period from August 1, 2017 to August 31, 2017

ASSET DETAIL AS OF 08/31/17					
Shares or Face Amount	Security Description	Market Value/ Price	Tax Cost/ Unit Cost	% of Total Yield at Market	Est Ann Inc
Cash Equ	ivalents				
69,421.480	US Bank Mmkt 5 - Ct 9AMMF05B2	69,421.48 1.0000	69,421.48 1.00	100.0 .20 *	138.84
Total Casi	h Equivalents	\$69,421.48	\$69,421.48	100.0	\$138.84
Total Ass	sets	\$69,421.48	\$69,421.48	100.0	\$138.84

ASSET DETAIL MESSAGES

Time of trade execution and trading party (if not disclosed) will be provided upon request.

Publicly traded assets are valued in accordance with market quotations or valuation methodologies from financial industry services believed by us to be reliable. Assets that are not publicly traded may be reflected at values from other external sources. Assets for which a current value is not available may be reflected at a previous value or as not valued, at par value, or at a nominal value. Values shown do not necessarily reflect prices at which assets could be bought or sold. Values are updated based on internal policy and may be updated less frequently than statement generation.

For further information, please contact your Analyst.

** The Yield at Market set forth in this statement for any money market fund is based on the interest rate applicable to that money market fund as of the last business day of the statement period (or most recent daily rate available) and may not be relied upon as (i) a yield estimate for the statement period as a whole, or (ii) a guarantee of future performance.





00- -M -N -PC -244-01 00376601 3766 0183518-00-03300-01 Page 5 of 6

ACCOUNT NUMBER: 221993016
CAPITAL TRUST AGENCY SENIOR HOUSING
REVENUEBONDS (BEACH HOUSE AT
WIREGRASS RANCH PROJECT) SERIES
2016B BORROWER EQUITY CAPITALIZED
INTEREST ACCOUNT

This statement is for the period from August 1, 2017 to August 31, 2017

CASH SUMMARY

	Income Cash	Principal Cash	Total Cash
Beginning Cash Balance as of 08/01/2017	\$.00	\$.00	\$.00
Taxable Interest	11.79		11.79
Transfers	- 11.79	11.79	
Net Money Market Activity		- 11.79	- 11.79
Ending Cash Balance as of 08/31/2017	\$0.00	\$0.00	\$0.00




00- -M -N -PC -244-01 00376601 3766 0183518-00-03300-01 Page 6 of 6

ACCOUNT NUMBER: 221993016
CAPITAL TRUST AGENCY SENIOR HOUSING
REVENUEBONDS (BEACH HOUSE AT
WIREGRASS RANCH PROJECT) SERIES
2016B BORROWER EQUITY CAPITALIZED
INTEREST ACCOUNT

	TRANSACTION DETAIL					
Date Posted	Description	Income Cash	Principal Cash	Tax Cost		
	Beginning Balance 08/01/2017	\$.00	\$.00	\$69,409.69		
08/01/17	Interest Earned On US Bank Mmkt 5 - Ct Interest From 7/1/17 To 7/31/17 9AMMF05B2	11.79				
08/02/17	Cash Disbursement Transfer To Principal Income Earnings	- 11.79				
08/02/17	Cash Receipt Transfer From Income Income Earnings		11.79			
08/02/17	Purchased 11.79 Units Of US Bank Mmkt 5 - Ct Trade Date 8/2/17 9AMMF05B2		- 11.79	11.79		
	Ending Balance 08/31/2017	\$0.00	\$0.00	\$69,421.48		





Glossarv

Accretion - The accumulation of the value of a discounted bond until maturity.

Adjusted Prior Market Realized Gain/Loss - The difference between the proceeds and the Prior Market Value of the transaction.

Adjusted Prior Market Unrealized Gain/Loss - The difference between the Market Value and the Adjusted Prior Market Value.

Adjusted Prior Market Value - A figure calculated using the beginning

Market Value for the fiscal year, adjusted for all asset related transactions during the period, employing an average cost methodology.

Amortization - The decrease in value of a premium bond until maturity.

Asset - Anything owned that has commercial exchange value. Assets may consist of specific property or of claims against others, in contrast to obligations due to others (liabilities).

Bond Rating - A measurement of a bond's quality based upon the issuer's financial condition. Ratings are assigned by independent rating services, such as Moody's, or S&P, and reflect their opinion of the issuer's ability to meet the scheduled interest and principal repayments for the bond.

Cash - Cash activity that includes both income and principal cash categories.

Change in Unrealized Gain/Loss - Also reported as Gain/Loss in Period in the Asset Detail section. This figure shows the market appreciation (depreciation) for the current period.

Cost Basis (Book Value) - The original price of an asset, normally the purchase price or appraised value at the time of acquisition. Book Value method maintains an average cost for each asset.

Cost Basis (Tax Basis) - The original price of an asset, normally the purchase price or appraised value at the time of acquisition. Tax Basis uses client determined methods such as Last-In-First-Out (LIFO), First-In-First-Out (FIFO), Average, Minimum Gain, and Maximum Gain. Ending Accrual - (Also reported as Accrued Income) Income earned but not yet received, or expenses incurred but not yet paid, as of the end of the reporting period.

Estimated Annual Income - The amount of income a particular asset is anticipated to earn over the next year. The shares multiplied by annual income rate.

Estimated Current Yield - The annual rate of return on an investment expressed as a percentage. For stocks, yield is calculated by taking the annual dividend payments divided by the stock's current share price. For bonds, yield is calculated by the coupon rate divided by the bond's market price.

Ex-Dividend Date - (Also reported as Ex-Date) For stock trades, the person who owns the security on the ex-dividend date will earn the dividend, regardless of who currently owns the stock.

Income Cash - A category of cash comprised of ordinary earnings derived from investments, usually dividends and interest.

Market Value - The price per unit multiplied by the number of units.

Maturity Date - The date on which an obligation or note matures.

Payable Date - The date on which a dividend, mutual fund distribution, or interest on a bond will be made.

Principal Cash - A category of cash comprised of cash, deposits, cash withdrawals and the cash flows generated from purchases or sales of investments.

 $\mbox{\bf Realized Gain/Loss Calculation}$ - The Proceeds less the Cost Basis of a transaction.

Settlement Date - The date on which a trade settles and cash or securities are credited or debited to the account.

Trade Date - The date a trade is legally entered into.

Unrealized Gain/Loss - The difference between the Market Value and Cost Basis at the end of the current period.

Yield on/at Market - The annual rate of return on an investment expressed as a percentage. For stocks, yield is calculated by the annual dividend payments divided by the stock's current share price. For bonds, yield is calculated by the coupon rate divided by the bond's market price.

The terms defined in this glossary are only for use when reviewing your account statement. Please contact your Relationship Manager with any questions.



003766 -N -244

U.S. Bank 1555 N. Rivercenter Dr. Suite 300 Milwaukee, WI 53212

թվարժերի վերովիուի Ուրի հանդեր հերկային հերկային

000001385 09 SP 000638704253332 P

PSL WIREGRASS LP ATTN DODD CRUTCHER 8214 WESTCHESTER DR SUITE 600 DALLAS TX 75225-6112

